Date Received 3-22-73

APT No 5806

T C No

Map Date

# MECKLENBURG COUNTY HEALTH DEPARTMENT

## ENVIRONMENTAL HEALTH DIVISION

### APPLICATION FOR PERCOLATION TEST

1) NAME OF OWNER Homecraft Builders, Inc. (LAST / FIRST / MIDDLE)

2) ADDRESS OF OWNER P. O. Box 12002 Charlotte, N. C. ZIP 28205

3) PHONE NO Home 537-5020 Office 333-0546


4) LOCATION OF PROPERTY 1621 CRANDEN DR. (STREET OR COUNTY ROAD)

5) SUBDIVISION CRANDON PARK LOT NO 57 BLOCK NO. B

MAP BOOK NO. 7 PAGE NO 709

6) DEED REFERENCE DEED BOOK 1848 PAGE NO 527

Application is hereby made to the Mecklenburg County Health Department for the conduct of a percolation test and an on site inspection of the lot hereinabove described for the purpose of determining if the lot is suitable for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge

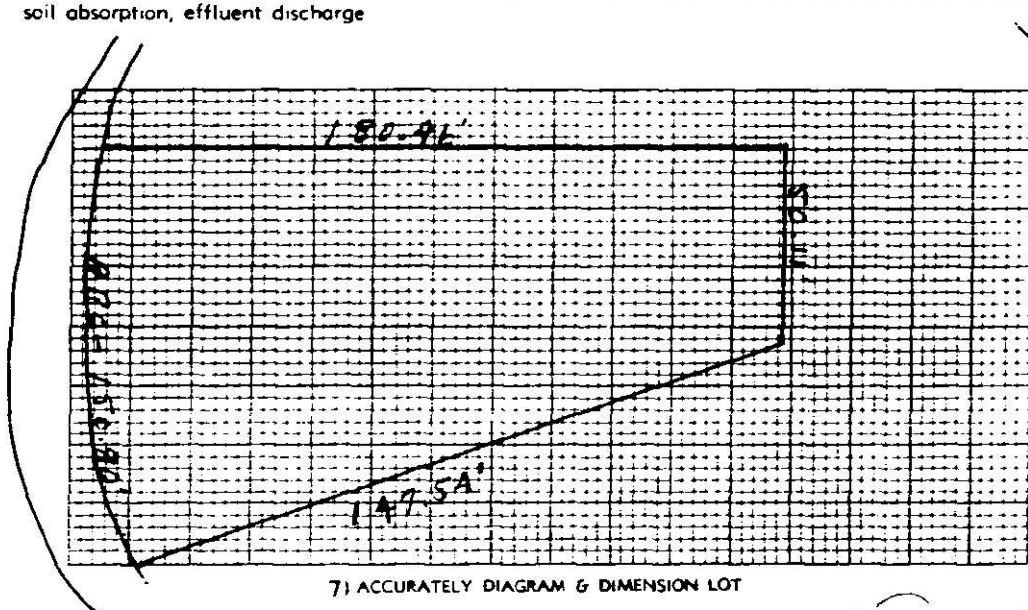


7) ACCURATELY DIAGRAM & DIMENSION LOT

Fred H Jr

OWNER

FORM NO. E-1-8-1-72

HEALTH DEPARTMENT'S COPY

Serial No. [illegible]3

PTR No. 5806

T C No. 039-254-01

Date Issued April 17, 1973

Map Date 9-1-70

**Do Not Issue A Building Permit Based On This Form**

# MECKLENBURG COUNTY HEALTH DEPARTMENT

## ENVIRONMENTAL HEALTH DIVISION


## PERCOLATION TEST REPORT

NAME OF OWNER Homecraft Builders, Inc. (LAST / FIRST / MIDDLE)

ADDRESS OF OWNER P. O. Box 12002 ZIP 28205

LOCATION OF PROPERTY 1621 Crandon Drive (STREET OR COUNTY ROAD)

SUBDIVISION Crandon Park LOT NO 57 BLOCK NO. B

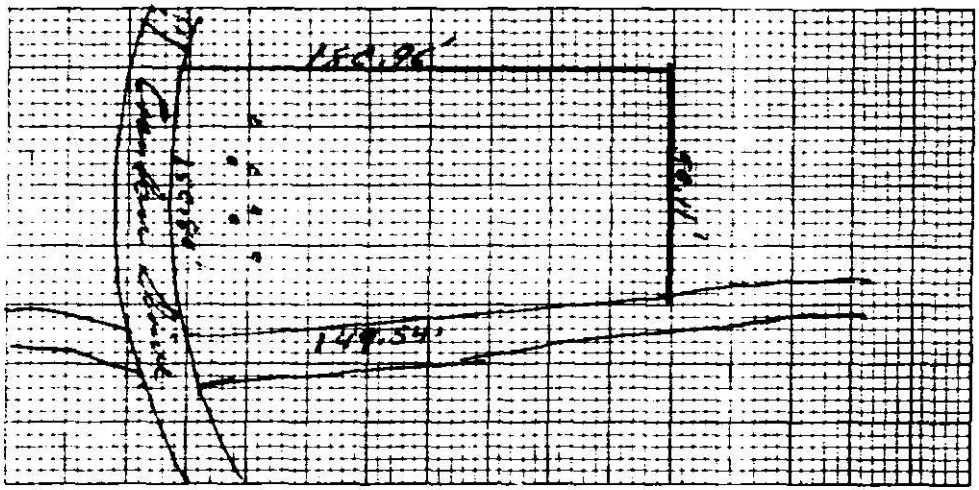


PLOT PLAN

This is to certify that a percolation test has been run and an on-site inspection made by the Mecklenburg County Health Department on the lot described above. The said test was conducted on that portion of the lot as indicated on above plot.

The percolation rate determined by the test was 60 min/in The said lot is approved for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption effluent discharge subject to the following terms and conditions:

1. A permit to install, construct, alter, or repair the specific system shall be obtained from the Mecklenburg County Health Department prior to the beginning of any construction of buildings, or of the wastewater treatment system on the said lot.
2. The size of the septic tank wastewater treatment system which must be installed will be determined by the Health Department prior to installation based on the percolation rate obtained above, and on the size and type of building constructed thereon.
3. This approval is valid only if the system is installed in the immediate area where the percolation test was run.
4. This approval is void if any grading, filling, or construction (including the drilling of a well) is performed on the lot which, in the opinion of the Health Department, renders the area where the percolation test was run unsuitable for the installation construction, alteration, and/or repair of such a system.

This approval is granted based on the laws of the State of North Carolina and the rules and regulations of the North Carolina State Board of Health and the Mecklenburg County Board of Health which were in effect on the date of issuance and is void if at any time in the future, prior to the completion of the system, these laws, rules, and regulations are changed such that this approval would not have been granted had the new or revised laws, rules, and regulations been in effect on the issue date.

John R. Adkisson

Director, Environmental Health Division or Authorized Section Head

FORM NO. E-2-4-1-71

HEALTH DEPARTMENT'S COPY
