Date Received 3/7/79

Please mail copy to:
Christine L. McCarter
3634 Chandworth Road
Charlotte, N. C. 28210

APT No. 15190
P.O.
T. C. No. 231-034-03

Map Date 3/9/76

MECKLENBURG COUNTY
DEPARTMENT OF ENVIRONMENTAL HEALTH

APPLICATION FOR SOIL INVESTIGATION

1) NAME OF OWNER Fisher (LAST) June (FIRST) Virgle (MIDDLE)

2) ADDRESS OF OWNER 3601 Matthews-Pineville Rd ZIP 28105
Matthews, N.C.

3) PHONE NO. Home 542-0363 Office 542-0363

4) LOCATION OF PROPERTY Kuykendall Road (STREET OR COUNTY ROAD)


5) SUBDIVISION _____ LOT NO. #1 BLOCK NO. 34

MAP BOOK NO 231 PAGE NO. 3

6) DEED REFERENCE DEED BOOK 4154 PAGE NO. 0063

Application is hereby made to the Mecklenburg County Department of Environmental Health for the conduct of a soil investigation and an on site inspection of the lot hereinabove described for the purpose of determining if the lot is suitable for the installation of an individual septic tank wastewater treatment system with subsurface soil absorption effluent discharge

KUYKENDALL

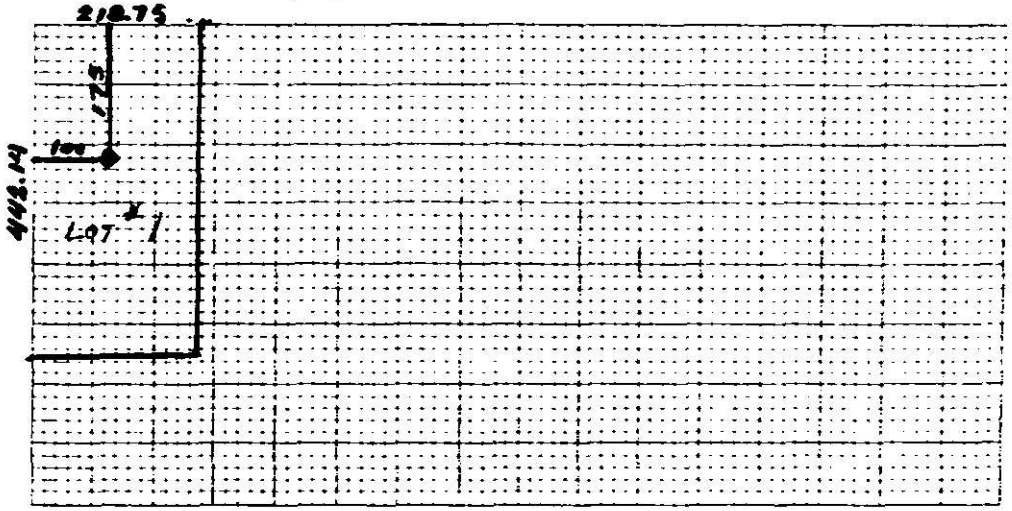

7) ACCURATELY DIAGRAM & DIMENSION LOT

Owner in Fee 3-5-79

OWNER

June Virgle Fisher

EHD-5-76

Environmental Health Department's Copy

NORTH CAROLINA
DEPARTMENT OF HUMAN RESOURCES
DIVISION OF HEALTH SERVICES
RALEIGH, NORTH CAROLINA

APPENDIX H
SITE EVALUATION

S.I.R. No. 15140

(Ground Absorption Sewage Disposal)

OWNER: James W. Fuqua
ADDRESS: 3601 Pineville-Matthews Rd.
COUNTY: Mecklenburg, N.C. 28105
LOCATION OF SITE: Fuqua Rendall Rd

DATE REQUESTED:
PLAT NO.: PC 231-034-03, Lot #1
LOT SIZE: 46,356

FACTORS	AREA 1	AREA 2	AREA 3	AREA 4
1. SLOPE (%)	(S) PS 2-10% U	(S) PS 2-10% U	S PS U	S PS U
2. SOIL TEXTURE (12-36 in.) (Sandy, loamy, clayey, Note 2:1, Clay)	S (PS) Clay U	S PS 2:1 Clay (U)	S PS U	S PS U
3. SOIL STRUCTURE (12-36 in.) (Clayey Soils)	S (PS) Blocky U	S PS Massive U	S PS U	S PS U
4. SOIL DEPTH (In.)	(S) 48" PS U	(S) 48" PS U	S PS U	S PS U
5. RESTRICTIVE HORIZONS (In.) (Impervious Strata, Rock)	(S) None PS U	(S) Rock PS U	S PS U	S PS U
6. SOIL DRAINAGE/GROUNDWATER (External & Internal)	(S) 7 to 15 PS ground water U	S Seasonal PS perched water table U	S PS U	S PS U
7. SOIL PERMEABILITY (Percolation Rate)	S (PS) moderate U	S PS Slow → U Slow	S PS U	S PS U
8. OTHER (Specify)	S PS U	S PS U	S PS U	S PS U
9. SITE CLASSIFICATION	~~Provisionally~~ Suitable	Unsuitable		
SOIL SERIES	Local	Helena		

S - Suitable PS - Provisionally Suitable U - Unsuitable


* See Diagram on Back (Include: Soil areas, property lines, roads, streams, gullies, wet areas, fill areas, wells, water bodies, slope patterns)

Recommendations/Comments: Note- Lot has an existing well and septic tank system (size & exact location not determined)

Described By: William B. Moelling

Title: Soil Scientist Date: 3-21-79

dhs form 2601 (1/79)
Sanitation

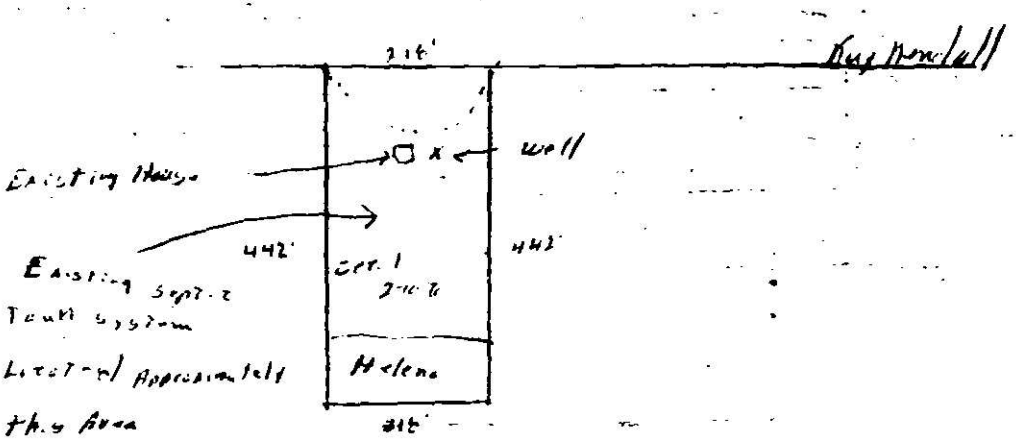
216'
Bus Randall
Existing House
well
442'
Cert. 1
442'
Existing Septic
Tank System
Lateral Approximately
this Area
Helena
216'

Serial No. 2604

PTR No. 15190

Date Issued March 22, 1979

T. C. No. po 231-034-03

Map Date 3/9/76


MECKLENBURG COUNTY
DEPARTMENT OF ENVIRONMENTAL HEALTH
SOIL INVESTIGATION REPORT

NAME OF OWNER Fisher, June
(LAST, FIRST, MIDDLE)

ADDRESS OF OWNER 3601 Matthews-Pineville Road ZIP 28105

LOCATION OF PROPERTY Kuykendall Road
(STREET OR COUNTY ROAD)

SUBDIVISION LOT NO #1 BLOCK NO.

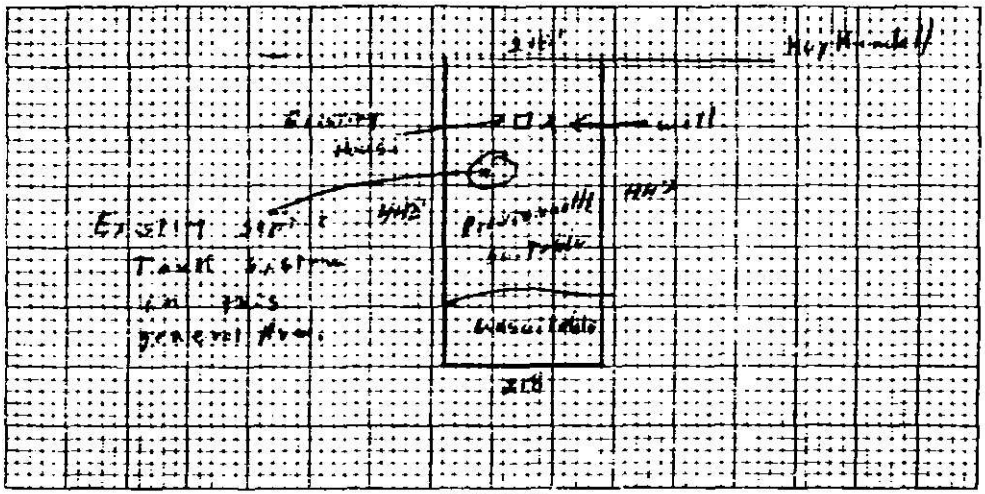

PLOT PLAN

This is to certify that a soil investigation and on-site investigation was made by the Mecklenburg County Department of Environmental Health on the lot described above. The said investigation was conducted on that portion of the lot as indicated on the above plot.

The permeability rate determined by the investigation was **Provisionally Suitable**. The said lot is approved for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption effluent discharge subject to the following terms and conditions:

1. A permit to install, construct, alter, or repair the specific system shall be obtained from the Mecklenburg County Department of Environmental Health prior to the beginning of any construction of buildings, or of the wastewater treatment system on the said lot.
2. The size of the septic tank wastewater treatment system which must be installed will be determined by the Mecklenburg County Department of Environmental Health prior to installation based on the permeability rate obtained above, and on the size and type of building constructed thereon.
3. This approval is valid only if the system is installed in the immediate area indicated as acceptable for system installation on the above plot.
4. This approval is void if any grading, filling, or construction, including the drilling of a well, is performed on the lot which, in the opinion of the Mecklenburg County Department of Environmental Health, renders the area indicated as acceptable for system installation unsuitable for installation, construction, alteration, and/or repair of such a system.

This approval is granted based on the laws of the State of North Carolina and the rules and regulations of the North Carolina Department of Human Resources, Division of Health Services and the Mecklenburg County Health Commission which were in effect on the date of issuance and is void if at any time in the future, prior to completion of the system, these laws, rules and regulations are changed such that this approval would not have been granted had the new or revised laws, rules, and regulations been in effect on the issue date.

William H. Wilcox
Soil Scientist

John R. Adkisson
Environmental Health Director or Authorized Section Head

EHD-S-76

Environmental Health Department's Copy

R
