Date Received 8 Apr 77

APT No. 1284
P.O. 227-094-02
T. C. No. 227-094-03

Map Date _____

MECKLENBURG COUNTY
DEPARTMENT OF ENVIRONMENTAL HEALTH

APPLICATION FOR SOIL INVESTIGATION

1) NAME OF OWNER Miss Mildred Reid RCD-1 Matthews N.C. Mrs Zeb Greene Rt 3 Box 208 Charlotte 28210
LAST FIRST MIDDLE

2) ADDRESS OF OWNER J. R. Gregory Parsons 4022-D Providence Rd Charlotte NC ZIP 28211

3) PHONE NO. Home 366-8084 Office 373-2274


4) LOCATION OF PROPERTY Kuykendall Rd.
STREET OR COUNTY ROAD

5) SUBDIVISION _____ LOT NO. _____ BLOCK NO. _____

MAP BOOK NO. _____ PAGE NO. _____

6) DEED REFERENCE: DEED BOOK _____ PAGE NO. _____

Application is hereby made to the Mecklenburg County Department of Environmental Health for the conduct of a soil investigation and an on site inspection of the lot hereinabove described for the purpose of determining if the lot is suitable for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge.

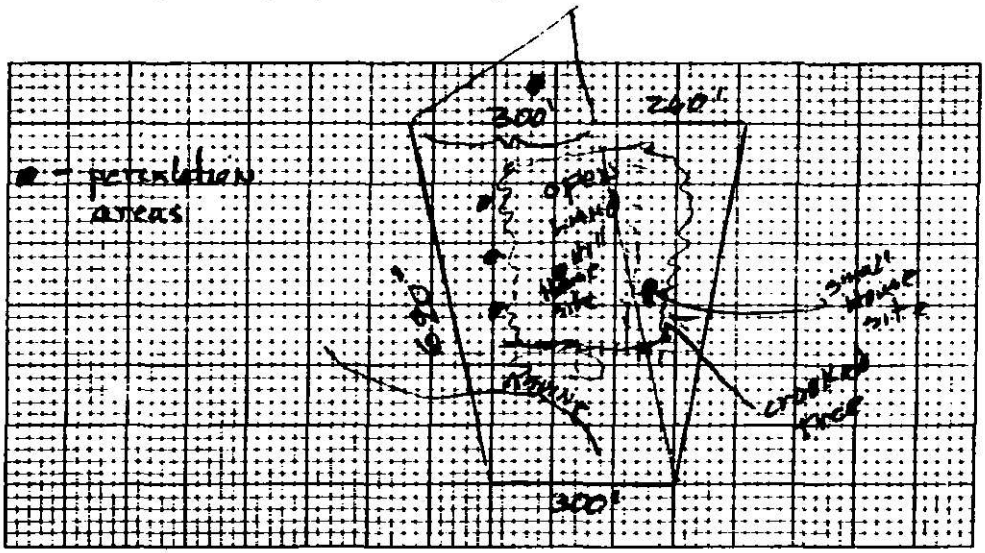

● - percolation areas

7) ACCURATELY DIAGRAM & DIMENSION LOT

J. Gregory Parsons
OWNER

EHD-5-76

Environmental Health Department's Copy

SOIL INVESTIGATION REPORT

Date of Investigation May 1 & 2, 1979 (Mrs. Mildred Peil) APT NO. 12164

Owner Mr. Felix Stueve P.O. 227-014-02 227-014-03

Location of Property Hwy Kendall Rd

Soil Suitability Ratings

Soil Properties	Soil 1	Soil 2	Soil 3	Soil 4
1. Soil Series	Parolat	Parolat Depressed Area	Willis (Rocks)	
2. Soil Slope	suitable 1-10% 10-25%	suitable 2-6%	unsuitable >30%	
3. Soil Depth	suitable 40"	suitable 40"	unsuitable <20"	
4. Soil Texture	Provisionally suitable Cl-l	Provisionally suitable Cl-l	unsuitable 2-1 Expanding Cl-l	
5. Soil Structure	Provisionally suitable Block-l	Provisionally suitable Block-l	unsuitable Massive	
6. Restrictive Horizons	-	-		
7. Soil Drainage	suitable water Table 70'	unsuitable Area collects surface water	— higher elevations during rains from com	
8. Soil Permeability (Percolation Rate)	Provisionally suitable Moderate 60 min/in.	unsuitable slow >120 min/in	unsuitable >130 min/in	
9. Other				
10. Overall Rating	Provisionally suitable	unsuitable	unsuitable	


Remarks/Recommendations Based on the investigation, adequate area of previously suitable soils for the installation of septic tank system. System design should be based on percolation rate of 60 min/in and the system located in the area of Parolat soils

See diagram on back

William R. Weeks
Soil Scientist

3/10/75
EHD 539

DIAGRAM OF PROPERTY

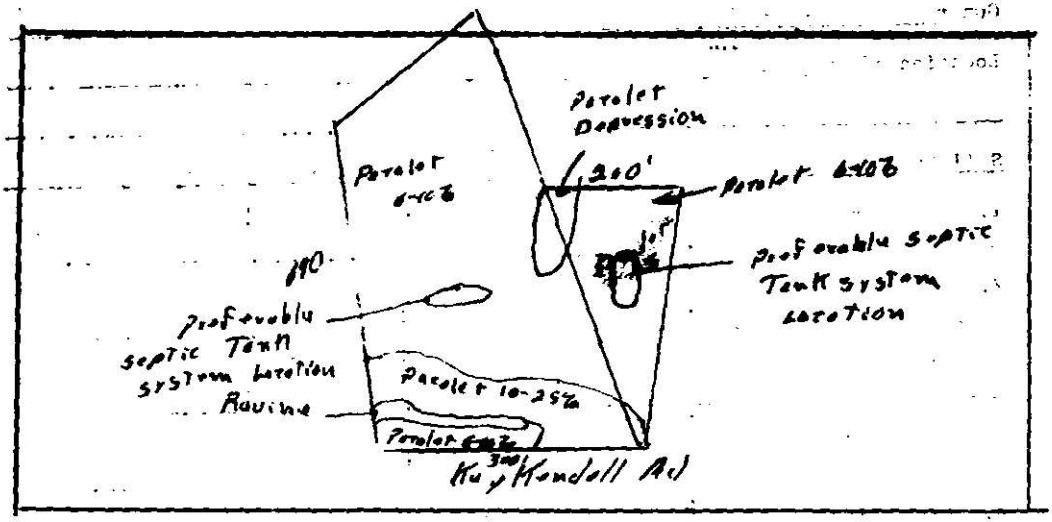

3/18/75

539

Serial No. 0681

PTR No. 12184
P.O.227-094-02
T. C. No. P.O.227-094-03

Date Issued April 26, 1977

Map Date


MECKLENBURG COUNTY
DEPARTMENT OF ENVIRONMENTAL HEALTH
SOIL INVESTIGATION REPORT

NAME OF OWNER Reid, Mildred & Feb. Greene
LAST FIRST MIDDLE

ADDRESS OF OWNER c/o R. Gregory Parsons, 4022-11 Providence ZIP 28211
Charlotte, NC

LOCATION OF PROPERTY Kuykendall Rd.
STREET OR COUNTY ROAD

SUBDIVISION LOT NO. BLOCK NO.

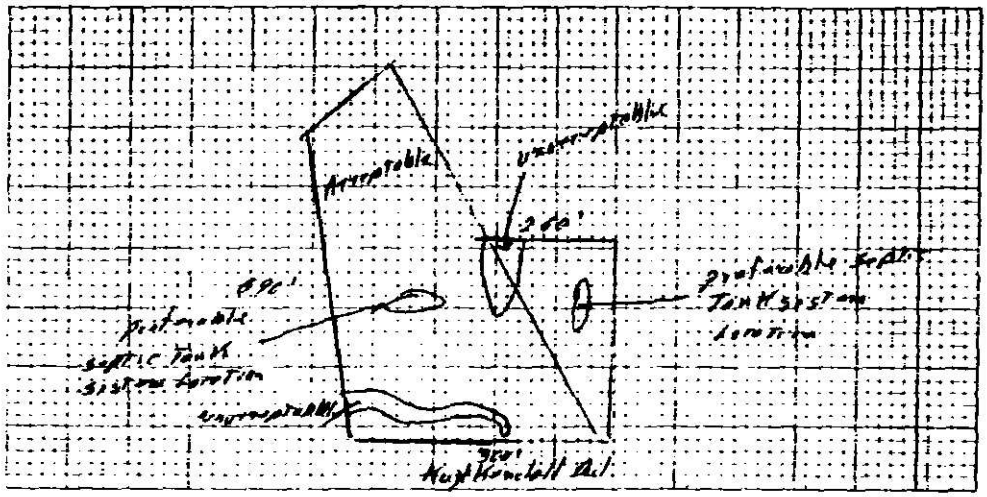

PLOT PLAN

This is to certify that a soil investigation study to investigate sewage disposal, the Mecklenburg County Department of Environmental Health has made for described above. The soil investigation was conducted on that portion of the lot as indicated on the above plot. Provisionally Suitable

The percolation rate determined by the investigation was 60 min/in. The said lot is approved for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption effluent discharge subject to the following terms and conditions:

1. A permit must be obtained from the Mecklenburg County Department of Environmental Health prior to the beginning of construction of the wastewater treatment system on the said lot.
2. The size of the septic tank wastewater treatment system shall be determined by the Mecklenburg County Department of Environmental Health at the time of application for the permit at the rate obtained above, and on the size and type of building to be constructed thereon.
3. This approval is valid only for the location indicated on the above plot as acceptable for system installation on the above plot.
4. This approval is void after one year from the date of issuance unless the testing of the soil is performed on the lot which, in the opinion of the Mecklenburg County Department of Environmental Health, for such the area indicated as acceptable for system installation unsuitable for installation construction material or any improper use of such a system.

This approval is granted based on the laws of the State of North Carolina and the rules and regulations of the North Carolina Department of Human Resources, Division of Health Services and the Mecklenburg County Health Commission which were in effect on the date of issuance and is void if at any time in the future, prior to completion of the system, these laws, rules and regulations are changed such that this approval would not have been granted had the new or revised laws, rules, and regulations been in effect on the issue date.

William A. Baglin
Soil Scientist

John A. Akerson
Environmental Health Director or
Authorized Section Head

EHD-5-76

Environmental Health Department's Copy
