Groundwater & Wastewater Services
Septic Project File & Data Review Worksheet

GWS File #: 7835B WASPS App #: _____

Primary ES assigned to project: JEREMY MICHAEL

Secondary ES assigned to project: CS

Project Type: New System ☐ Alteration ☐ Repair ☑ Modified Plot Plan ☐

I. File Review:

Rule or Law	Permit Application			
.1937(d)	Is the Application complete	Yes ☑	No ☐	N/A ☐
.1937(d)	Is there a Site plan/Plat with application	Yes ☑	No ☐	N/A ☐
.1937(d)	Is the Facility shown?	Yes ☑	No ☐	N/A ☐
.1937(d)	Are appurtenances shown	Yes ☑	No ☐	N/A ☐
	Site Evaluation Information			
.1939 (a)(1)	Topography and Landscape Position Recorded?	Yes ☐	No ☐	N/A ☑
.1940 (a-g)	Slope % Recorded?	Yes ☐	No ☐	N/A ☐
.1939 (a)(2)	Texture Class Recorded?	Yes ☐	No ☐	N/A ☐
.1939 (a)(2)	Structure type Recorded?	Yes ☐	No ☐	N/A ☐
.1939 (a)(2)	Consistence Recorded?	Yes ☐	No ☐	N/A ☐
.1939 (a)(2)	Mineralogy Recorded?	Yes ☐	No ☐	N/A ☐
.1939 (a)(3)	Soil Wetness Condition Recorded?	Yes ☐	No ☐	N/A ☐
.1939 (a)(4)	Soil Depth to Rock or Parent Material Recorded When Encountered	Yes ☐	No ☐	N/A ☐
.1939 (a)(5)	Depth to Restrictive Horizons Recorded When Encountered?	Yes ☐	No ☐	N/A ☐
.1939 (a)(6)	Sufficient Available Space Recorded?	Yes ☐	No ☐	N/A ☐
.1937(m)	Are the Profile Locations Shown?			
.1939(a)	Are the S/PS Profiles in system & in repair area?	Yes ☐	No ☐	N/A ☐
& .1945(b)	Number of auger borings made: _____ Were sufficient auger borings made?	Yes ☐	No ☐	N/A ☐
.1939(d), .1955, .1956, .1957	LTAR	Yes ☐	No ☐	N/A ☑
	Improvement Permit/Construction Authorization			
.1937(g) 130A-336(a)	Proposed System Type stated-Initial	Yes ☐	No ☐	N/A ☑
.1945(b)	Proposed System Type stated-Repair	Yes ☐	No ☐	N/A ☐
130A-336 (a)(3)	System location identifiable by setbacks - Initial	Yes ☐	No ☐	N/A ☐
.1937(g) .1945(b)	System components shown – Initial	Yes ☐	No ☐	N/A ☐
.1945(b)	Repair area shown	Yes ☐	No ☐	N/A ☐
.1937 (f)(g)	Does System design match facility, flow & WWcharacteristics?	Yes ☐	No ☐	N/A ☐
.1937 (f)(g)	Is System design consistent with soil/site conditions?	Yes ☐	No ☐	N/A ☐
.1937 (f)(g)	Is the System located in the approved area?	Yes ☐	No ☐	N/A ☐
130A-336(a)	Is the Design flow (gpd) indicated?	Yes ☐	No ☐	N/A ☑

130A-336(a)	Number of Bedrooms, employees, seats, etc. indicated?	Yes ☐	No ☐	N/A ☐
.1937(g)	Trench depth indicated?	Yes ☐	No ☐	N/A ☐
.1937(g)	Trench width indicated?	Yes ☐	No ☐	N/A ☐
.1937(g)	Trench length indicated?	Yes ☐	No ☐	N/A ☐
130A-336(a)(1)	Proposed/existing well shown?	Yes ☐	No ☐	N/A ☐
130A-336(a)(1)	Property line lengths shown?	Yes ☐	No ☐	N/A ☐
130A-336(a)	Facility/appurtenance setbacks shown from fixed points?	Yes ☐	No ☐	N/A ☑
	Operation Permit			
.1937(i)	System type as described in table V(a) of rule .1961	Yes ☑	No ☐	N/A ☐
.1937(i)	Conditions for system performance, operation, maintenance, monitoring and reporting.	Yes ☑	No ☐	N/A ☐

II. WASPS Review:

Construction authorization issued	Yes ☐	No ☐	N/A ☐
Installation approval issued	Yes ☑	No ☐	N/A ☐
Operation permit issued	Yes ☑	No ☐	N/A ☐
Other related documentation	Yes ☐	No ☐	N/A ☐

Items requiring correction/modification: _____

Comments: REPAIR - 7835B

IA issued date: 7/2/08

OP issued date: 7/9/08

Review performed by: IR Date performed: 7/1/08

C Sherrill

MECKLENBURG COUNTY
GROUNDWATER & WASTEWATER SERVICES

APPLICATION FOR A RESIDENTIAL SITE IMPROVEMENT PERMIT/ CONSTRUCTION AUTHORIZATION FOR AN ON-SITE WASTEWATER SYSTEM, NEW WELL INSTALLATION, OR REPAIR OF EXISTING WELL

1. SEPTIC / TYPE APPLICATION: ☐ N/A ☐ NEW SYSTEM ☐ ALTERATION ☑ REPAIR ☐ MODIFIED PLOT PLAN

2. WELL / TYPE APPLICATION: ☑ N/A ☐ NEW WELL ☐ MAJOR REPAIR ☐ ABANDONMENT

3. JOB LOCATION INFORMATION:
TAX PARCEL NUMBER: 031-182-51
STREET ADDRESS: 2321 Mt. Holly Huntersville Rd.
CITY: Charlotte,
STATE: NC ZIP: 28214
SUBDIVISION NAME:
LOT #: LOT SIZE (acres):
TOWNSHIP:
☐ 0-MECKLENBURG ☐ 3-CORNELIUS ☐ 6-HUNTERSVILLE
☑ 1-CHARLOTTE ☐ 4-PINEVILLE ☐ 7-MINT HILL
☐ 2-DAVIDSON ☐ 5-MATTHEWS

4. BUILDING INFORMATION:
BUILDING TYPE:
☐ SINGLE MOBILE HOME ☐ MODULAR HOME
☐ DOUBLE WIDE ☐ MULTIPLE FAMILY
☑ HOUSE ☐ OTHER _____
HEATED SQUARE FOOTAGE: 900
NUMBER OF BEDROOMS: 2
NUMBER OF OCCUPANTS: 2
FOUNDATION TYPE:
☐ CONCRETE SLAB ☐ BASEMENT WITH PLUMBING
☑ CRAWL SPACE ☐ BASMENT WITH NO PLUMBING

5. IF PLANNING TO EXPAND OR ALTER THE EXISTING SEPTIC SYSTEM PLEASE COMPLETE THE FOLLOWING SECTION: ☑ N/A

NUMBER OF BEDROOMS TO BE ADDED: _____ NUMBER OF ADDITIONAL OCCUPANTS IN THE RESIDENCE: _____

6. WATER SUPPLY: ☑ MUNICIPAL ☐ PRIVATE WELL ☐ PUBLIC WELL ☐ SHARED WELL ☐ OTHER _____

7. PROPOSED USE OF WELL: ☑ N/A ☐ IRRIGATION ☐ POTABLE (DRINKING WATER) ☐ OTHER _____

8. PLEASE INDICATE AND RANK DESIRED SEPTIC SYSTEM TYPE(S) IN ORDER OF PREFERENCE *(1-MOST DESIRED 5-LEAST DESIRED)*:

☐ N/A ☐ ANY TYPE ☑ CONVENTIONAL ☑ ACCEPTED ☑ INNOVATIVE ☐ ALTERNATIVE ☐ OTHER _____

8A. RANK: 1 3 2 4 5

9. DO ANY OF THE FOLLOWING APPLY TO THE PROPERTY IN QUESTION? IF "YES" PLEASE ATTACH SUPPORTING DOCUMENTATION.

BURIED CABLES, LANDFILLS, STUMPHOLES	☐ YES	☑ NO	GRADING/SOIL REMOVAL PERFORMED	☐ YES	☑ NO
EXISTING WASTEWATER (SEPTIC) SYSTEMS	☑ YES	☐ NO	JURISDICTIONAL WETLANDS	☐ YES	☑ NO
WELLS, SPRINGS, OR WATER LINES	☐ YES	☑ NO	APPROVAL REQUIRED BY ANY OTHER PUBLIC AGENCY	☐ YES	☑ NO
EASEMENTS OR RIGHT-OF-WAYS	☐ YES	☑ NO	WASTEWATER OTHER THAN DOMESTIC SEWAGE	☐ YES	☑ NO
CHEMICAL/PETROLEUM STORAGE TANKS	☐ YES	☑ NO	KNOWN UNDERGROUND CONTAMINATION	☐ YES	☑ NO
WASTE STORAGE	☐ YES	☑ NO	GROUNDWATER USE RESTRICTIONS/VARIANCES	☐ YES	☑ NO

10. WHAT DATE WAS THE PROPERTY ORIGINALLY DEEDED AND RECORDED? _____ ☑ UNKNOWN

11. WHAT IS THE ANTICIPATED CLOSING DATE FOR THIS PROPERTY? _____ ☑ N/A

12. PROPERTY OWNER:
NAME: Joshua E. Stover
ADDRESS: 2321 Mt. Holly Huntersville Rd.
CITY: Charlotte
STATE: NC ZIP: 28214
HOME PHONE: 704-907-2850
WORK PHONE:
MOBILE PHONE: S/A
FAX: 704-392-9122

13. OWNER'S LEGAL REPRESENTATIVE, IF APPLICABLE:
NAME:
ADDRESS: S/A
CITY:
STATE: ZIP:
HOME PHONE:
WORK PHONE:
MOBILE PHONE:
FAX:

MECKLENBURG COUNTY – GROUNDWATER & WASTEWATER SERVICES
700 N. TRYON ST. SUITE 211 CHARLOTTE, NC 28202, OFFICE: 704-336-5103, FAX: 704-336-6984

Revised on: 7/1/08

14. SEPTIC SYSTEM PERMIT APPLICATION:

If the information in this application is falsified, changed, or the site is altered, then the Improvement Permit and Authorization to Construct shall become invalid. I have read this application and certify that the information provided herein is true, complete and correct. Authorized county and state officials are granted right of entry to conduct necessary inspections to determine compliance with applicable laws and rules. I understand that I am solely responsible for the proper identification and labeling of all property lines and corners and making the site accessible so that a complete site evaluation can be performed. The permit is valid for either sixty (60) months or is non-expiring depending upon the documentation submitted: complete site plan = 60 months, complete plat = non-expiring.

_____ (Initial here for septic system applications)

15. WELL PERMIT APPLICATION:

If the information in this application is falsified, changed, or the site is altered, then the Well Permit shall become invalid. I have read this application and certify that the information provided herein is true, complete and correct. Authorized county and state officials are granted right of entry to conduct necessary inspections to determine compliance with applicable laws and rules. I understand that I am solely responsible for the proper identification and labeling of all property lines and corners and making the site accessible so that a complete site evaluation can be performed. The permit is valid for a period of twelve (12) months from the date of issuance.

_____ (Initial here for well applications)

16. APPLICATION SIGNATURE SECTION:

ONLY COMPLETE APPLICATIONS WILL BE PROCESSED. A proper signature is required in order to process your application. Please review the application carefully and sign in the space provided below.

_____ 7/1/08

Property Owner's or Owner's Legal Representative Signature — Date

---

OFFICE USE ONLY

☐ SURVEY PLAT TO SCALE SUBMITTED ☐ SCALED SITE PLAN SUBMITTED ☐ UN-SCALED SITE PLAN SUBMITTED

SEPTIC APPLICATION FEES RECEIVED: $ N/A DATE FEE RECEIVED: 7/1/08

WELL APPLICATION FEES RECEIVED: $ _____ DATE FEE RECEIVED: _____

APPLICATION PROCESSED BY: Annette Gladney

GWS FILE NUMBER ASSIGNED: 7835B

APPLICATION ID NUMBER ASSIGNED: 3666

COMMENTS:

MECKLENBURG COUNTY – GROUNDWATER & WASTEWATER SERVICES
700 N. TRYON ST. SUITE 211 CHARLOTTE, NC 28202, OFFICE: 704-336-5103, FAX: 704-336-6984


Revised on: 7/1/08

Mecklenburg County
Land Use & Environmental Service Agency
Groundwater & Wastewater Services
700 N. Tryon St., Suite 211
Charlotte, NC 28202
Phone: (704) 336-5103
Fax: (704) 336-6894

File #_____
Date_____

PROPOSED PLOT PLAN

A map showing existing and proposed property lines and easements with dimensions, the location of the single family residence, non-single family residence, or other facility, and appurtenances, the site for the proposed well, and the location of existing or proposed sewer lines and/or sewage disposal systems, surface water bodies, aboveground or underground storage tanks. Name all roads adjoining the property. If this a repair indicate the type of repair.

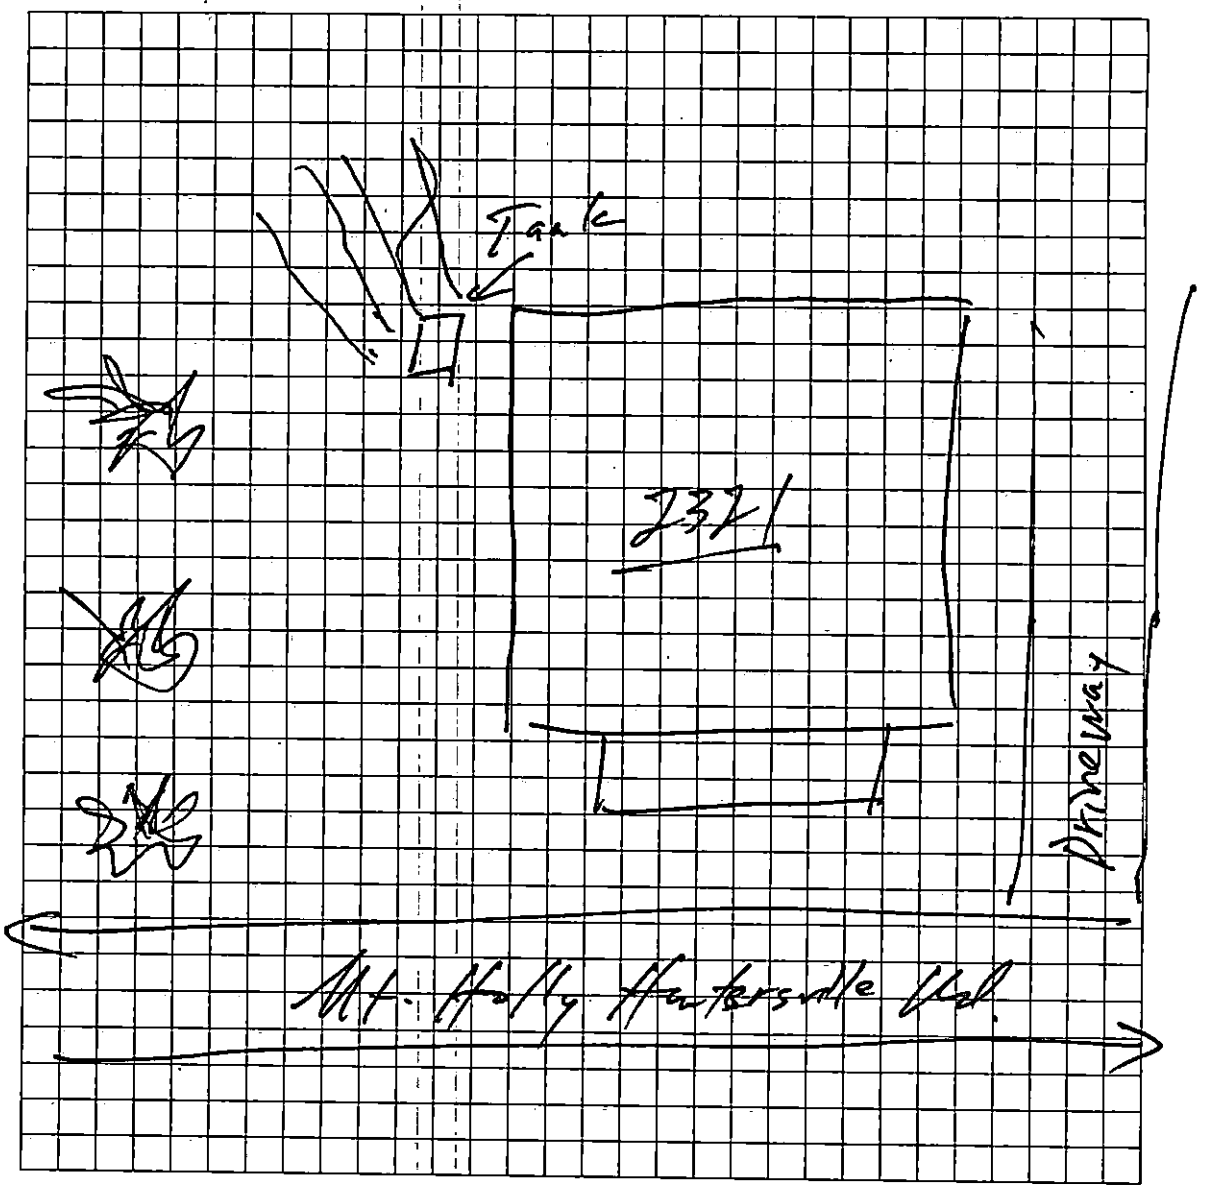

Owner/Agent Signature	
Date 7/1/08	

LBC 12/15/04

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St., Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

INSTALLATION APPROVAL for an ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

File #: 7835B Permit #: _____ Tax Parcel #: 031-182-51

Property Owner: Joshua Stoner

Job Location Address: 2321 Mt. Holly Huntersville Rd.

City: Charlotte State: NC Zip Code: 28214

Installation Approval Issuance Date: 7-2-08

Permission is hereby given to ☐ install ☐ alter ☒ repair an on-site wastewater treatment & and disposal system, with subsurface soil absorption and effluent discharge, as specified herein at the described location. This approval is granted based upon the application information submitted to our office. All work shall be completed on or before 8-2-08, after which date this approval shall be null and void. The system shall meet all of the construction requirements of 15A NCAC 18A. 1900 which are in effect on the date of granting this approval. An **Operation Permit** must be obtained from the Mecklenburg County Health Department before any system can be covered up or placed into service. The issuance of this permit does not in any way guarantee that the system anticipated to be constructed will operate properly, or relieve any person now of hereafter owning, controlling or using such system from any liability resulting from the failure of the system to operate properly.

***NOTICE: This system shall not be installed while soils are in a wet condition.**

Permitted Design Flow: 240 GPD

Site LTAR: 0.3 GPD/ft² (For new installations only.)

Liquid Capacity of Septic Tank: Existing gallons

Liquid Capacity of Dosing Tank: N/A gallons

Drainfield Design ☐ N/A

Trench Depth: 36 inches

Trench Width: 3 feet

Line Spacing: 9 feet (O.C.)

Total line length: 210 feet

# of Lines: 3 @ 70 feet

Depth of Media: 12 inches (Type) 25% Reduction

Distribution Device: ~~0-Box~~ Chamber end cap

Bed Design *(For Repair Installations ONLY.)* ☒ N/A

Bed Depth: _____ inches

Bed Width: _____ feet

Total line length: _____ feet

# of Lines: _____ @ _____ feet

Depth of Media: _____ inches (Type) _____

Distribution Device: _____

Water Supply Source

☒ Municipal ☐ Private Well ☐ Community Well

☐ Other _____


Minimum System Setbacks

Distance from Building Foundation: 5 feet

Distance from Property Line: 10 feet

Distance from Water Supply Source: 50 feet

SKETCH OF SYSTEM LAYOUT
(Proposed Layout)

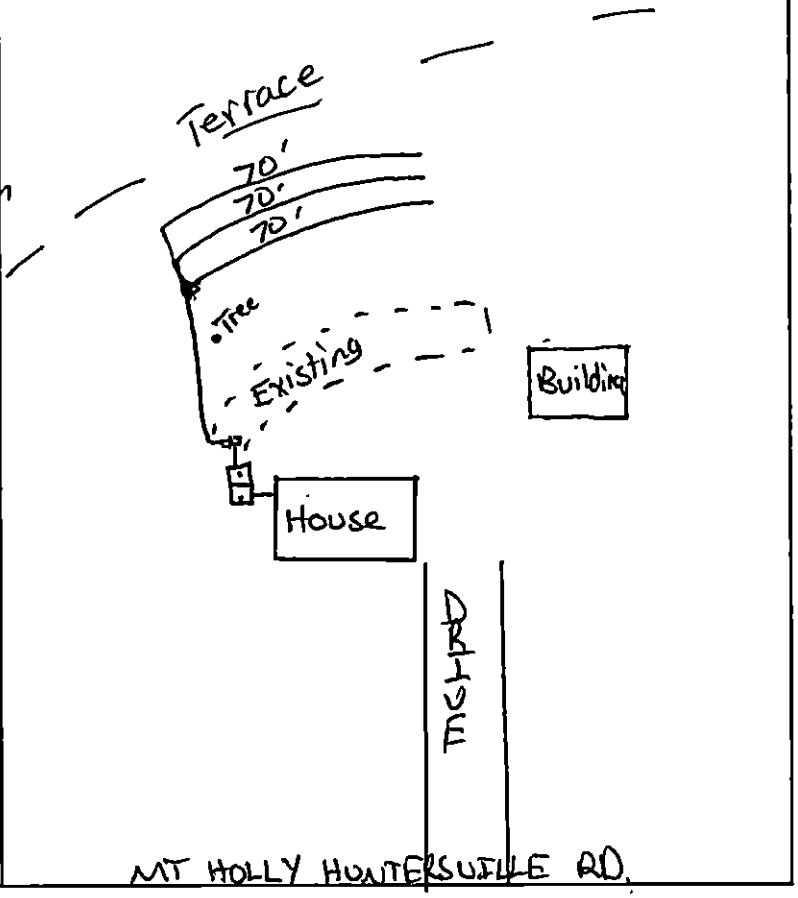

Comments: System Classification & Type: III g System

DENR Authorized Agent: Jeremy Michael Signature: Jeremy Michael

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St., Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

OPERATION PERMIT for an ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

File #: 7835B Permit #: _____ Tax Parcel #: 031-182-5

Property Owner: Joshua Stoner

Job Location Address: 7321 Mt. Holly Huntersville Rd

City: Charlotte State: NC Zip Code: 28214

Operation Permit Issuance Date: 7/9/08 Contractor Name: Dellinger

Permitted Design Flow: 240 GPD

Liquid Capacity of Septic Tank: existing gallons

Liquid Capacity of Dosing Tank: N/A gallons

Effluent Pump Model: N/A

Drainfield Installation ☐ N/A

Trench Depth: 36 inches

Trench Width: 3 feet

Line Spacing: 9 feet (O.C.)

Total line length: 210 feet

# of Lines: 3 @ 70 feet

Depth of Media: 12 inches (Type) Infiltrator

Depth of Cover: 24 inches

Distribution Device: Chamber endcap

Inspection Dates

Tank(s) Inspected: 7/9/08

Excavation Inspected: 7/9/08

Pump & Controls Inspected: N/A

Bed Installation *(For Repair Installations ONLY.)* ☑ N/A

Bed Depth: _____ inches

Bed Width: _____ feet

Total line length: _____ feet


# of Lines: _____ @ _____ feet

Depth of Media: _____ inches (Type) _____

Depth of Cover: _____ inches

Distribution Device: _____

SKETCH OF SYSTEM INSTALLATION
(As-Built Drawing)

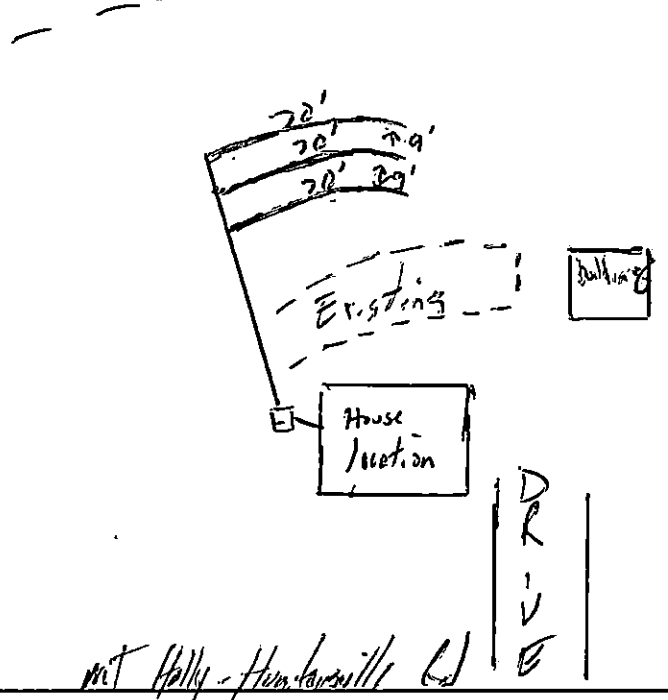

Water Supply Source

☒ Municipal ☐ Private Well ☐ Community Well

☐ Other _____

System Installation Setbacks

Distance from Building Foundation: >5 feet

Distance from Property Line: 10 feet

Distance from Water Supply Source: 50 feet

The undersigned has inspected the Septic Tank System described above, and certifies it has been ☐ installed ☐ altered ☒ repaired ☒ as detailed in the plot above ☐ in accordance with the permit issued and meets the provisions of 15A NCAC 18A. 1900, "Laws and Rules for Sewage Treatment and Disposal Systems" in effect on the date of issuance of the permit. The issuance of this Operation Permit does not in any way guarantee that the system will operate properly or relieve any person now or hereafter owning, controlling, or using such system from any liability resulting from the failure of the system to operate properly. This document is issued subject to those restrictions and conditions shown on the permit(s) and the provisions of 15A NCAC 18A. 1900 in addition to those listed below under "Comments." This document shall be null and void if any information contained in the application is untrue or if any additions are made to the property which would increase the requirements for said system.

Notice: Disturbance of the designated repair area may result in the Suspension or Revocation of this permit.

Comments: System Classification & Type: 1/1q System IQ4-W G NA NA

DENR Authorized Agent: Chris Sherrill, RS, LSS Signature: Chris Sherrill

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St., Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

OPERATION PERMIT for an
ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

File #: 7835B Permit #: _____ Tax Parcel #: 031-182-51

Property Owner: JOSHUA STOVER

Job Location Address: 2321 MT. HOLLY - HUNTERSVILLE RD

City: CHARLOTTE State: NC Zip Code: 28214

OPERATION PERMIT CONDITIONS:

I. Performance: System shall perform in accordance with 15A NCAC 18A .1961.

II. Monitoring: System shall be monitored as required by 15A NCAC 18A .1961.

III. Maintenance: Ground absorption sewage treatment and disposal systems shall be checked, and the contents of the septic tank removed, periodically from all compartments, to ensure proper operation of the system. The contents shall be pumped whenever the solids level is found to be more than 1/3 of the liquid depth in any compartment.

IV. Operation: System shall be operated in accordance with 15A NCAC 18A .1961.

System Classification: III-A

*Operation Permits for Type V and VI systems expire five (5) years from the date of issuance (in accordance with Table V(a)). The system owner must contact GWS six (6) months prior to expiration for permit renewal.

Subsurface system operator required: Yes ☐ No ☑

☐ This type of system requires the system owner to maintain a contract with a certified operator to perform system inspection, maintenance, and reporting as required in 15A NCAC 18A .1961. and Table V(a). The system owner is responsible for all fees associated with these services.

☑ System does not require inspection by GWS on a routine frequency.

☐ System requires inspection by GWS once every five (5) years. The system owner is responsible for all fees associated with the inspection.

☐ System requires inspection by GWS once every three (3) years. The system owner is responsible for all fees associated with the inspection.

☐ System requires inspection by GWS once every twelve (12) months. The system owner is responsible for all fees associated with the inspection.

☐ System requires inspection by GWS once every six (6) months. The system owner is responsible for all fees associated with the inspection.

V. Other:

DENR Authorized Agent: Chris Sherrill Date: 7/9/08

Signature: Christopher M Sherrill

File #: 7835B
Date: 7/9/08
Inspected By: CS

Final Inspection Check List

Septic Tank

Tank construction EXISTING PCC

Septic tank installed in correct orientation and is level? Yes ☑ No ☐

Septic tank is in good condition with no visible defects or leaks? Yes ☑ No ☐

Septic tank stamped with appropriate markings? Yes ☑ No ☐

Id Number: — Date: — Size: — Gallons

Lids present and in good condition? Yes ☑ No ☐

Tank air vent unobstructed? Yes ☑ No ☐

Baffle wall with 4" opening unobstructed? Yes ☑ No ☐

Effluent filter installed correctly in tank? Yes ☑ No ☐

Outlet pipe has a watertight seal with cast in place boot and clamp? Yes ☑ No ☐

1/8" per ft. of fall on outlet pipe? Yes ☑ No ☐

Risers used appropriately if required? Yes ☑ No ☐

Pump Tank (If Applicable)

Pump tank installed with riser above grade and is level? Yes ☐ No ☐

Pump tank is in good condition with no visible defects or leaks? Yes ☐ No ☐

Inlet pipe properly sealed/grouted? Yes ☐ No ☐

Discharge pipe properly sealed/grouted? Yes ☐ No ☐

Pump tank stamped with appropriate markings? Yes ☐ No ☐

Id Number: _____ Date: _____ Size: _____ Gallons

Lids present and in good condition? Yes ☐ No ☐

Pump installed in tank? Yes ☐ No ☐

Pump Make _____ Model _____

Control floats installed correctly? Yes ☐ No ☐

Check valve installed correctly? Yes ☐ No ☐

Gate valve installed on discharge piping? Yes ☐ No ☐

Discharge pipe size? _____ in.

Nema 4X control panel used? Yes ☐ No ☐

Electrical conduits sealed from gas entry? Yes ☐ No ☐

Distribution Box (If Applicable)

1/8" per ft. of fall on inlet pipe? Yes ☐ No ☐

Distribution box installed at least 2' from septic tank? Yes ☐ No ☐

Distance from tank outlet _____ ft.

Distribution box and lid in good condition? Yes ☐ No ☐

D-box level and stable? Yes ☐ No ☐

Inlet and outlet/s properly sealed and watertight? Yes ☐ No ☐

Speed levels present and adjusted properly? Yes ☐ No ☐

Pressure Manifold (If Applicable)

Manifold material, Schedule _____ PVC

Manifold diameter _____ in.

Size of taps _____ in. / Number of taps _____

Shutoff valves provided for each tap? Yes ☐ No ☐

Cleanout installed and accessible? Yes ☐ No ☐

Access provided to set head pressure? Yes ☐ No ☐

Gate valve installed to regulate flow through manifold? Yes ☐ No ☐

Location of valve: _____

Manifold housed in appropriate enclosure? Yes ☐ No ☐

Manifold installed level and secured to enclosure? Yes ☐ No ☐

Pressure head set to _____ ft.

Drainfield (Conventional)

Number of lines installed _____

Total length of drainline installed _____ft.

Trench width _____ft.

Trench spacing O.C. _____ft.

Trench depth _____in.

Tire Chips Used? Yes ☐ No ☐

Geotextile fabric in place? Yes ☐ No ☐

Depth of stone / tire chips _____in.

Distance from house _____ft.

Distance from property lines: Left _____ft. Right _____ft. Front _____ ft. Rear _____ft.

Distance from well _____ft.

Drainlines installed level and on contour? Yes ☐ No ☐

Drainfield (Innovative 25% Reduction)

Number of lines installed 3

Total length of drainline installed 210 ft.

Trench width 3 ft.

Trench spacing O.C. 9 ft.

Trench depth 36 in.

Protective barrier installed over polystyrene? Yes ☐ No ☑

Distance from house 5+ ft.

Distance from property lines: Left 10+ ft. Right 10+ ft. Front 10+ ft. Rear 10+ ft.

Distance from well N/A ft.

Drainlines installed level and on contour? Yes ☑ No ☐

Drainfield (PPBPS 50% Reduction)

Number of lines installed _____

Total length of drainline installed _____ft.

Trench width _____ft.

Trench spacing O.C. _____ft.

Trench depth _____in.

6" sand bed on trench bottom? Yes ☐ No ☐

Correct type & amount of sand installed inside panels? Yes ☐ No ☐

Distance from house _____ft.

Distance from property lines: Left _____ft. Right _____ft. Front _____ ft. Rear _____ft.

Distance from well _____ft.

Drainlines installed level and on contour? Yes ☐ No ☐

Grade Shots with Level

Trench #: 1		Trench #: 2		Trench #: 3	
Shot #	Reading	Shot #	Reading	Shot #	Reading
1	4'10"	1	5'9"	1	6'10"
2		2		2	

Trench #: ___		Trench #: ___		Trench #: ___	
Shot #	Reading	Shot #	Reading	Shot #	Reading

Trench #: ___		Trench #: ___		Trench #: ___	
Shot #	Reading	Shot #	Reading	Shot #	Reading
