8932B

Supervisor/Administrative Professional Checklist

New Septic ☑ **New Well** ☐ **Use Existing** ☐ **Alteration** ☐ **Modified Plot Plan** ☐

New Septic Fees Paid:

IP ($250.00) DW2 4/22/14 Initials/Date

CA ($200.00) LE 6/12/15 Initials/Date

OP ($200.00) LE 6/12/15 Initials/Date

(CA and OP fees need to be paid before a building permit can be issued)

New Well Fee Paid: $550.00 _____ Initials/Date

Use Existing Fee Paid: $100.00 _____ Initials/Date

Alteration Fee Paid: $300.00 (Total) $200 (If use existing was paid)_____ Initials/Date

Modified Plot Plan Fee Paid: $100.00 _____ Initials/Date

Floor plans need to be submitted and reviewed before CA can be issued. ☑ Reviewed ☑ SAM 6/23/15

This site is served by septic and well. Verify each is complete before final hold is released. ☑

Septic file completed. ☑ SAM 4/26/16 Well file completed. ☐ _____

Send permit for signature. ☑ Signature received. ☑ 6/3/14

This septic system requires a certified operator contract before final hold is released. ☐

Certified operator contract is on file. ☐ _____

Groundwater & Wastewater Services
Septic Project File & Data Review Worksheet

GWS File#: 8932B WASPS App #: 6808

Primary ES assigned to project: Jacob Presley

Secondary ES assigned to project:

Project Type: New System ☑ Alteration ☐ Repair ☐ Modified Plot Plan ☐

I. File Review:

Rule or Law	Permit Application			
.1937(d)	Is the Application complete	Yes ☑	No ☐	N/A ☐
.1937(d)	Is there a Site plan/Plat with application	Yes ☑	No ☐	N/A ☐
.1937(d)	Is the Facility shown?	Yes ☑	No ☐	N/A ☐
.1937(d)	Are appurtenances shown	Yes ☑	No ☐	N/A ☐
	Site Evaluation Information			
.1939 (a)(1)	Topography and Landscape Position Recorded?	Yes ☑	No ☐	N/A ☐
.1940 (a-g)	Slope % Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(2)	Texture Class Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(2)	Structure type Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(2)	Consistence Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(2)	Mineralogy Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(3)	Soil Wetness Condition Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(4)	Soil Depth to Rock or Parent Material Recorded When Encountered	Yes ☑	No ☐	N/A ☐
.1939 (a)(5)	Depth to Restrictive Horizons Recorded When Encountered?	Yes ☑	No ☐	N/A ☐
.1939 (a)(6)	Sufficient Available Space Recorded?	Yes ☑	No ☐	N/A ☐
.1937(m)	Are the Profile Locations Shown?			
.1939(a)	Are the S/PS Profiles in system & in repair area?	Yes ☑	No ☐	N/A ☐
& .1945(b)	Number of auger borings made: 4 Were sufficient auger borings made?	Yes ☑	No ☐	N/A ☐
.1939(d), .1955, .1956, .1957	LTAR 0.3	Yes ☑	No ☐	N/A ☐
	Improvement Permit/Construction Authorization			
.1937(g) 130A-336(a)	Proposed System Type stated-Initial	Yes ☑	No ☐	N/A ☐
.1945(b)	Proposed System Type stated-Repair	Yes ☑	No ☐	N/A ☐
130A-336 (a)(3)	System location identifiable by setbacks - Initial	Yes ☑	No ☐	N/A ☐
.1937(g) .1945(b)	System components shown – Initial	Yes ☑	No ☐	N/A ☐
.1945(b)	Repair area shown	Yes ☑	No ☐	N/A ☐
.1937 (f)(g)	Does System design match facility, flow & WWcharacteristics?	Yes ☑	No ☐	N/A ☐
.1937 (f)(g)	Is System design consistent with soil/site conditions?	Yes ☑	No ☐	N/A ☐
.1937 (f)(g)	Is the System located in the approved area?	Yes ☑	No ☐	N/A ☐
130A-336(a)	Is the Design flow (gpd) indicated?	Yes ☑	No ☐	N/A ☐

130A-336(a)	Number of Bedrooms, employees, seats, etc. indicated?	Yes ☑	No ☐	N/A ☐	
.1937(g)	Trench depth indicated?	Yes ☑	No ☐	N/A ☐	
.1937(g)	Trench width indicated?	Yes ☑	No ☐	N/A ☐	
.1937(g)	Trench length indicated?	Yes ☑	No ☐	N/A ☐	
130A-336(a)(1)	Proposed/existing well shown?	Yes ☑	No ☐	N/A ☐	Have not applied for well permit yet
130A-336(a)(1)	Property line lengths shown?	Yes ☑	No ☐	N/A ☐	
130A-336(a)	Facility/appurtenance setbacks shown from fixed points?	Yes ☑	No ☐	N/A ☐	

Operation Permit

.1937(i)	System type as described in table V(a) of rule .1961	Yes ☐	No ☐	N/A ☐
.1937(i)	Conditions for system performance, operation, maintenance, monitoring and reporting.	Yes ☐	No ☐	N/A ☐

IL WASPS Review:

Construction authorization issued	Yes ☑	No ☐	N/A ☐
Installation approval issued	Yes ☐	No ☐	N/A ☐
Operation permit issued	Yes ☑	No ☐	N/A ☐
Other related documentation	Yes ☑	No ☐	N/A ☐

Items requiring correction/modification: _____

Comments:

_____

_____

_____

_____

_____

IA issued date: 12/15/15

OP issued date: 4/26/16

Review performed by: JAM Date performed: _____

8932B

MECKLENBURG COUNTY
HEALTH DEPARTMENT

APPLICATION FOR A RESIDENTIAL SITE IMPROVEMENT PERMIT/ CONSTRUCTION AUTHORIZATION FOR AN ON-SITE WASTEWATER SYSTEM, NEW WELL INSTALLATION, OR REPAIR OF EXISTING WELL

1. SEPTIC / TYPE APPLICATION: ○ N/A ☑ NEW SYSTEM ○ ALTERATION ○ REPAIR ○ MODIFIED PLOT PLAN

2. WELL / TYPE APPLICATION: ○ N/A ○ NEW WELL ○ MAJOR REPAIR ○ ABANDONMENT

3. JOB LOCATION INFORMATION:
TAX PARCEL NUMBER: 13917340
STREET ADDRESS: 16112 Blackberry Hills Dr
CITY: MIDLAND
STATE: NC ZIP: 28107
SUBDIVISION NAME: Blackberry Hills
LOT #: 4 LOT SIZE (acres): 2.046
TOWNSHIP:
☑ MECKLENBURG ○ CORNELIUS ○ HUNTERSVILLE
○ DAVIDSON ○ CHARLOTTE ○ PINEVILLE
○ MATTHEWS ○ MINT HILL

4. BUILDING INFORMATION:
BUILDING TYPE:
○ SINGLE MOBILE HOME ○ MODULAR HOME
○ DOUBLE WIDE ○ MULTIPLE FAMILY
☒ HOUSE ○ OTHER _____
HEATED SQUARE FOOTAGE: 2400
NUMBER OF BEDROOMS: 4
NUMBER OF OCCUPANTS: 2
FOUNDATION TYPE:
○ CONCRETE SLAB ○ BASEMENT WITH PLUMBING
☒ CRAWL SPACE ○ BASEMENT WITH NO PLUMBING

5. IF PLANNING TO EXPAND OR ALTER THE EXISTING SEPTIC SYSTEM PLEASE COMPLETE THE FOLLOWING SECTION: ☒ N/A
NUMBER OF BEDROOMS TO BE ADDED: _____ NUMBER OF ADDITIONAL OCCUPANTS IN THE RESIDENCE: _____

6. WATER SUPPLY: ○ MUNICIPAL ☒ PRIVATE WELL ○ PUBLIC WELL ○ SHARED WELL ○ OTHER _____

7. PROPOSED USE OF WELL: ○ N/A ○ IRRIGATION ☒ POTABLE (DRINKING WATER) ○ OTHER _____

8. PLEASE INDICATE AND RANK DESIRED SEPTIC SYSTEM TYPE(S) IN ORDER OF PREFERENCE (1-MOST DESIRED 5-LEAST DESIRED):
☐ N/A ☐ ANY TYPE ☐ CONVENTIONAL ☐ ACCEPTED ☐ INNOVATIVE ☐ ALTERNATIVE ☐ OTHER _____

8A. RANK: 1 2 3 4 ___

9. DO ANY OF THE FOLLOWING APPLY TO THE PROPERTY IN QUESTION? IF "YES" PLEASE ATTACH SUPPORTING DOCUMENTATION.

BURIED CABLES, LANDFILLS, STUMPHOLES	○ YES ☒ NO	GRADING/SOIL REMOVAL PERFORMED	○ YES ☒ NO
EXISTING WASTEWATER (SEPTIC) SYSTEMS	○ YES ☒ NO	JURISDICTIONAL WETLANDS	○ YES ☒ NO
WELLS, SPRINGS, OR WATER LINES	○ YES ☒ NO	APPROVAL REQUIRED BY ANY OTHER PUBLIC AGENCY	○ YES ☒ NO
EASEMENTS OR RIGHT-OF-WAYS	○ YES ☒ NO	WASTEWATER OTHER THAN DOMESTIC SEWAGE	○ YES ☒ NO
CHEMICAL/PETROLEUM STORAGE TANKS	○ YES ☒ NO	KNOWN UNDERGROUND CONTAMINATION	○ YES ☒ NO
WASTE STORAGE	○ YES ☒ NO	GROUNDWATER USE RESTRICTIONS/VARIANCES	○ YES ☒ NO

10. WHAT DATE WAS THE PROPERTY ORIGINALLY DEEDED AND RECORDED? _____ ☐ UNKNOWN

11. WHAT IS THE ANTICIPATED CLOSING DATE FOR THIS PROPERTY? MAY 30, 2014 ☐ N/A

12. PROPERTY OWNER:
NAME: JAY & CYNTHIA ROSSI
ADDRESS: 10720 VICINO CT.
CITY: MATTHEWS
STATE: NC ZIP: 28105
WORK PHONE: 704 573 4335
MOBILE PHONE: 704 668 1297
FAX: _____
E-MAIL: CLTCROSSI@CAROLINA.RR.COM

13. OWNER'S LEGAL REPRESENTATIVE, IF APPLICABLE:
NAME: Brenda Farmer
ADDRESS: 4001 Hwy 24/27
CITY: Midland, NC 28107
STATE: NC ZIP: 28107
WORK PHONE: 704-791-5437
MOBILE PHONE: _____
FAX: 704-888-3805
E-MAIL: brendaleefarmer@gmail.com

MECKLENBURG COUNTY – GROUNDWATER & WASTEWATER SERVICES
700 N. TRYON ST. SUITE 211 CHARLOTTE, NC 28202, OFFICE: 704-336-5103, FAX: 704-336-6894

Revised on: 12/15/10



14. SEPTIC SYSTEM PERMIT APPLICATION:

If the information in this application is falsified, changed, or the site is altered, then the Improvement Permit and Authorization to Construct shall become invalid. *I have read this application and certify that the information provided herein is true, complete and correct.* Authorized county and state officials are granted right of entry to conduct necessary inspections to determine compliance with applicable laws and rules. I understand that I am solely responsible for the proper identification and labeling of all property lines and corners and making the site accessible so that a complete site evaluation can be performed. The permit is valid for either sixty (60) months or is non-expiring depending upon the documentation submitted: complete site plan = 60 months, complete plat = non-expiring.

BSA *(Initial here for septic system applications)*

15. WELL PERMIT APPLICATION:

If the information in this application is falsified, changed, or the site is altered, then the Well Permit shall become invalid. I have read this application and certify that the information provided herein is true, complete and correct. Authorized county and state officials are granted right of entry to conduct necessary inspections to determine compliance with applicable laws and rules. I understand that I am solely responsible for the proper identification and labeling of all property lines and corners and making the site accessible so that a complete site evaluation can be performed. The permit is valid for a period of twelve (12) months from the date of issuance.

_____ *(Initial here for well applications)*

16. APPLICATION SIGNATURE SECTION:

ONLY COMPLETE APPLICATIONS WILL BE PROCESSED. A proper signature is required in order to process your application. Please review the *application carefully and sign in the space provided below.* A PROPOSED PLOT PLAN is required to be submitted with each application.

Property Owner's or Owner's Legal Representative Signature

April 16, 2014
Date

OFFICE USE ONLY

● SURVEY PLAT TO SCALE SUBMITTED ○ SCALED SITE PLAN SUBMITTED ○ UN-SCALED SITE PLAN SUBMITTED

SEPTIC APPLICATION FEE RECEIVED: $_____ DATE FEE RECEIVED: _____

WELL APPLICATION FEE RECEIVED: $_____ DATE FEE RECEIVED: _____

APPLICATION PROCESSED BY: _____

GWS FILE NUMBER ASSIGNED: _____

APPLICATION ID NUMBER ASSIGNED: _____

COMMENTS:

MECKLENBURG COUNTY – GROUNDWATER & WASTEWATER SERVICES
700 N. TRYON ST. SUITE 211 CHARLOTTE, NC 28202, OFFICE: 704-336-5103, FAX: 704-336-6894

Revised on: 12/15/10

Department of Environment, Health, and Natural Resources
Division of Environmental Health
On-site Wastewater Section

Sheet: 1 of 2
Property ID: 139-173-40
Lot #: 4
File #: *8932B*
AppID: 6808

SOIL/SITE EVALUATION
for ON-SITE WASTEWATER SYSTEM

Jay & Cynthia Rossi
Address: 10720 Vicino Ct., Matthews, NC 28105
Proposed Facility: 4 BR Residence
Design Flow (.1949): 480 GPD
Location of Site: 16112 Blackberry Hills Dr, Midland, NC 28107
Water Supply: [X] Public [X] Individual [ ] Well
Evaluation Method: [X] Auger Boring [ ] Pit
Type of Wastewater: [X] Sewage [ ] Industrial Process

Applicant: Brenda Farmer
Date Evaluated: 5/7/2014
Property Size: 2.046 ac
Property Recorded: Unknown
[ ] Spring [ ] Other
[ ] Cut
[ ] Mixed

PROFILE #	1940 Landscape Position/ Slope%	Horizon Depth (IN:)	SOIL MORPHOLOGY 1941 .1941 Structure/ Texture	.1941 Consistence Mineralogy	b PROFILE FACTORS 1942 Soil Wetness/ Color	.1943 Soil Depth (IN:)	.1956 Sapro Class	.1944 Restr Horiz	General Comments	Profile Class & LTAR	Maximum Trench Bottom Depth for 3' Wide Conventional Trench
Boring #1	LS 4%	0 - 2	gr L	FR SEXP	>50"	50	NA	NA		PS IV 0.3	36"
		2 - 8	mfsbk CL	FR SEXP							
		8 - 50	mfsbk C	FI SEXP							
Boring #2	LS 3%	0 - 2	gr L	FR SEXP	>50"	50	NA	NA		PS IV 0.3	36"
		2 - 50	mfsbk C	FI SEXP							
Boring #3	R 2%	0 - 3	gr L	FR SEXP	>49"	49	NA	NA	yellow brown mottles from 41 - 49"	PS IV 0.3	36"
		3 - 12	mfsbk CL	FR SEXP							
		12 - 41	mfsbk C	FI SEXP							
		41 - 49	mfabk C	FI SEXP							
Boring #4	R 2%	0 - 4	mfsbk CL	FR SEXP	>49"	49	NA	NA	yellow brown mottles from 37 - 49"	PS IV 0.3	36"
		4 - 37	mfsbk C	FI SEXP							
		37 - 49	mfabk C	FI SEXP							

Description	Initial System	Repair System
Available Space (.1945)	PS	PS
System Type(s)	IIIbg	IIIbg
Site LTAR (gpd/sq ft)	0.3	0.3


Other Factors (.1946):
Soil Evaluation By: Jacob Presley, REHSI, LSS
Others Present:
Site Classification (.1948): Provisionally Suitable
Site Evaluation By: Jacob Presley, REHSI, LSS
Others Present:

COMMENTS:

Landscape Position	Group	Texture	.1955 LTAR	Structure
R-Ridge	I	S-Sand	1.2 - 0.8	sg-Single Grain
SS-Shoulder Slope		LS-Loamy Sand		mass-Massive
LS-Linear Slope				cr-Crumb
FS-Foot Slope	II	SL-Sandy Loam	0.8 - 0.6	gr-Granular
NS-Nose Slope		L-Loam		sbk-Subangular Blocky
HS-Head Slope				abk-Angular Blocky
CC-Concave Slope	III	Si-Silt	0.6 - 0.3	pl-Platy
CV-Convex Slope		SiCL-Silty Clay Loam		pr-Prismatic
T-Terrace		CL-Clay Loam		Sap-Saprolite
FP-Flood Plain		SCL-Sandy Clay Loam		**Structure Prefixes**
D-Drainage Way		SiL-Silt Loam		w-weak
				m-moderate
				s-strong
				f-fine
	IV	SC-Sandy Clay	0.4 - 0.1	m-medium
		SiC-Silty Clay		c-coarse
		C-Clay		

Consistence Moist	Consistence Wet	Mineralogy
VFR-Very Friable	SS-Slightly Sticky	SEXP-Slightly Expansive
FR-Friable	S-Sticky	EXP-Expansive
FI-Firm	VS-Very Sticky	
VFI-Very Firm	NP-Non-Plastic	**Classification**
EFI-Extremely Firm	SP-Slightly Plastic	US-Unsuitable
	P-Plastic	PS-Provisionally Suitable
	VP-Very Plastic	S-Suitable
		NA-Not Applicable

Sketch of Soil Evaluation Locations

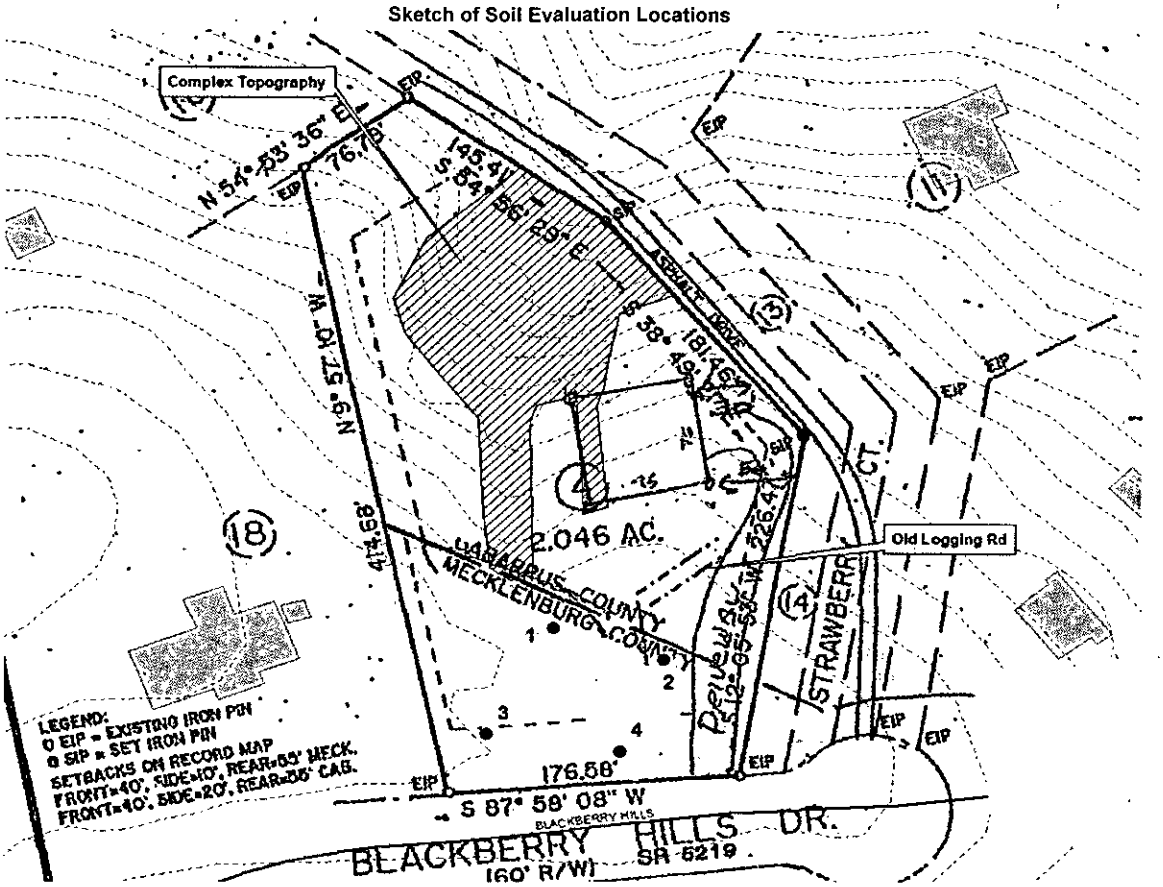

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St, Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

IMPROVEMENT PERMIT for a RESIDENTIAL ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

Permit #: **30006808** GWS File #: **8932B** Tax Parcel #: **139-173-40**

- This IMPROVEMENT PERMIT is subject to revocation if site plans or the intended use change. There is to be NO grading, filling, or disturbance of the soil in the area of the septic tank system or repair area.
- CONSTRUCTION AUTHORIZATION must be obtained prior to receiving a Building Permit. The Construction Authorization is **NOT** transferable. Do not clear, grade, fill or disturb soil prior to obtaining a Construction Authorization.
- Domestic-type wastewater only. No industrial process wastewater may be discharged into the system.

I. This Improvement Permit Shall: Expire in Five (5) Years **Expiration Date (If Applicable):** 5/8/2019

Type of Installation: Residential - New System Lot Number: 4

Structure Type: HOUSE Size (ft^2): 2400 # Bedrooms: 4 # Occupants: 2

Building Foundation: Crawl Space Water Supply: Private Well

II. Initial System Type: Pump to Approved **System Classification:** IIIb

Initial System Specifications:

Design Flow (gpd):	480	LTAR (gpd/ft^2):	0.3	Septic Tank Size (gal):	1500	Pump Tank Size (gal):	1000
Trench Width (ft):	3	Trench Spacing (ft):	9	Absorption Area (ft^2):	1200	Total Trench Length (ft):	400
Maximum Trench Depth (in):	36	Depth of Media (in):	12	Distribution Device:	Pressure Manifold		

III. Repair System Type: Pump to Approved **System Classification:** IIIb

Repair System Specifications:

Design Flow (gpd):	480	LTAR (gpd/ft^2):	0.3	Septic Tank Size (gal):	1500	Pump Tank Size (gal):	1000
Trench Width (ft):	3	Trench Spacing (ft):	9	Absorption Area (ft^2):	1200	Total Trench Length (ft):	400
Maximum Trench Depth (in):	36	Depth of Media (in):	12	Distribution Device:	Pressure Manifold		

IV. Permit Conditions/Comments:

(Please See the Following Page for Permit Conditions.)

The undersigned, an authorized agent of the MECKLENBURG COUNTY HEALTH DEPARTMENT, certifies that the Department is issuing an IMPROVEMENT PERMIT for the above referenced property. This permit is being issued in accordance with the *Laws and Rules For Sewage Treatment, and Disposal Systems* and is subject to the following provisions:

- No work shall be conducted on the septic system until an INSTALLATION APPROVAL is granted by the Department.
- The septic system installer shall be a registered septic contractor with Mecklenburg County Health Department.
- The permitted system shall be installed in accordance with the included PLOT PLAN.
- This IMPROVEMENT PERMIT is transferable.

DENR Authorized Agent: Jacob Presley

Signature: JPS

Date Issued: 5/8/2014

Owner/Legal Agent: JAY E. Rossi - Cynthia S. Rossi
Print Name

Signature: Jay E Rossi - Cynthia S. Rossi

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St, Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

IMPROVEMENT PERMIT for a RESIDENTIAL
ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

Permit #: **30006808** GWS File #: **8932B**

IV. Permit Conditions/Comments:

- This type of septic system requires an inspection once every 5 years by our office. The system owner is responsible for any fees, as determined by the Mecklenburg County Board of Commissioners, associated with this inspection.
- All components of the septic system must be installed in accordance with the required setbacks listed on the corresponding plot plan.
- All components of the septic system must be located at least 100 ft. (50 ft. minimum) from all private wells.
- Flow from all gutters and downspouts shall be directed not to discharge water onto or across any part of the septic system.

The undersigned, an authorized agent of the MECKLENBURG COUNTY HEALTH DEPARTMENT, certifies that the Department is issuing an IMPROVEMENT PERMIT for the above referenced property. This permit is being issued in accordance with the *Laws and Rules For Sewage Treatment and Disposal Systems* and is subject to the following provisions:

- No work shall be conducted on the septic system until an INSTALLATION APPROVAL is granted by the Department.
- The septic system installer shall be a registered septic contractor with Mecklenburg County Health Department.
- The permitted system shall be installed in accordance with the included PLOT PLAN.
- This IMPROVEMENT PERMIT is transferable.

DENR Authorized Agent: Jacob Presley

Signature: JPP

Date Issued: 5/8/2014

Owner/Legal Agent: JAY E. Rossi - Cynthia S. Rossi
Print Name

Signature: Jay E Rossi - Cynthia S. Rossi

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St., Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

Septic System Pre-Construction Meeting Checklist

File # 89328 App # 6808 Tax Parcel # 139-173-40

Property Owner: Jay Rossi

Job Location Address: 16112 Blackberry Hills Dr

City: Midland State: NC Zip Code: ~~28096~~ 28107

1. **Does System design match facility, flow & wastewater characteristics?**

   ☑ YES ☐ NO

   Comments: _____

2. **Is there sufficient available space for the septic systems initial and repair areas?**

   ☑ YES ☐ NO

   Comments: _____

3. **Can the septic system be installed per the permit conditions and drawing on file?**

   ☑ YES ☐ NO

   Comments: _____

*** If "NO" is checked for any of the above the existing permit may need to be revoked.**

Permission is hereby given to ☑ install ☐ alter ☐ repair an on-site wastewater treatment & and disposal system, with subsurface soil absorption and effluent discharge meeting all of the construction requirements of 15A NCAC 18A .1900 which are in effect on the date of granting this approval. **System shall not be installed while soils are in wet condition.**

Bradley W. Hallman — 12/15/15

Authorized Agent **Date**

Commercial Sevices.

Others Present

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St., Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DHHS
Division of Environmental Health
On-Site Wastewater Section

OPERATION PERMIT for an
ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

File #: 8932B Permit #: 6808 Tax Parcel #: 139-173-40

Property Owner: Jay Rossi

Job Location Address: 16112 Blackberry Hills Dr

City: Midland State: NC Zip Code: 28107

Operation Permit Issuance Date: 4-26-16 Contractor Name: Jerry Wetley

Permitted Design Flow: 480 GPD Liquid Capacity of Dosing Tank: 1000 gallons 6/29/15

Liquid Capacity of Septic Tank: 1000 gallons Manufacture Lowder Effluent Pump Model: ME-45

Drainfield Installation ☐ N/A

Trench Depth: 36 inches

Trench Width: 3 feet

Line Spacing: 9 feet (O.C.)

Total line length: 408 feet

# of Lines: 4 @ 102 feet

Depth of Media: 12 inches (Type) Quick 4

Depth of Cover: 12+ inches

Distribution Device: manifold

Bed Installation *(For Repair Installations ONLY.)* ☒ N/A

Bed Depth: _____ inches

Bed Width: _____ feet

Total line length: _____ feet

# of Lines: _____ @ _____ feet

Depth of Media: _____ inches (Type) _____

Depth of Cover: _____ inches

Distribution Device: _____

Water Supply Source

☐ Municipal ☒ Private Well ☐ Community Well

☐ Other _____

System Installation Setbacks

Distance from Building Foundation: 15' feet

Distance from Property Line: 10 feet

Distance from Water Supply Source: 100' feet


Inspection Dates

Tank(s) Inspected: 1-7-16 Lowder 9-8 All STB-48 6/29/15

Excavation Inspected: 70' 1-7-16

Pump & Controls Inspected: 4-13-16

SKETCH OF SYSTEM INSTALLATION (As-Built Drawing)

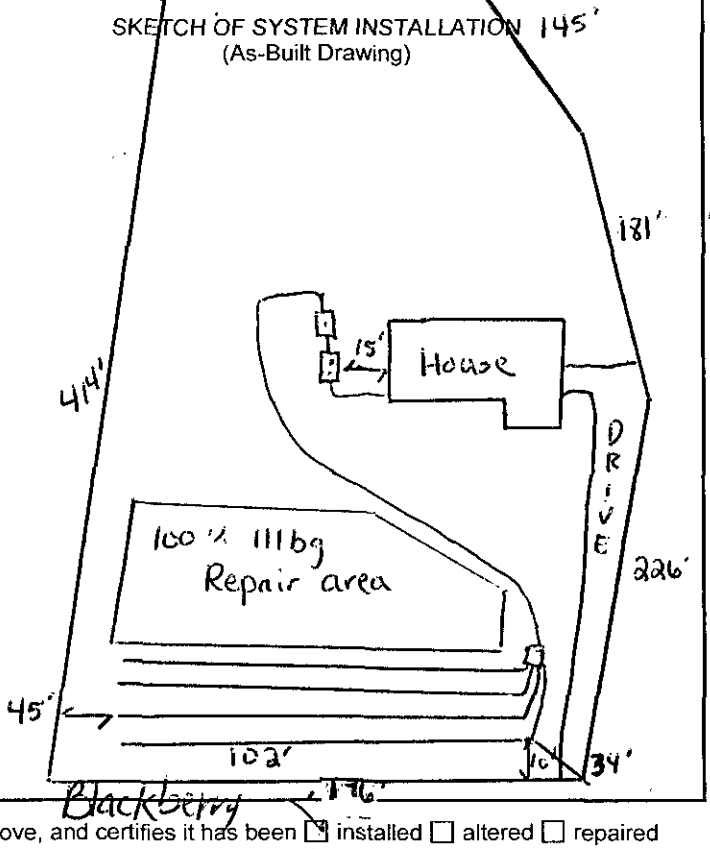

The undersigned has inspected the Septic Tank System described above, and certifies it has been ☒ installed ☐ altered ☐ repaired ☐ as detailed in the plot above ☒ in accordance with the permit issued and meets the provisions of 15A NCAC 18A. 1900, "Laws and Rules for Sewage Treatment and Disposal Systems" in effect on the date of issuance of the permit. The issuance of this Operation Permit does not in any way guarantee that the system will operate properly or relieve any person now or hereafter owning, controlling, or using such system from any liability resulting from the failure of the system to operate properly. This document is issued subject to those restrictions and conditions shown on the permit(s) and the provisions of 15A NCAC 18A. 1900 in addition to those listed below under "Comments." This document shall be null and void if any information contained in the application is untrue or if any additions are made to the property which would increase the requirements for said system.

Notice: Disturbance of the designated repair area may result in the Suspension or Revocation of this permit.

Comments: System Classification & Type: III b | 04 | p | NA | NA

DENR Authorized Agent: April Bumgarner Signature: April Bumgarner, REHS

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St., Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

OPERATION PERMIT for an
ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

File #: 89328 Permit #: 6808 Tax Parcel #: 139-173-40

Property Owner: Jay Rossi

Job Location Address: 16112 Blackberry Hills Dr.

City: Midland State: NC Zip Code: 28107

OPERATION PERMIT CONDITIONS:

I. Performance: System shall perform in accordance with 15A NCAC 18A .1961.

II. Monitoring: System shall be monitored as required by 15A NCAC 18A .1961.

III. Maintenance: Ground absorption sewage treatment and disposal systems shall be checked, and the contents of the septic tank removed, periodically from all compartments, to ensure proper operation of the system. The contents shall be pumped whenever the solids level is found to be more than 1/3 of the liquid depth in any compartment.

IV. Operation: System shall be operated in accordance with 15A NCAC 18A .1961.

System Classification: IIIb

*Operation Permits for Type V and VI systems expire five (5) years from the date of issuance (in accordance with Table V(a)). The system owner must contact GWS six (6) months prior to expiration for permit renewal.

Subsurface system operator required: Yes ☐ No ☒

☐ This type of system requires the system owner to maintain a contract with a certified operator to perform system inspection, maintenance, and reporting as required in 15A NCAC 18A .1961. and Table V(a). The system owner is responsible for all fees associated with these services.

☐ System does not require inspection by GWS on a routine frequency.

☒ System requires inspection by GWS once every five (5) years. The system owner is responsible for all fees associated with the inspection.

☐ System requires inspection by GWS once every three (3) years. The system owner is responsible for all fees associated with the inspection.

☐ System requires inspection by GWS once every twelve (12) months. The system owner is responsible for all fees associated with the inspection.

☐ System requires inspection by GWS once every six (6) months. The system owner is responsible for all fees associated with the inspection.

V. Other:

DENR Authorized Agent: April Bumgarner Date: 4-26-16

Signature: April Bumgarner, REHS

MECKLENBURG COUNTY
LAND USE AND ENVIRONMENTAL SERVICES
Payment Receipt

Receipt Information

Date:	06/12/15	**Amount:**	200.00
Receipt #:	95028	**Tendered:**	200.00
Check / Auth #:	CHECK 1642	**Returned:**	0.00
Received By:	ELLISLW		

Account Information

Account #: 200000
Contractor: Weiss Custom Homes Corp
Attn:
Address: 10612 Providence Rd Ste D #203
Address:
City/State/Zip: Charlotte, NC 28277

Item	Description	Permit#	Quantity	Unit Price	Total Price
0703	Septic Operational Permit 16112 BlackBerry Hills Dr		1	200.00	200.00

Outstanding Balances

Month-To-Date	Prior Month	30 Days	60 Days	90 Days	Balance

MECKLENBURG COUNTY
LAND USE AND ENVIRONMENTAL SERVICES
Payment Receipt

Receipt Information

Date:	06/12/15	**Amount:**	200.00
Receipt #:	95027	**Tendered:**	200.00
Check / Auth #:	CHECK 1642	**Returned:**	0.00
Received By:	ELLISLW		

Account Information

Account #: 200000
Contractor: Weiss Custom Homes Corp
Attn:
Address: 10612 Providence Rd Ste D #203
Address:
City/State/Zip: Charlotte, NC 28277

Item	Description	Permit#	Quantity	Unit Price	Total Price
0734	Septic Construction Authorizat 16112 BlackBerry Hills Dr		1	200.00	200.00

Outstanding Balances

Month-To-Date	Prior Month	30 Days	60 Days	90 Days	Balance

S

FEE: 200.00
DATE:6/23/2015

MECKLENBURG COUNTY
GROUNDWATER & WASTEWATER SERVICES

FILE NUMBER: 8932B

PERMIT NUMBER: 30006808

PARCEL NUMBER: 13917340

JOB LOCATION INFORMATION

ADDRESS: 16112 BLACKBERRY HILLS DR

CITY: MIDLAND **STATE: NC** **ZIP:** 28107

ISSUED TO: Jay & Cynthia Rossi

CONSTRUCTION AUTHORIZATION ISSUANCE DATE: 6/23/2015

CONSTRUCTION AUTHORIZATION CONDITIONS


1. WASTEWATER SYSTEM CONSTRUCTION AND INSTALLATION MUST MEET ALL CONDITIONS AND SPECIFICATIONS AS SET FORTH IN IMPROVEMENT PERMIT NUMBER 30006808, AND THE ATTACHED SITE PLAN WITH SYSTEM DETAILS. CONSTRUCTION AND INSTALLATION MUST ALSO MEET ALL REQUIREMENTS SET FORTH IN THE RULES GOVERNING SANITARY SEWAGE COLLECTION, TREATMENT, AND DISPOSAL AND ANY OTHER APPLICABLE RULES AND LAWS.

2. A PRE-CONSTRUCTION MEETING MUST BE SECURED PRIOR TO INSTALLATION OF THE SEPTIC TANK SYSTEM. THE INSTALLER OF THE SYSTEM SHALL BE A LICENSED SEPTIC TANK CONTRACTOR WITH THE NORTH CAROLINA ONSITE WASTEWATER CONTRACTOR INSPECTOR CERTIFICATION BOARD.

3. ANY ALTERATION IN SITE OR SOIL CONDITIONS (INCLUDING LOCATION OF STRUCTURES AND APPURTENANCES) OR MODIFICATION IN USE, DESIGN WASTEWATER FLOW, OR WASTEWATER CHARACTERISTICS AS SPECIFIED IN THE ASSOCIATED IMPROVEMENT PERMIT AND APPLICATION, MAY SUBJECT THIS CONSTRUCTION AUTHORIZATION AND ASSOCIATED PERMIT(S) TO REVOCATION.

4. THIS CONSTRUCTION AUTHORIZATION AS PROVIDED IN G.S. 130A-335(f) AND G.S. 130A-336(b) SHALL BE VALID FOR A PERIOD EQUAL TO THE VALIDITY OF THE IMPROVEMENT PERMIT, NOT TO EXCEED 60 MONTHS.


Parcel # 139-173-40
File # 8932B
AppID: 6808

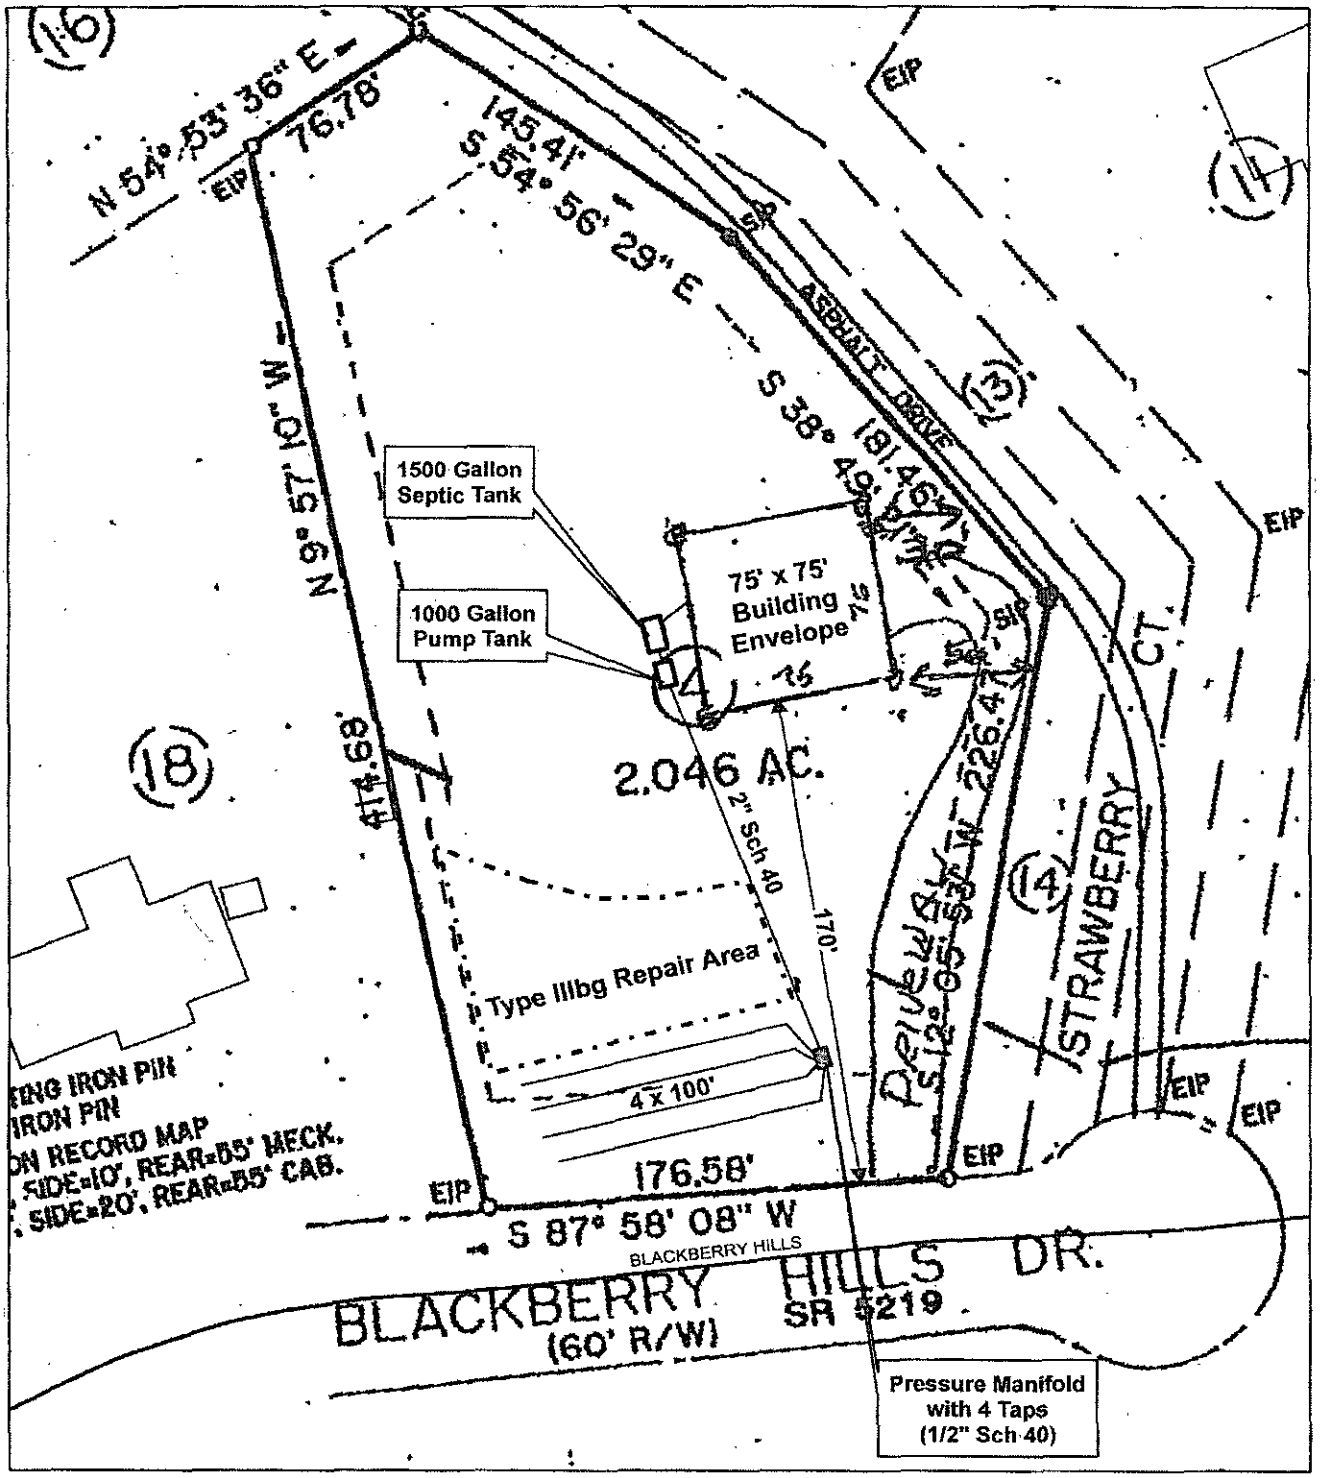

Map Created By: Jacob Presley
Map Created On: 5/8/14

0 30 60 Feet

Parcel # 139-173-40
File # 8932B
AppID: 6808

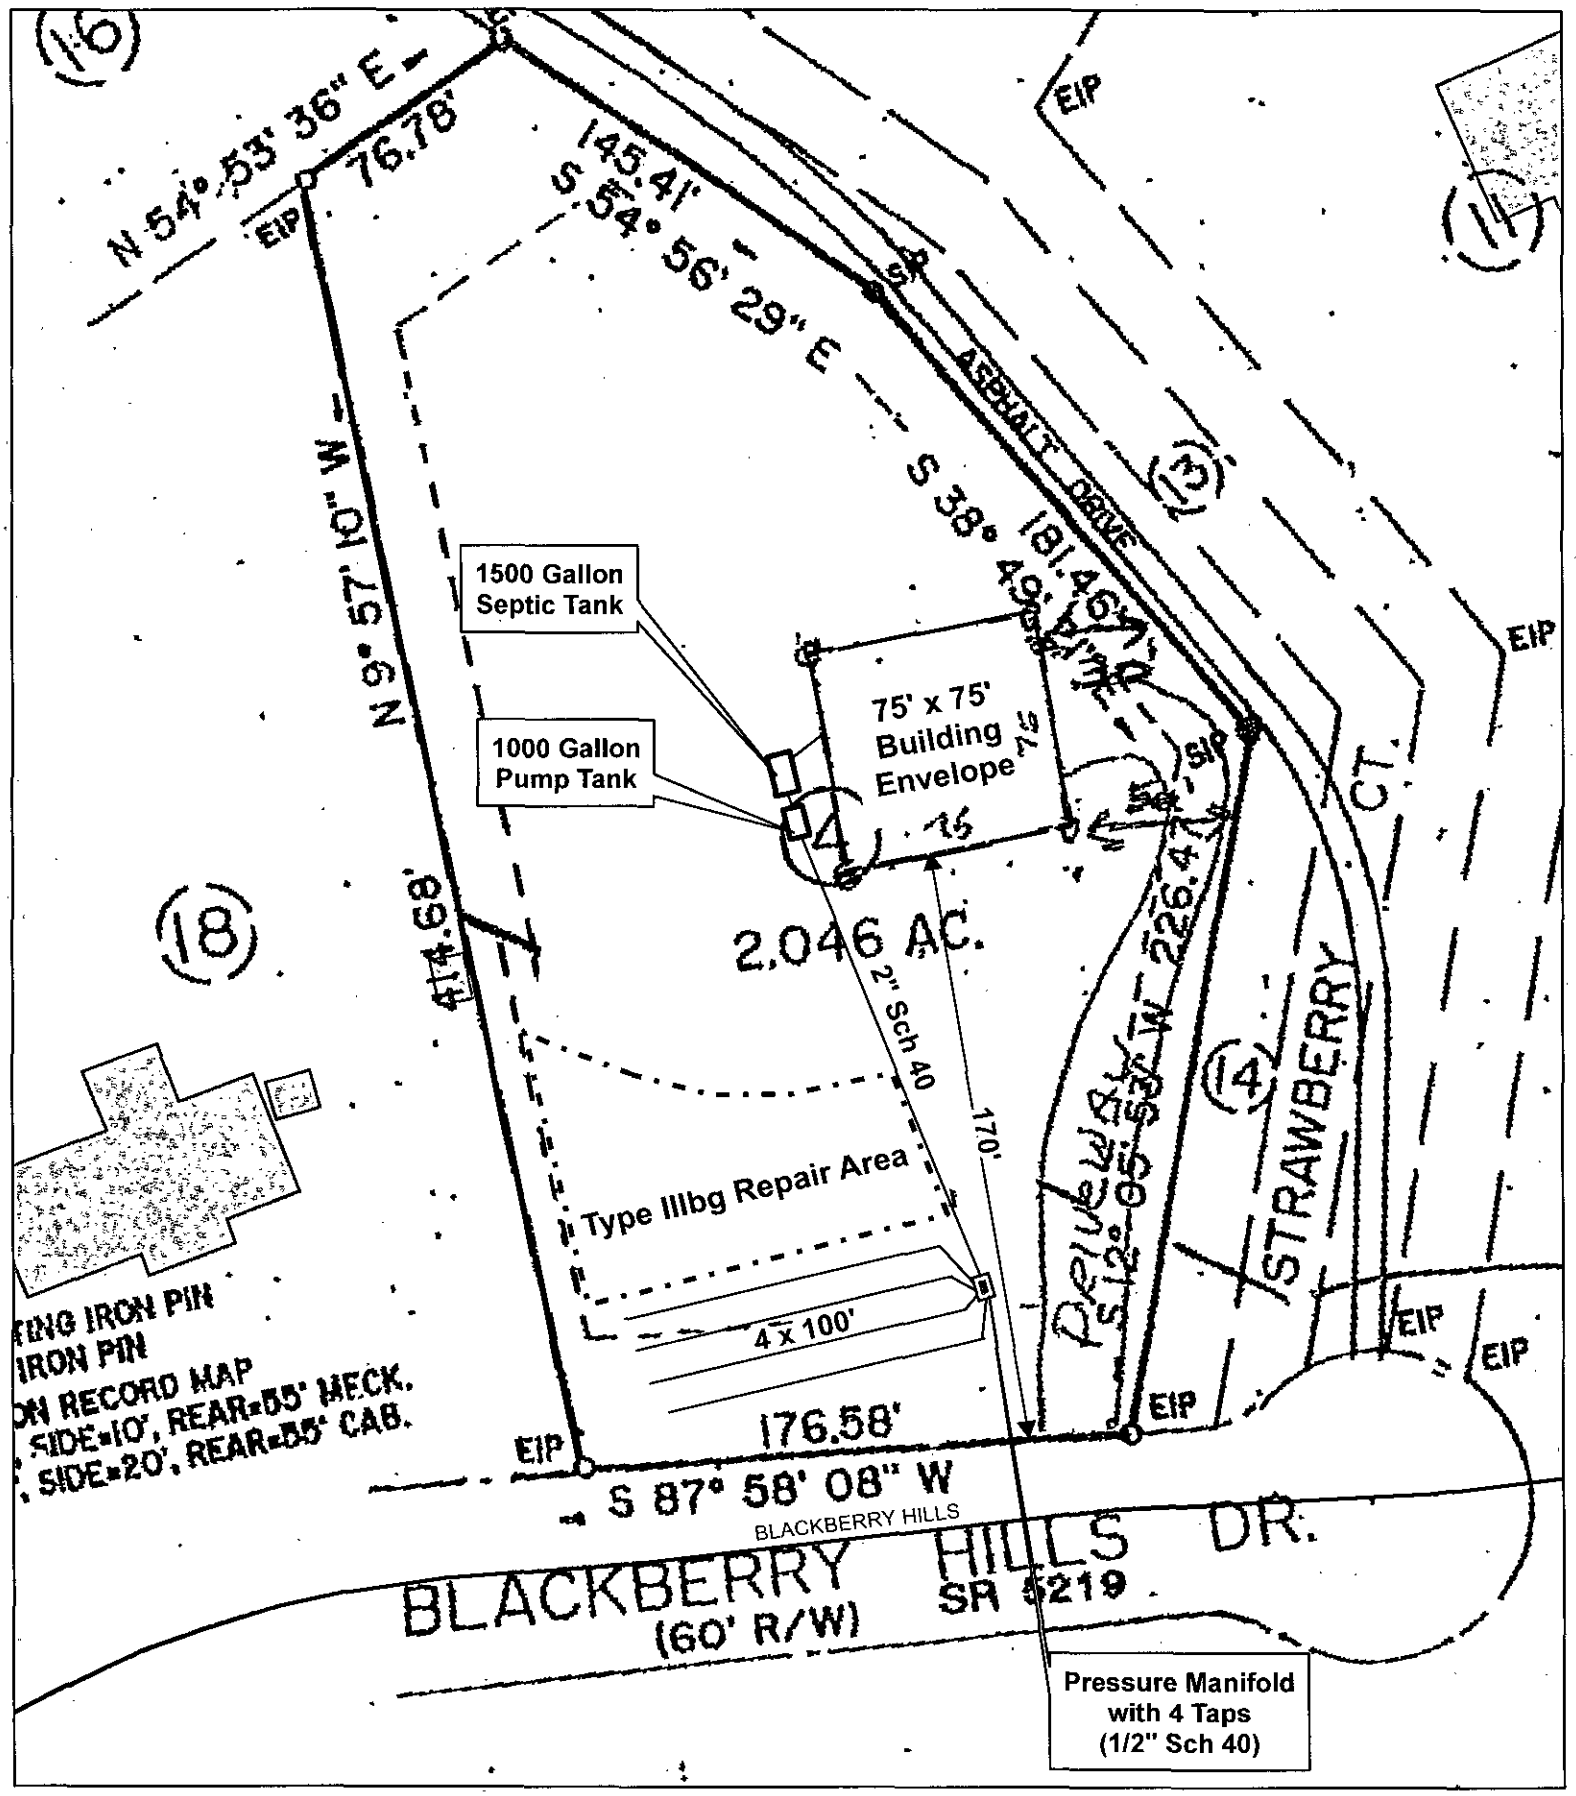

Map Created By: Jacob Presley
Map Created On: 5/8/14

0 30 60 Feet

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St, Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

IMPROVEMENT PERMIT for a RESIDENTIAL ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

Permit #: **30006808** GWS File #: **8932B** Tax Parcel #: **139-173-40**

- This IMPROVEMENT PERMIT is subject to revocation if site plans or the intended use change. There is to be **NO** grading, filling, or disturbance of the soil in the area of the septic tank system or repair area.
- CONSTRUCTION AUTHORIZATION must be obtained prior to receiving a Building Permit. The Construction Authorization is **NOT** transferable. Do not clear, grade, fill or disturb soil prior to obtaining a Construction Authorization.
- Domestic-type wastewater only. No industrial process wastewater may be discharged into the system.

I. This Improvement Permit Shall: Expire in Five (5) Years **Expiration Date (If Applicable):** 5/8/2019

Type of Installation: Residential - New System Lot Number: 4

Structure Type: HOUSE Size (ft^2): 2400 # Bedrooms: 4 # Occupants: 2

Building Foundation: Crawl Space Water Supply: Private Well

II. Initial System Type: Pump to Approved **System Classification:** IIIb

Initial System Specifications:

Design Flow (gpd):	480	LTAR (gpd/ft^2):	0.3	Septic Tank Size (gal):	1500	Pump Tank Size (gal):	1000
Trench Width (ft):	3	Trench Spacing (ft):	9	Absorption Area (ft^2):	1200	Total Trench Length (ft):	400
Maximum Trench Depth (in):	36	Depth of Media (in):	12	Distribution Device:	Pressure Manifold		

III. Repair System Type: Pump to Approved **System Classification:** IIIb

Repair System Specifications:

Design Flow (gpd):	480	LTAR (gpd/ft^2):	0.3	Septic Tank Size (gal):	1500	Pump Tank Size (gal):	1000
Trench Width (ft):	3	Trench Spacing (ft):	9	Absorption Area (ft^2):	1200	Total Trench Length (ft):	400
Maximum Trench Depth (in):	36	Depth of Media (in):	12	Distribution Device:	Pressure Manifold		

IV. Permit Conditions/Comments:

(Please See the Following Page for Permit Conditions.)

The undersigned, an authorized agent of the MECKLENBURG COUNTY HEALTH DEPARTMENT, certifies that the Department is issuing an IMPROVEMENT PERMIT for the above referenced property. This permit is being issued in accordance with the *Laws and Rules For Sewage Treatment, and Disposal Systems* and is subject to the following provisions:

- No work shall be conducted on the septic system until an INSTALLATION APPROVAL is granted by the Department.
- The septic system installer shall be a registered septic contractor with Mecklenburg County Health Department.
- The permitted system shall be installed in accordance with the included PLOT PLAN.
- This IMPROVEMENT PERMIT is transferable.

DENR Authorized Agent: Jacob Presley Owner/Legal Agent: _____
Print Name

Signature: _____ Signature: _____

Date Issued: 5/8/2014

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St, Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

IMPROVEMENT PERMIT for a RESIDENTIAL ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

Permit #: **30006808** GWS File #: **8932B**

IV. Permit Conditions/Comments:

- This type of septic system requires an inspection once every 5 years by our office. The system owner is responsible for any fees, as determined by the Mecklenburg County Board of Commissioners, associated with this inspection.
- All components of the septic system must be installed in accordance with the required setbacks listed on the corresponding plot plan.
- All components of the septic system must be located at least 100 ft. (50 ft. minimum) from all private wells.
- Flow from all gutters and downspouts shall be directed not to discharge water onto or across any part of the septic system.

The undersigned, an authorized agent of the MECKLENBURG COUNTY HEALTH DEPARTMENT, certifies that the Department is issuing an IMPROVEMENT PERMIT for the above referenced property. This permit is being issued in accordance with the *Laws and Rules For Sewage Treatment and Disposal Systems* and is subject to the following provisions:

- No work shall be conducted on the septic system until an INSTALLATION APPROVAL is granted by the Department.
- The septic system installer shall be a registered septic contractor with Mecklenburg County Health Department.
- The permitted system shall be installed in accordance with the included PLOT PLAN.
- This IMPROVEMENT PERMIT is transferable.

DENR Authorized Agent: Jacob Presley


Signature: JAPS

Date Issued: 5/8/2014

Owner/Legal Agent: _____
Print Name

Signature: _____

THIS IS TO CERTIFY THAT ON THE 10 DAY OF September 19 99 I SURVEYED THE PROPERTY SHOWN ON THIS PLAT. AND THAT THE PROPERTY LINES, WALLS AND BUILDINGS ARE AS SHOWN HEREON: THAT THE BUILDINGS LOCATED ON SAID LOT DO NOT ENCROACH OR PROJECT ON ADJACENT STREETS OR PROPERTY; AND THAT NO ADJACENT BUILDINGS OR WALLS ENCROACH OR PROJECT ON SAID PREMISES.




VICINITY MAP

SIGNED Edward R Buckner

Professional Land Surveyor # L-915
3479 Monarch Ct.
Harrisburg, NC 28075

NORTH CAROLINA PROFESSIONAL SEAL L-915 LAND SURVEYOR EDWARD R. BUCKNER

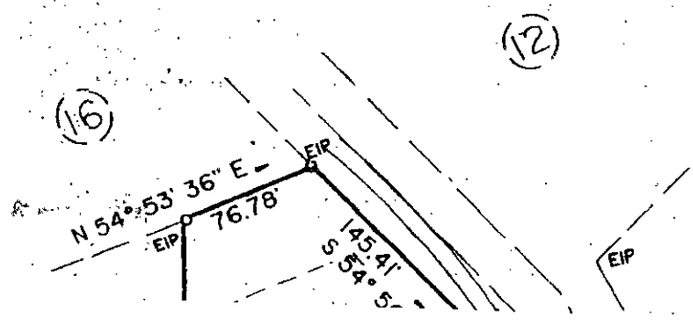

MECKLENBURG COUNTY
Health Department

E. Winters Mabry, MD
Director


(704) 432-3199

Addendum to Application for
New Well or Septic System Installation
Abandonment or Repair of Existing Well or Septic System

Your signature below confirms the following:

1. The information on the application is true, complete and accurate.
2. Authorized county and state officials are granted right of entry to conduct necessary inspections to determine compliances with applicable laws and rules.
3. I acknowledge that BRENDA FARMER is acting as my legal representative (agent) in the submittal of the application for a water supply well or septic permit located at

_____
Number Street Town
(Or Parcel Number)



MECKLENBURG COUNTY
LAND USE AND ENVIRONMENTAL SERVICES
Payment Receipt

Receipt Information

Date:	04/22/14	**Amount:**	250.00
Receipt #:	89235	**Tendered:**	250.00
Check / Auth #:	CHECK 5011	**Returned:**	0.00
Received By:	SADERLW		

Account Information

Account #: 200000
Contractor: ROSSI CYNTHIA & JAY
Attn:
Address: 10720 VICINO CT
Address:
City/State/Zip: MATTHEWS, NC 28105

Item	Description	Permit#	Quantity	Unit Price	Total Price
0701	Improvment Permit App-Residen 16112 BLACKBERRY HILLS DR		1	250.00	250.00

Outstanding Balances

Month-To-Date	Prior Month	30 Days	60 Days	90 Days	Balance
350.00	265.00	1,719.65			
