W

Date Received 9-19-73

MECK COUNTY HEALTH DEPT.
RECEIVED
SEP 13 1973
ENVIRONMENTAL HEALTH DIVISION

APT No. 6989

T. C. No.

Map Date

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

APPLICATION FOR PERCOLATION TEST

1) NAME OF OWNER McKinney (LAST) Mongo (FIRST) Ruder (MIDDLE)

2) ADDRESS OF OWNER 2645 Matthews Indian Trail Rd. ZIP

3) PHONE NO Home 821-8715 Office 525-8110


4) LOCATION OF PROPERTY Matthews Indian Trail Rd. (STREET OR COUNTY ROAD) County Rd. 3453

5) SUBDIVISION LOT NO BLOCK NO

MAP BOOK NO PAGE NO

6) DEED REFERENCE DEED BOOK 3607 PAGE NO 0869

Application is hereby made to the Mecklenburg County Health Department for the conduct of a percolation test and an on site inspection of the lot hereinabove described for the purpose of determining if the lot is suitable for the installation of an individual septic tank wastewater treatment system with subsurface soil absorption, effluent discharge

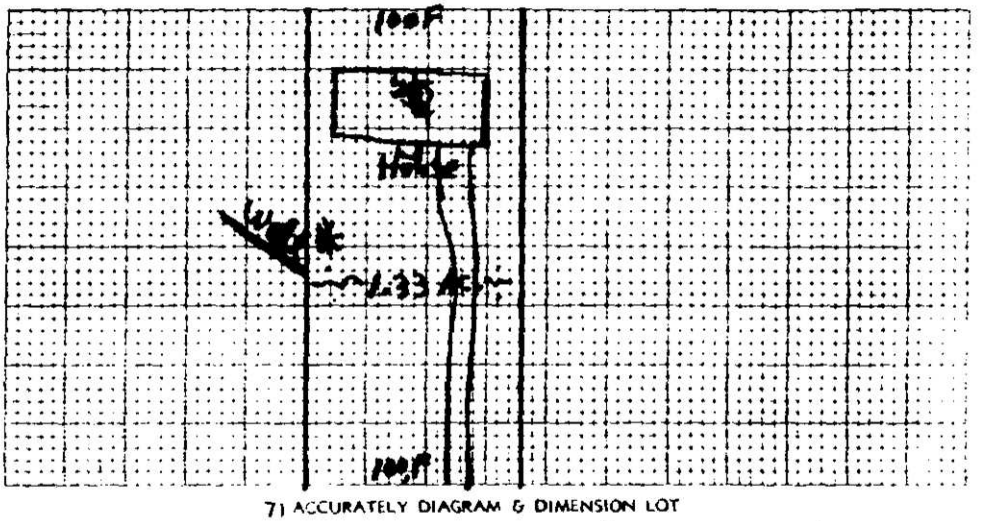

7) ACCURATELY DIAGRAM & DIMENSION LOT

OWNER Mongo R. McKinney Jr.

FORM NO E-1-9-1-72

HEALTH DEPARTMENT'S COPY

MECKLENBURG COUNTY
Department of Public Health

1200 Blythe Boulevard
Charlotte, North Carolina 28203
Telephone 374-2113

Date Issued
1. September 26, 1973 SITE DISAPPROVAL REPORT
2. _____ INDIVIDUAL SEPTIC TANK SYSTEM WITH SUBSURFACE,
3. _____ SOIL ABSORPTION, EFFLUENT DISCHARGE

SDR No. 6989
T.C. No. 215-071-25
4-7-71

NAME OF OWNER McKinney, Alonzo Ruben

ADDRESS OF OWNER 2645 Matthews Indian Trail Rd. ZIP _____

LOCATION OF LOT Matthews Indian Trail Road or County Road3453

The lot described above has been disapproved for the installation of an individual septic tank system with subsurface, soil absorption, effluent discharge due to the following:

FAILURE TO PASS PERCOLATION TEST (60 minutes per inch or less)

	Test No.	Date of Test	Percolation Rate
X	1.	9-25-73	300 min/in
____	2.	_____	_____ min/in
____	3.	_____	_____ min/in

____ ON SITE INSPECTION REVEALED LOT TO BE UNSUITABLE FOR THE FOLLOWING REASON(S) _____

Thomas R. Ward
Environmentalist

(Stencil No.)
EHD 398
8/70

FORM NO.
E-19-8-14-70

MECKLENBURG COUNTY HEALTH DEPARTMENT

INTER-OFFICE COMMUNICATION

DATE: September 26, 1973

TO: Thomas R. Ward
Environmentalist

FROM: W. Everette Lynn, Jr. W.E.L.
Soil Scientist

SUBJECT: APT #6989 (McKinney)
Matthews-Indian Trail Road
9-25-73

Soils were found to be of the Herndon series and shallow silty soils. The perc. test was conducted in the area of shallow silty soils. These soils are shallow to impervious, weathered slate rock. This results in inadequately slow permeability and percolation rate.

The area of Herndon soils is located to the rear of the proposed homesite. These soils have good aeration, good drainage and moderate permeability.

It is recommended that the lot be granted approval for installation of a septic tank system with design based on a 60 min./in. perc. rate. The system should be located in the area of Herndon soils.

WEL:jdg

Serial No. [illegible]

PTR No. 6989

T C No 215-071-25

Date Issued September 26, 1973

Map Date 4-7-71

Do Not Issue A Building Permit Based On This Form

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION


PERCOLATION TEST REPORT

NAME OF OWNER McKinney, Alonzo Ruben
LAST FIRST MIDDLE

ADDRESS OF OWNER 2645 Matthews-Indian Trail Road ZIP

LOCATION OF PROPERTY Matthews Indian Trail Road or County Road 3453
STREET OR COUNTY ROAD

SUBDIVISION LOT NO BLOCK NO

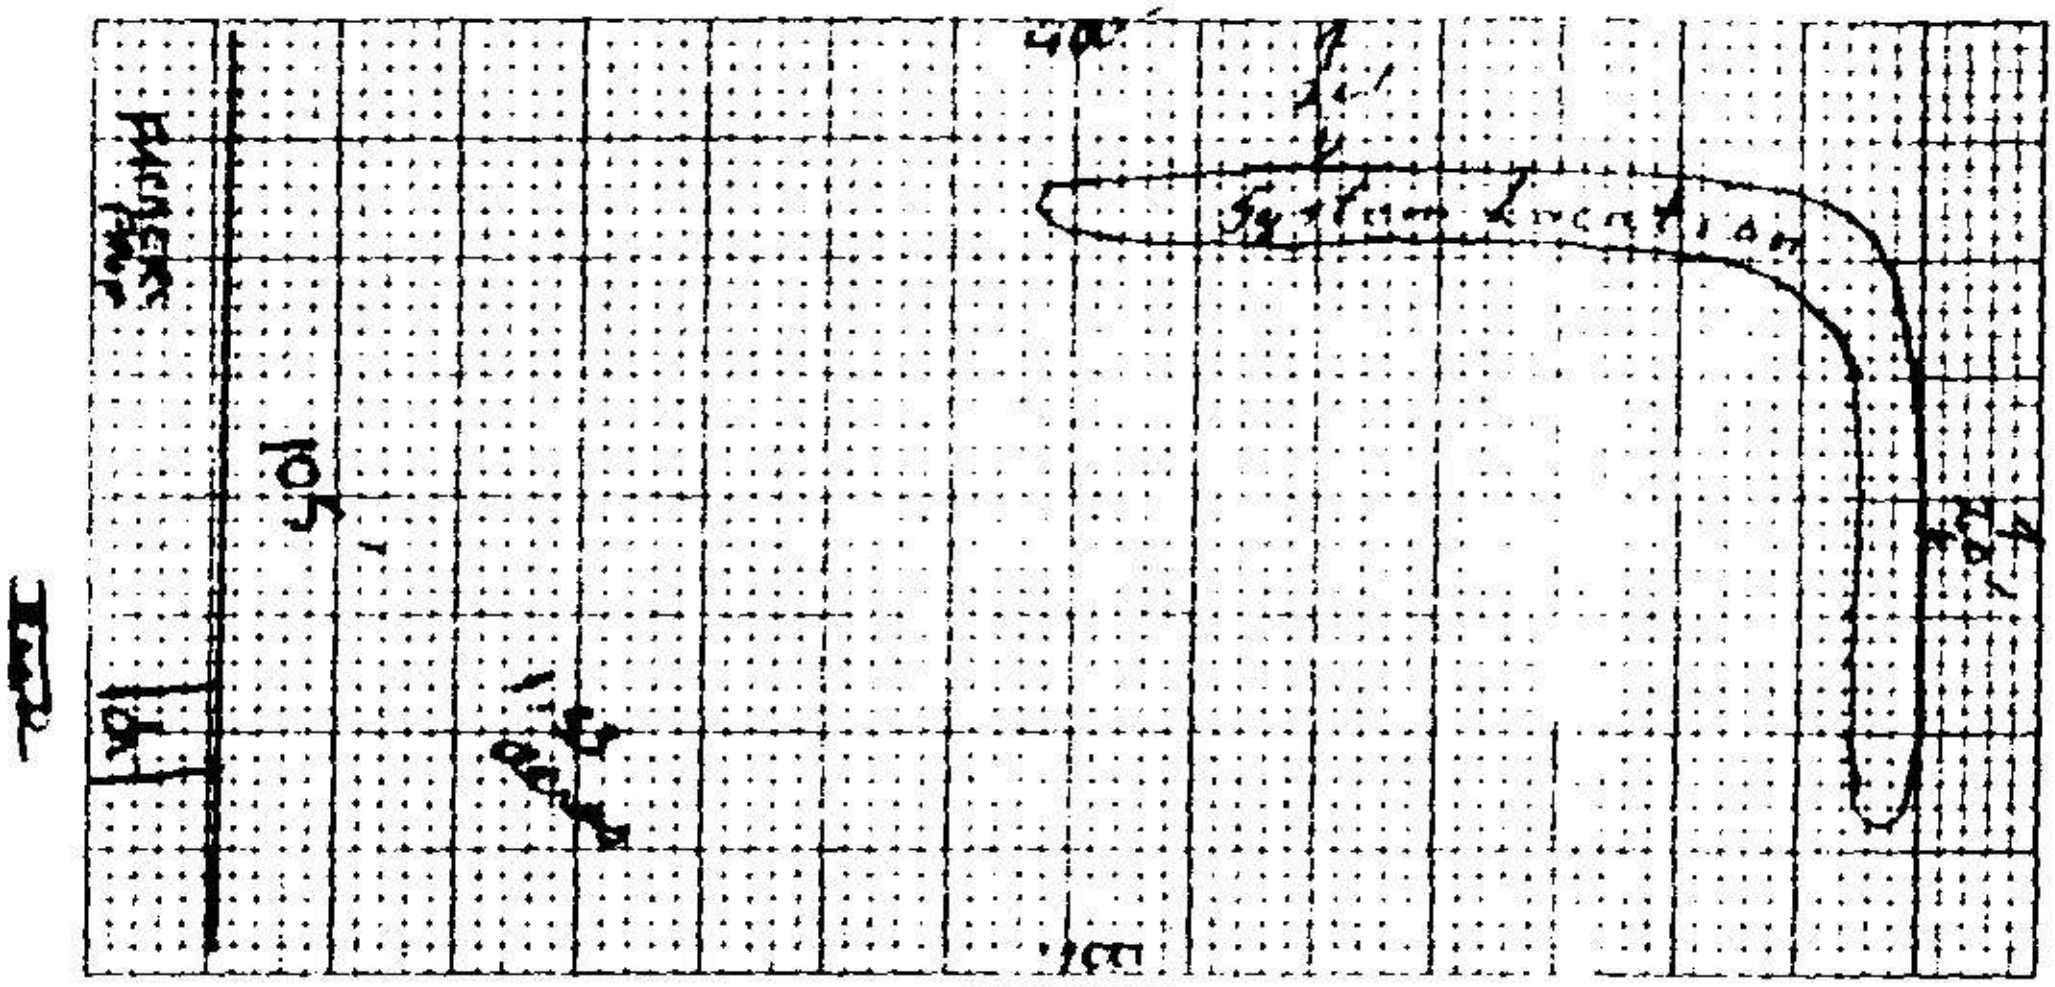

PLOT PLAN

This is to certify that a percolation test has been run and an on site inspection made by the Mecklenburg County Health Department on the lot described above. The said test was conducted on that portion of the lot as indicated on above plot.

The percolation rate determined by the test was [illegible] min/in.* The said lot is approved for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption effluent discharge subject to the following terms and conditions.

1. A permit to install, construct, alter, or repair the specific system shall be obtained from the Mecklenburg County Health Department prior to the beginning of any construction of buildings, or of the wastewater treatment system on the said lot.
2. The size of the septic tank wastewater treatment system which must be installed will be determined by the Health Department prior to installation based on the percolation rate obtained above, and on the size and type of building constructed thereon.
3. This approval is valid only if the system is installed in the immediate area where the percolation test was run.
4. This approval is void if any grading, filling, or construction (including the drilling of a well) is performed on the lot which, in the opinion of the Health Department, renders the area where the percolation test was run unsuitable for the installation, construction, alteration, and/or repair of such a system.

This approval is granted based on the laws of the State of North Carolina and the rules and regulations of the North Carolina State Board of Health and the Mecklenburg County Board of Health which were in effect on the date of issuance and is void if at any time in the future, prior to the completion of the system, these laws, rules, and regulations are changed such that this approval would not have been granted had the new or revised laws, rules, and regulations been in effect on the issue date.

* Results based on soil analysis.

Director, Environmental Health Division or Authorized Section Head

FORM NO E-[illegible]

Soil Scientist

HEALTH DEPARTMENT'S COPY

Date Received 10 3 73

MECK COUNTY HEALTH DEPT
RECEIVED
OCT 03 1973
ENVIRONMENTAL HEALTH DIVISION

ICAR IS Application No 6989

T C No 215-04 2,5


Map Date 4 7 71

MECKLENBURG COUNTY HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION

Application for an
Installation, Construction, Alteration, and/or Repair Permit
Individual Septic Tank System with Subsurface, Soil Absorption, Effluent Discharge

The owner of that property described hereinafter hereby applies to the Mecklenburg County Health Department for a permit to

1 ✓ Install or Construct 2 Alter or Repair an individual septic tank wastewater treatment system with a subsurface soil absorption effluent discharge

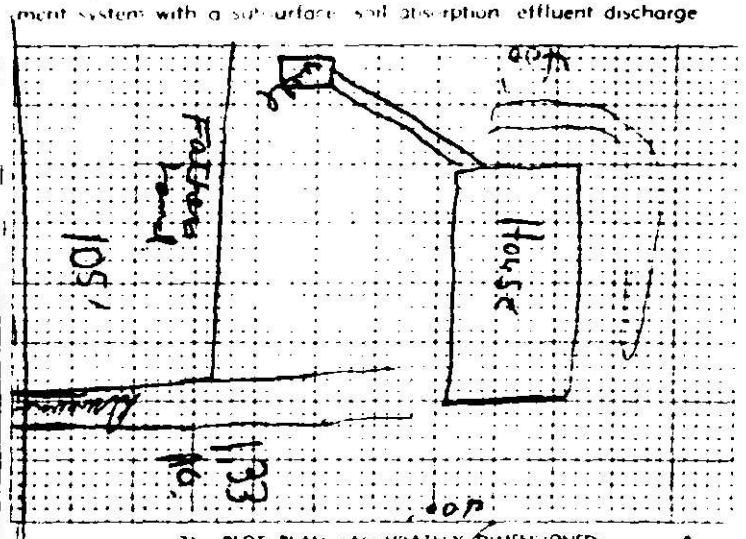

4 No. of Bedrooms 3

5 Estimated Daily Max. No. Employees

6 Washing Machine ✓ Yes No

7 Garbage Disp. Yes ✓ No

8 Dishwasher Yes ✓ No

9 Water supply:
A Individual Well ✓
B Community System
C Municipality
1 Well
2 Connection

10 Type Sewage System
If public sewer, Yes ✓ No
Public sewer available? Yes No

11 FHA Case No.

12 VA Case No.

13) PLOT PLAN (ACCURATELY DIMENSIONED)

13) NAME OF OWNER McKinney (LAST) Glenn Ruben (FIRST) (MIDDLE)

14) ADDRESS OF OWNER 2645 Matthews Indian Trail Rd., Matthews N.C.

15) PHONE NO Home 821-8715 Office [redacted] 525-8110

16) LOCATION OF SYSTEM Matthews Indian Trail Rd (or County Rd. 3453) (STREET OR COUNTY ROAD)

17) SUBDIVISION ____ Lot No ____ Block No ____

Map Book No [redacted] Page No [redacted]

18) DEED REFERENCE — DEED BOOK 3607 AT PAGE 0869

19) HAS A PERCOLATION TEST BEEN RUN? ____ YES ____ NO DATE RUN 7/23/73

20) PTR NUMBER (See Instructions) [illegible]

The undersigned person hereby agrees that he has read the foregoing application and that the contents of same are true. It is understood that any permit applied for herein shall be void and of no effect if any of the above facts are not true

DATE OF APPLICATION

OWNER Glenn Ruben McKinney

E-4-9-1-72

HEALTH DEPARTMENT'S COPY

Date Issued October 3, 1973

Serial No. 3487

IMPROVEMENTS PERMIT

LA No. 6989

T. C. No 215-071-25

Map Date 4-7-71

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

TO THE BUILDING INSPECTION DEPARTMENT

APPROVAL OF LOT FOR INSTALLATION OF AN INDIVIDUAL SEPTIC TANK WITH SUBSURFACE, SOIL ABSORPTION, EFFLUENT DISCHARGE

NAME OF OWNER McKinney (LAST) Alonzo (FIRST) Ruben (MIDDLE)

ADDRESS OF OWNER 2645 Matthews-Indian Trail Road ZIP 28105

LOCATION OF LOT Matthews Indian Trail Road or County Road 3453 (STREET OR COUNTY ROAD)

SUBDIVISION _____ LOT NO _____ BLOCK NO. _____

MAP BOOK NO _____ PAGE NO _____

The above specified lot is approved by the Mecklenburg County Health Department for the installation of an individual septic tank system with subsurface, soil absorption, effluent discharge based on the percolation test results which yielded a percolation rate of 60 min/in on an on site inspection of the said lot, and upon the information supplied in the "Application for an Installation, Construction, Alteration, and/or Repair Permit", number 6989. This approval is subject to the following terms and conditions.

1. That the nitrification field be installed, constructed, altered, and/or repaired in the same area where the percolation test was run.
2. That an "Installation, Construction, Alteration, and/or Repair Permit" be issued and in full force and effect when the system is installed, constructed, altred, and/or repaired and that the system be installed in accordance with same

This approval may be revoked and the building inspection department requested to revoke any building permit(s) which have been issued to authorize construction on the said lot if at any time it is determined that any information contained in the "Application for an Installation, Construction, Alteration, and/or Repair Permit" is not correct or is untrue or that the septic tank system is not being installed, constructed, altered and/or repaired in accordance with a valid Installation, Construction, Alteration, and/or Repair Permit

Thomas R. Ward
Environmentalist

John R. Robertson
Director Environmental Health Division or Authorized Section Head

FORM NO E-3-4-1-71

HEALTH DEPARTMENT'S COPY

Serial No. 5115 ICAR(S) Permit No. 6989

Date Issued 17 Apr 74

T C No 215 C11 25

Map Date 9 Apr 71


MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

INSTALLATION, CONSTUCTION, ALTERATION, AND/OR REPAIR PERMIT

(Individual Septic Tank System with Subsurface, Soil Absorption, Effluent Discharge)

Permission is hereby given to ✓ Install or Construct ___ Alter or Repair the individual septic tank waste water treatment system with absorption field absorption effluent discharge as requested herein at the described location. This permit is granted based upon the information supplied on application 6989 dated 3 Oct 73 and this permit shall be void and of no effect if the information provided in the application is not complied with. All work shall be completed on or before 17 May 74 after which date this permit shall be null and void.

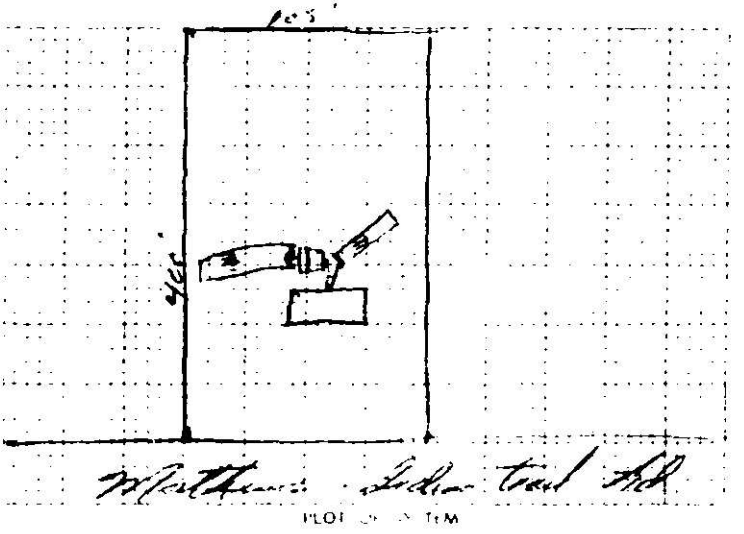

PLOT PLAN

Percolation Rate 60

Liquid Capacity of Tank 1000

Tank Construction PC

Absorption and/or Nitrification Lines

Total Line Length 420' (150 lin ft + 3(75 lin ft))

Number of Lines 6 (3 @ 70' ea)

Distance from Water 10

Distance from Property Lines 15'

Distance from Well

NAME OF OWNER Mr. Henry Pharis Parker

LOCATION OF PROPERTY Matthews - Indian Trail Rd. (Co Rd 3413)

This system must meet all requirements as set forth in the regulations of the Mecklenburg County Board of Health in effect on the date of the granting of this permit. A certificate of approval must be issued by the Health Director before any system can be covered up or otherwise rendered inspectable. It can be used

Comments Staple (Carter)

Director of Environmental Health

Environmentalist W. H. Lusby

If the permit is for the installation or construction of a new system it must be signed by the division head of Environmental Health Division in order to be valid. Only the signature of the Environmentalist is necessary where an existing system is being altered or repaired.

Form E-5-9-1-72

Serial 4710

C of A (s) No. 6989

Date Issued 23 Apr 74

T C No. 215-071-25

Map Date 7 Apr 71

CERTIFICATE OF COMPLETION

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

CERTIFICATE OF APPROVAL

(Individual Septic Tank System with Subsurface, Soil Absorption, Effluent Discharge)

Name of Owner McKinney (LAST) Otango (FIRST) Baker (MIDDLE)

Location of Property Matthews-Indian Trail Rd. (Coll 3453)

Application Number 6989 Permit Number 6989

Inspection Data:

Liquid Capacity of Tank 1000 Tank Material P.C. (7'6" x 3'0" x 3'7")

Total Length of Drain Tile 40'+150'+150' Number of Lines 3 (3' x 60' x 12")

Depth of Filter Material 12" Cover Depth 18"

Water Supply Source Ind. Well Distance from Water Source 150'+

Excavation Inspected 23 Apr 74 (DATE) Tank Inspected 23 Apr 74 (DATE)

Nitrification Field Inspected 23 Apr 74 (DATE)

Washing Machine Line Inspected, If Applicable 23 Apr 74 (DATE)

The undersigned has inspected the Individual Septic Tank System with subsurface, soil absorption, effluent discharge as described above and it has been ✓ installed or constructed, altered or repaired in accordance with the permit issued and the regulations of the Mecklenburg County Board of Health in effect on the date of issuance of the permit. The issuance of this Certificate of Approval does not in any way guarantee that the system will operate properly or relieve any person now or hereafter owning, controlling, or using such system from any liability resulting from the failure of the system to operate properly. This Certificate of Approval is issued subject to those restrictions and conditions shown on the permit(s) in addition to those listed below under comments. This Certificate of Approval shall be null and void if any information contained in the application is untrue or if any additions are made to the property which would increase the requirements for said system.

Comments Staple (Tank)

Environmentalist

FORM NO E-6-4-1-71

HEALTH DEPARTMENT'S COPY
