Groundwater & Wastewater Services: Septic Project File & D

Edit Response | Delete Response | Manage Permissions | Workflows | Alert Me

GWS File #:	14962
WASPS App #:	8514
Primary ES assigned to project:	April Bumgarner
Secondary ES assigned to project:	
Project Type:	Modified Plot Plan
Site Evaluation Information: .1939(a)(1) - Topography and Landscape Position Recorded?	Yes
Site Evaluation Information: .1940(a-g) - Slope % Recorded?	Yes
Site Evaluation Information: .1939(a)(2) - Texture Class Recorded?	Yes
Site Evaluation Information: .1939(a)(2) - Structure Type Recorded?	Yes
Site Evaluation Information: .1939 (a)(2) - Consistence Recorded?	Yes
Site Evaluation Information: .1939(a)(2) - Mineralogy Recorded?	Yes
Site Evaluation Information: .1939(a)(3) - Soil Wetness Condition Recorded?	Yes
Site Evaluation Information: .1939(a)(4) - Soil Depth to Rock or Parent Material Recorded when Encountered?	Yes
Site Evaluation Information: .1939(a)(5) - Depth to Restrictive Horizons Recorded when Encountered?	N/A
Site Evaluation Information: .1939(a)(6) - Sufficient Available Space Recorded?	Yes
Site Evaluation Information: .1937(m) - Are the Profile Locations Shown?	Yes
Site Evaluation Information: .1939(a) - Are the S/PS Profiles in system & in repair area?	Yes
Site Evaluation Information: .1939(d), .1955, .1956, .1957 - LTAR	Yes
Improvement Permit/Construction Authorization: .1937(g), 130A-336(a) - Proposed System Type stated - Initial	Yes
Improvement Permit/Construction Authorization: .1945(b) - Proposed System Type stated - Repair	N/A
Improvement Permit/Construction Authorization: 130A-336(a)(3) - System location identifiable by setbacks - Initial	Yes
Improvement Permit/Construction Authorization: .1937(g), .1945(b) - System components shown - Initial	Yes
Information Permit/Construction Authorization: .1945(b) - Repair area shown	N/A
Improvement Permit/Construction Authorization: .1937(f)(g) - Does System design match facility, flow & WW characteristics?	Yes
Improvement Permit/Construction Authorization: .1937(f)(g) - Is System design consistent with soil/site conditions?	Yes
Improvement Permit/Construction Authorization: .1937(f)(g) - Is the System located in the approved area?	Yes
Improvement Permit/Construction Authorization: 130A-336(a) - Number of Bedrooms, employees, seats, etc. indicated?	Yes
Improvement Permit/Construction Authorization: .1937 (g) - Trench depth correct?	Yes
Improvement Permit/Construction Authorization: .1937(g) - Trench width correct?	Yes
Improvement Permit/Construction Authorization: .19379(g) - Trench length correct?	Yes
Improvement Permit/Construction Authorization: 130A-336(a)(1) - Proposed/existing well shown?	N/A

Improvement Permit/Construction Authorization: 130A-336(a)(1) - Property line lengths shown?	No
Improvement Permit/Construction Authorization: 130A-336(a) - Facility/appurtenance setbacks shown from fixed points?	Yes
Corrections/modifications needed?	Yes
Comments:	Insert property line lengths and house pad dimensions.
IA issued date:	
OP Issued date:	
Review performed by:	11/8/18 Jeremy Michael
Date performed:	11/2/2016

Created at 11/2/2016 9:00 AM by Michael, Jeremy
Last modified at 11/2/2016 9:00 AM by Michael, Jeremy

Close

APP 8514 File # 14962

20 SEP '16 PM 4:25

MECKLENBURG COUNTY
HEALTH DEPARTMENT

APPLICATION FOR A RESIDENTIAL SITE IMPROVEMENT PERMIT/ CONSTRUCTION AUTHORIZATION FOR AN ON-SITE WASTEWATER SYSTEM, NEW WELL INSTALLATION, OR REPAIR OF EXISTING WELL

1. SEPTIC / TYPE APPLICATION: ○ N/A ○ NEW SYSTEM ○ ALTERATION ○ REPAIR ◉ MODIFIED PLOT PLAN

2. WELL / TYPE APPLICATION: ◉ N/A ○ NEW WELL ○ MAJOR REPAIR ○ ABANDONMENT

3. JOB LOCATION INFORMATION:
TAX PARCEL NUMBER: 139-051-18
STREET ADDRESS: 8842 Glencroft Rd.
CITY: Mint Hill
STATE: NC ZIP: 28227
SUBDIVISION NAME: Glen Croft
LOT #: 11 LOT SIZE (acres): .160
TOWNSHIP:
◉ MECKLENBURG ○ CORNELIUS ○ HUNTERSVILLE
○ DAVIDSON ○ CHARLOTTE ○ PINEVILLE
○ MATTHEWS ○ MINT HILL

4. BUILDING INFORMATION:
BUILDING TYPE:
○ SINGLE MOBILE HOME ○ MODULAR HOME
○ DOUBLE WIDE ○ MULTIPLE FAMILY
◉ HOUSE ○ OTHER
HEATED SQUARE FOOTAGE: 1950
NUMBER OF BEDROOMS: 3
NUMBER OF OCCUPANTS: 6
FOUNDATION TYPE:
○ CONCRETE SLAB ○ BASEMENT WITH PLUMBING
◉ CRAWL SPACE ○ BASEMENT WITH NO PLUMBING

5. IF PLANNING TO EXPAND OR ALTER THE EXISTING SEPTIC SYSTEM PLEASE COMPLETE THE FOLLOWING SECTION: ☐ N/A
We want to move septic tank in front of house
NUMBER OF BEDROOMS TO BE ADDED: _____ NUMBER OF ADDITIONAL OCCUPANTS IN THE RESIDENCE: _____

6. WATER SUPPLY: ◉ MUNICIPAL ○ PRIVATE WELL ○ PUBLIC WELL ○ SHARED WELL ○ OTHER _____

7. PROPOSED USE OF WELL: ◉ N/A ○ IRRIGATION ○ POTABLE (DRINKING WATER) ○ OTHER _____

8. PLEASE INDICATE AND RANK DESIRED SEPTIC SYSTEM TYPE(S) IN ORDER OF PREFERENCE *(1-MOST DESIRED 5-LEAST DESIRED)*:
☐ N/A ☑ ANY TYPE ☐ CONVENTIONAL 1 ACCEPTED ☑ INNOVATIVE ☑ ALTERNATIVE ☐ OTHER _____

8A. RANK: 2 1 3 4 ___

9. DO ANY OF THE FOLLOWING APPLY TO THE PROPERTY IN QUESTION? IF "YES" PLEASE ATTACH SUPPORTING DOCUMENTATION.

BURIED CABLES, LANDFILLS, STUMPHOLES	○ YES ◉ NO	GRADING/SOIL REMOVAL PERFORMED	○ YES ◉ NO
EXISTING WASTEWATER (SEPTIC) SYSTEMS	○ YES ◉ NO	JURISDICTIONAL WETLANDS	○ YES ◉ NO
WELLS, SPRINGS, OR WATER LINES	○ YES ◉ NO	APPROVAL REQUIRED BY ANY OTHER PUBLIC AGENCY	○ YES ◉ NO
EASEMENTS OR RIGHT-OF-WAYS	○ YES ◉ NO	WASTEWATER OTHER THAN DOMESTIC SEWAGE	○ YES ◉ NO
CHEMICAL/PETROLEUM STORAGE TANKS	○ YES ◉ NO	KNOWN UNDERGROUND CONTAMINATION	○ YES ◉ NO
WASTE STORAGE	○ YES ◉ NO	GROUNDWATER USE RESTRICTIONS/VARIANCES	○ YES ◉ NO

10. WHAT DATE WAS THE PROPERTY ORIGINALLY DEEDED AND RECORDED? _____ ☑ UNKNOWN

11. WHAT IS THE ANTICIPATED CLOSING DATE FOR THIS PROPERTY? 4-20-17 ☐ N/A

12. PROPERTY OWNER:
NAME: Katherine & Johnny Whitley
ADDRESS: 8019 Walnut Breeze Lane
CITY: Charlotte
STATE: NC ZIP: 28227
WORK PHONE: 980-329-1465
MOBILE PHONE: 704-622-2703
FAX: _____
E-MAIL: Kannwhitley@gmail.com
johnny1whitley@yahoo.com

13. OWNER'S LEGAL REPRESENTATIVE, IF APPLICABLE:
NAME: _____
ADDRESS: _____
CITY: _____
STATE: ____ ZIP: _____
WORK PHONE: _____
MOBILE PHONE: _____
FAX: _____
E-MAIL: _____

1-800-426-2781 x4641

14. SEPTIC SYSTEM PERMIT APPLICATION:

If the information in this application is falsified, changed, or the site is altered, then the Improvement Permit and Authorization to Construct shall become invalid. I have read this application and certify that the information provided herein is true, complete and correct. Authorized county and state officials are granted right of entry to conduct necessary inspections to determine compliance with applicable laws and rules. I understand that I am solely responsible for the proper identification and labeling of all property lines and corners and making the site accessible so that a complete site evaluation can be performed. The permit is valid for either sixty (60) months or is non-expiring depending upon the documentation submitted: complete site plan = 60 months, complete plat = non-expiring.

KW JW (Initial here for septic system applications)

15. WELL PERMIT APPLICATION:

If the information in this application is falsified, changed, or the site is altered, then the Well Permit shall become invalid. I have read this application and certify that the information provided herein is true, complete and correct. Authorized county and state officials are granted right of entry to conduct necessary inspections to determine compliance with applicable laws and rules. I understand that I am solely responsible for the proper identification and labeling of all property lines and corners and making the site accessible so that a complete site evaluation can be performed. The permit is valid for a period of twelve (12) months from the date of issuance.

_____ (Initial here for well applications)

16. APPLICATION SIGNATURE SECTION:

ONLY COMPLETE APPLICATIONS WILL BE PROCESSED. A proper signature is required in order to process your application. Please review the application carefully and sign in the space provided below. A PROPOSED PLOT PLAN is required to be submitted with each application.

Kathryn A. White 9-20-2016

Property Owner's or Owner's Legal Representative Signature — Date

John A. White

OFFICE USE ONLY

○ SURVEY PLAT TO SCALE SUBMITTED ○ SCALED SITE PLAN SUBMITTED ○ UN-SCALED SITE PLAN SUBMITTED

SEPTIC APPLICATION FEE RECEIVED: $ _____ DATE FEE RECEIVED: _____

WELL APPLICATION FEE RECEIVED: $ _____ DATE FEE RECEIVED: _____

APPLICATION PROCESSED BY: _____

GWS FILE NUMBER ASSIGNED: _____

APPLICATION ID NUMBER ASSIGNED: _____

COMMENTS:

MECKLENBURG COUNTY – GROUNDWATER & WASTEWATER SERVICES
700 N. TRYON ST. SUITE 211 CHARLOTTE, NC 28202, OFFICE: 704-336-5103, FAX: 704-336-6894


File #: _____

PROPOSED PLOT PLAN

A drawing showing the locations of the following items is required: existing and proposed property lines with dimensions, easements or right-of-ways, proposed building pad(s) or existing building footprint(s), all appurtenances (garage, driveway, deck, pool, etc.), location of existing or proposed well(s), location of existing or proposed sewer lines and sewage disposal systems, surface water bodies, and any aboveground or underground storage tanks. Provide names for all roads that adjoin the property.

Street Address: 8842 Glencroft Rd Tax Parcel #: 139-051-18

Subdivision Name: Glen Croft Lot #: 11



see Attached train

Property Owner's or Owner's Legal Representative Signature

9-20-2016
Date

MECKLENBURG COUNTY – GROUNDWATER & WASTEWATER SERVICES
700 N. TRYON ST. SUITE 211 CHARLOTTE, NC 28202, OFFICE: 704-336-5103, FAX: 704-336-6894

Revised on: 12/15/10

Department of Environment, Health, and Natural Resources
Division of Environmental Health
On-site Wastewater Section

Sheet: 1 of 2
Property ID: 139-051-18
Lot #: 11
File #: 14962
AppID: 8514

SOIL/SITE EVALUATION
for ON-SITE WASTEWATER SYSTEM

Owner: Katherine & John Whitley
Address: 8019 Walnut Creek Ln, Charlotte, NC 28227
Proposed Facility: 3BR House
Design Flow (.1949): 360 GPD
Location of Site: 8842 Glencroft Rd, Mint Hill, NC 28227
Water Supply: [ ] Public [ ] Individual [ ] Well [ ] Spring [X] Municipal
Evaluation Method: [X] Auger Boring [ ] Pit [ ] Cut
Type of Wastewater: [X] Sewage [ ] Industrial Process [ ] Mixed

Applicant: owner
Date Evaluated: 10/4/2016
Property Size: 0.6 ac
Property Recorded: Unknown

PROFILE #	.1940 Landscape Position/ Slope%	Horizon Depth (IN.)	SOIL MORPHOLOGY .1941 .1941 Structure/ Texture	.1941 Consistence Mineralogy	b PROFILE FACTORS .1942 Soil Wetness/ Color	.1943 Soil Depth (IN.)	.1956 Sapro Class	.1944 Restr Horiz	General Comments	Profile Class & LTAR	Maximum Trench Bottom Depth for 3' Wide Conventional Trench
Boring #1	LS 3%	0 - 14	sbk SCL	SS SP FR SEXP	>48"	48	NA	NA		PS IV 0.275	35"
		14 - 45	sbk C	S P FR SEXP							
		45 - 48	sbk CL	SS SP FR SEXP							
Boring #2	LS 3%	0 - 8	sbk SCL	SS SP FR SEXP	>45"	45	NA	NA		PS IV 0.275	32"
		8 - 39	sbk C	S P FR SEXP							
		39 - 45	sbk CL	SS SP FR SEXP							
		45	Saprolite								
Boring #3	LS 9%	0 - 6	sbk CL	SS SP FR SEXP	>48"	48	NA	NA		PS IV 0.275	33"
		6 - 43	sbk C	S P FR SEXP							
		43 - 48	sbk CL	SS SP FR SEXP							

Description	Initial System	Repair System
Available Space (.1945)	PS	
System Type(s)	IIIb	
Site LTAR (gpd/sq ft)	0.275	Repair Exempt?


Other Factors (.1946): NA
Soil Evaluation By: Jacob Presley, LSS, REHS
Others Present:
Site Classification (.1948): PS
Site Evaluation By: April Bumgarner, REHS
Others Present:

COMMENTS:

Landscape Position	Group	Texture	.1955 LTAR	Structure
R-Ridge	I	S-Sand	1.2 - 0.8	sg-Single Grain
SS-Shoulder Slope		LS-Loamy Sand		mass-Massive
LS-Linear Slope				cr-Crumb
FS-Foot Slope	II	SL-Sandy Loam	0.8 - 0.6	gr-Granular
NS-Nose Slope		L-Loam		sbk-Subangular Blocky
HS-Head Slope				abk-Angular Blocky
CC-Concave Slope	III	Si-Silt	0.6 - 0.3	pl-Platy
CV-Convex Slope		SiCL-Silty Clay Loam		pr-Prismatic
T-Terrace				Sap-Saprolite
FP-Flood Plain		CL-Clay Loam		**Structure Prefixes**
D-Drainage Way		SCL-Sandy Clay Loam		w-weak
				m-moderate
		SiL-Silt Loam		s-strong
				f-fine
	IV	SC-Sandy Clay	0.4 - 0.1	m-medium
		SiC-Silty Clay		c-coarse
		C-Clay		

Consistence Moist	Consistence Wet	Mineralogy
VFR-Very Friable	SS-Slightly Sticky	SEXP-Slightly Expansive
FR-Friable	S-Sticky	EXP-Expansive
FI-Firm	VS-Very Sticky	
VFI-Very Firm	NP-Non-Plastic	**Classification**
EFI-Extremely Firm	SP-Slightly Plastic	US-Unsuitable
	P-Plastic	PS-Provisionally Suitable
	VP-Very Plastic	S-Suitable
		NA-Not Applicable

Sketch of Soil Evaluation Locations

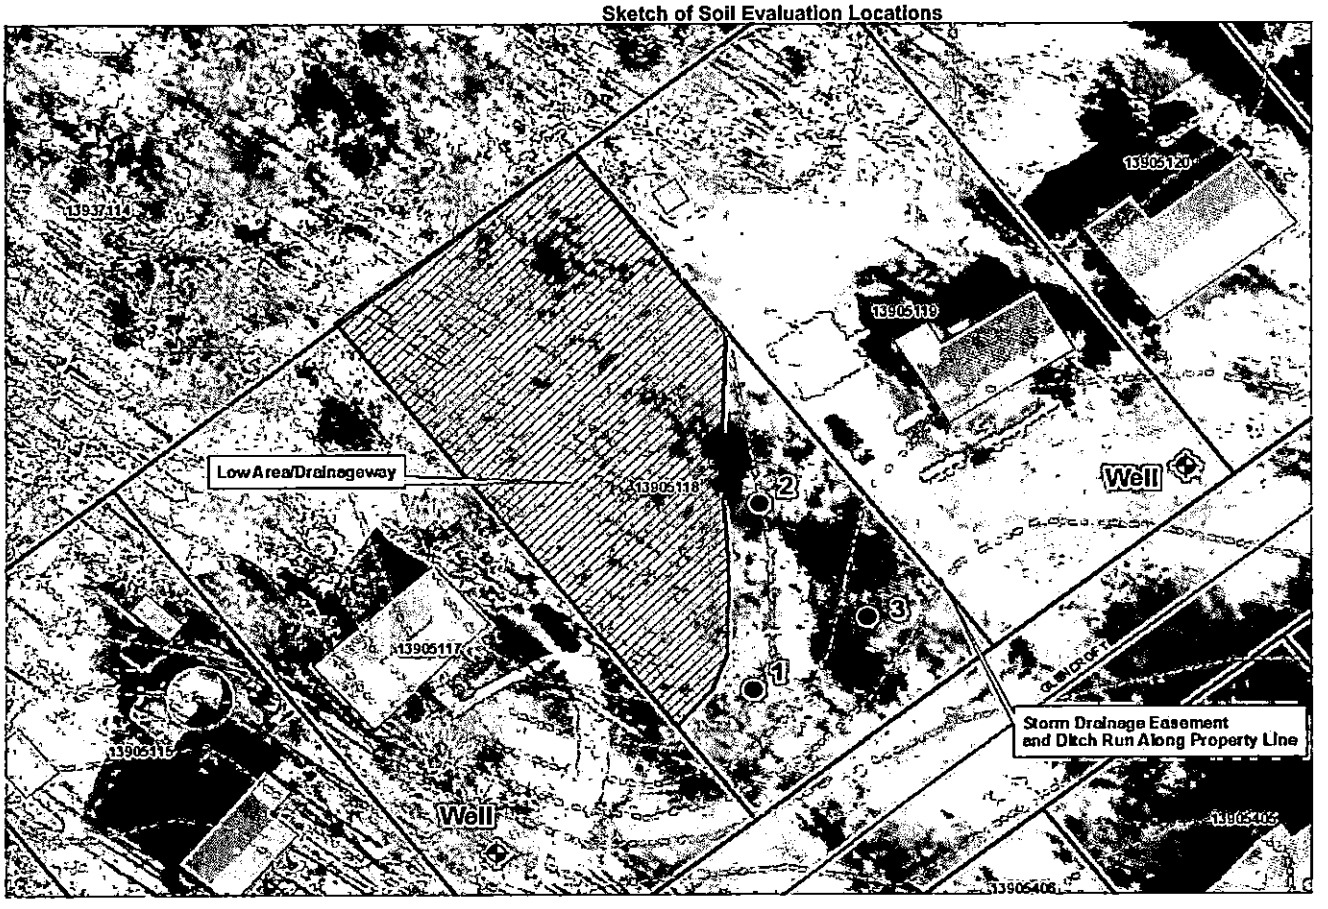

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St, Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

IMPROVEMENT PERMIT for a RESIDENTIAL ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

Permit #: 30008514 GWS File #: 14962 Tax Parcel #: 139-051-18

- This IMPROVEMENT PERMIT is subject to revocation if site plans or the intended use change. There is to be NO grading, filling, or disturbance of the soil in the area of the septic tank system or repair area.
- CONSTRUCTION AUTHORIZATION must be obtained prior to receiving a Building Permit. The Construction Authorization is NOT transferable. Do not clear, grade, fill or disturb soil prior to obtaining a Construction Authorization.
- Domestic-type wastewater only. No industrial process wastewater may be discharged into the system.

I. This Improvement Permit Shall: Expire In Five (5) Years **Expiration Date (If Applicable):** 10/31/2021

Type of Installation: Residential - Modified Plot Plan Lot Number: 0

Structure Type: HOUSE Size (ft^2): 1950 # Bedrooms: 3 # Occupants: 6

Building Foundation: Water Supply: Municipal

II. Initial System Type: Pump to Accepted **System Classification:** IIIb

Initial System Specifications:

Design Flow (gpd): 360 LTAR (gpd/ft^2): 0.275 Septic Tank Size (gal): 1000 Pump Tank Size (gal): 1000

Trench Width (ft): 3 Trench Spacing (ft): 9 Absorption Area (ft^2): 982 Total Trench Length (ft): 327

Maximum Trench Depth (in): 24 Depth of Media (in): 12 Distribution Device: Pressure Manifold

III. Repair System Type: N/A **System Classification:**

Repair System Specifications:

Design Flow (gpd): 0 LTAR (gpd/ft^2): 0.0 Septic Tank Size (gal): 0 Pump Tank Size (gal): 0

Trench Width (ft): 0 Trench Spacing (ft): 0 Absorption Area (ft^2): 0 Total Trench Length (ft): 0

Maximum Trench Depth (in): 0 Depth of Media (in): 0 Distribution Device: N/A

IV. Permit Conditions/Comments:

(Please See the Following Page for Permit Conditions.)

The undersigned, an authorized agent of the STATE OF NORTH CAROLINA, certifies that the Department is issuing an IMPROVEMENT PERMIT for the above referenced property. This permit is being issued in accordance with the *Laws and Rules For Sewage Treatment, and Disposal Systems* and is subject to the following provisions:

- No work shall be conducted on the septic system until a Pre-Construction meeting has been completed by the Department.
- The septic system installer shall be a licensed septic contractor with the North Carolina Wastewater Contractor Inspector Certification Board.
- The permitted system shall be installed in accordance with the included PLOT PLAN.
- This IMPROVEMENT PERMIT is transferable.

Authorized Agent: April Bumgarner Owner/Legal Agent: Katherine A Whitley
Print Name

Signature: April Bumgarner Signature: Katherine A. Whitley

Date Issued: 10/31/2016

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St, Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

IMPROVEMENT PERMIT for a RESIDENTIAL
ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

Permit #: **30008514** GWS File #: **14962**

IV. Permit Conditions/Comments:

- This type of septic system requires an inspection once every 5 years by our office. The system owner is responsible for any fees, as determined by the Mecklenburg County Board of Commissioners, associated with this inspection.
- 100% repair area is not required for this property. However, the maximum feasible area shall be allocated for a repair area.
- All waterlines must be located a minimum of 10 ft. from any part of the septic system.
- Foundation drains shall be constructed not to discharge water onto or across any part of the septic system.
- The septic system shall be located at least 15 feet from any foundation drain.


The undersigned, an authorized agent of the STATE OF NORTH CAROLINA, certifies that the Department is issuing an IMPROVEMENT PERMIT for the above referenced property. This permit is being issued in accordance with the *Laws and Rules For Sewage Treatment and Disposal Systems* and is subject to the following provisions:

- No work shall be conducted on the septic system until a Pre-Construction meeting has been completed by the Department.
- The septic system installer shall be a licensed septic contractor with the North Carolina Wastewater Contractor Inspector Certification Board.
- The permitted system shall be installed in accordance with the included PLOT PLAN.
- This IMPROVEMENT PERMIT is transferable.

Authorized Agent: April Bumgarner
Signature: April Bumgarner
Date Issued: 10/31/2016

Owner/Legal Agent: Katherine A. Whitley
Print Name
Signature: Katherine A. Whitley

On-site Wastewater Improvement Permit Diagram

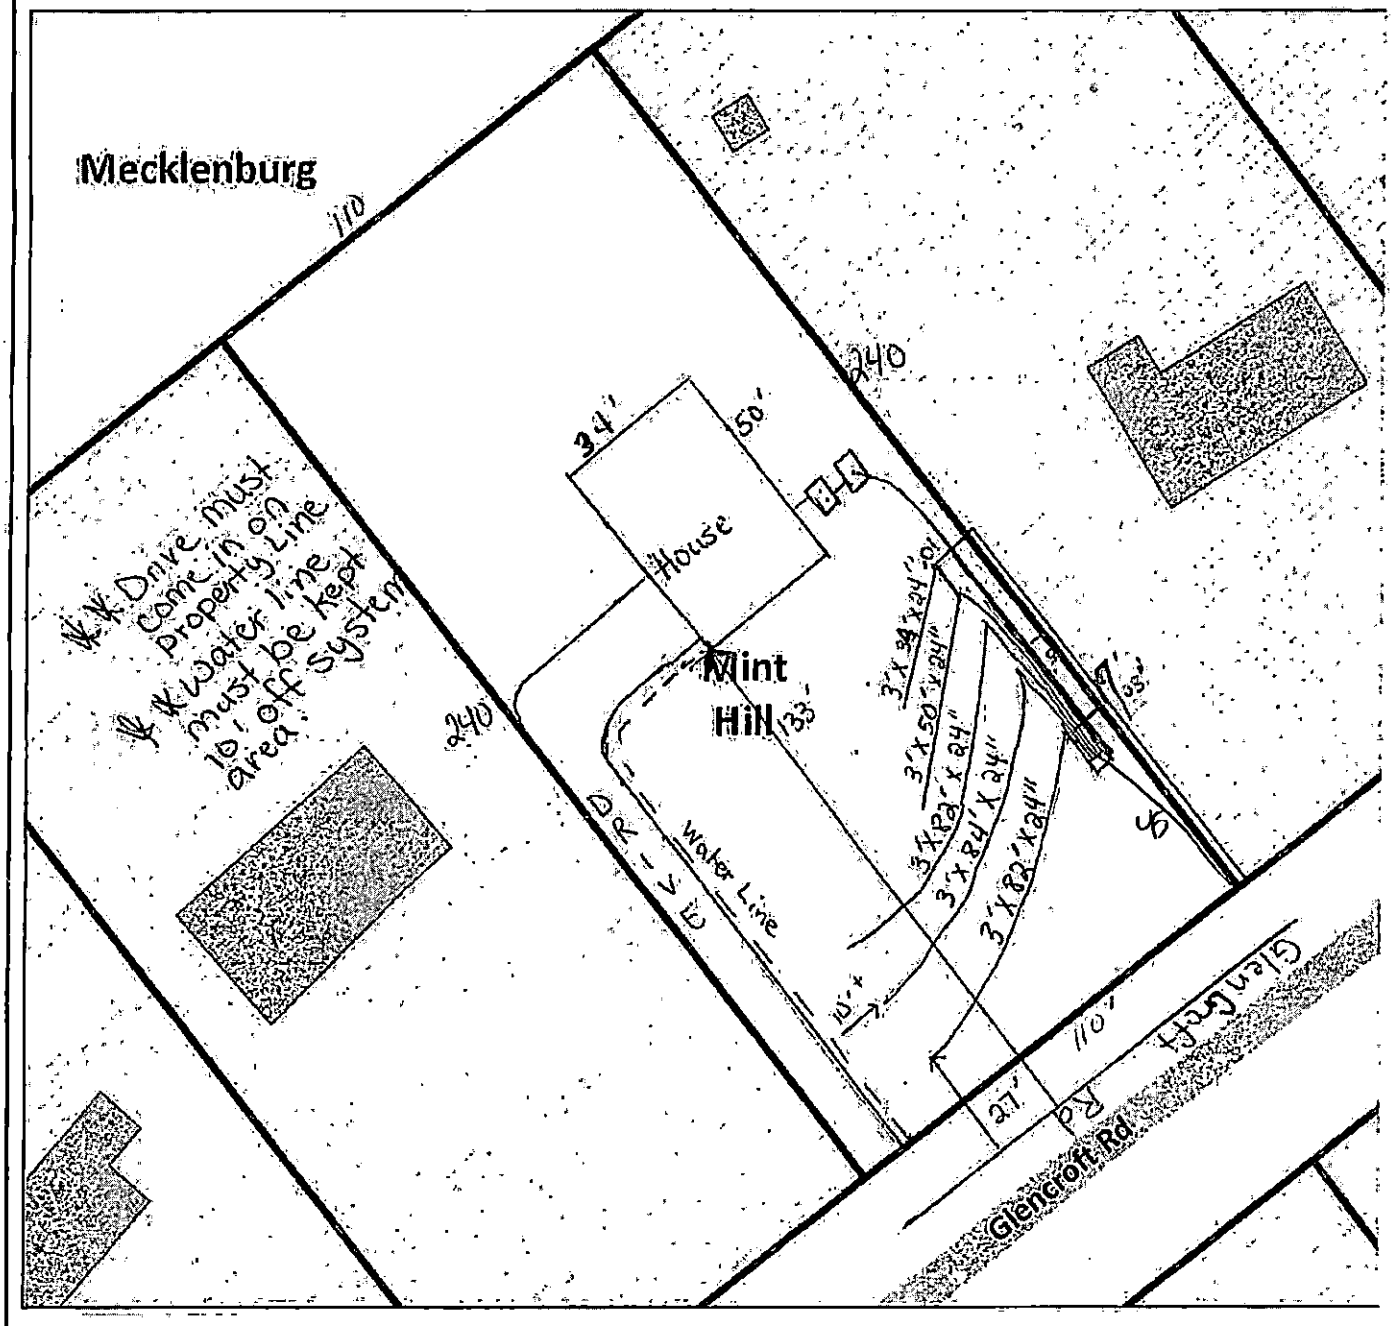

Mecklenburg County Health Department
Environmental Health - Groundwater and Wastewater Services

Permit #: 8514
PID #: 139-051-18
File #: 14962

Authorized Agent: April Bumgarner Date: 10-31-16

Owner/ Legal Agent: Kelly A. Ashley Date: 11-14-2016

1 inch = 40 fee

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St., Suite 211 Charlotte, NC 28202
Phone: (980) 314-1680 Fax: (704) 336-6894

Septic System Pre-Construction Meeting Checklist

File # 14962 App # 8514 Tax Parcel # 139-051-18

Property Owner: Johnny Whitley

Job Location Address: 8842 Glencroft Rd

City: Mint Hill State: NC Zip Code: 28227

1. **Does System design match facility, flow & wastewater characteristics?**

   ☑ YES ☐ NO

   Comments: _____

2. **Is there sufficient available space for the septic systems initial and repair areas?**

   ☑ YES ☐ NO

   Comments: Drive way will be relocated to the property line.

3. **Can the septic system be installed per the permit conditions and drawing on file?**

   ☑ YES ☐ NO

   Comments: _____

* If "NO" is checked for any of the above the existing permit may need to be revoked.

Permission is hereby given to ☑ install ☐ alter ☐ repair an on-site wastewater treatment & and disposal system, with subsurface soil absorption and effluent discharge meeting all of the construction requirements of 15A NCAC 18A .1900 which are in effect on the date of granting this approval. System shall not be installed while soils are in wet condition.

April Burrgauer — Authorized Agent

12-14-17 — Date

Johnny Whitley 12-14-17 / Stevens septic 1/4/18 — Others Present

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St., Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DHHS
Division of Environmental Health
On-Site Wastewater Section

OPERATION PERMIT for an ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

File #: 14962 Permit #: 8514 Tax Parcel #: 139-051-18

Property Owner: Johnny Whitley

Job Location Address: 8842 Glencroft Rd

City: Mint Hill State: NC Zip Code: 28227

Operation Permit Issuance Date: 1-4-18 Contractor Name: Stevens Septic

Permitted Design Flow: 360 GPD Liquid Capacity of Dosing Tank: 1000 gallons 10-13-17

Liquid Capacity of Septic Tank: 1000 gallons 11-14-17 Manufacture Dellinger Effluent Pump Model: _____

Drainfield Installation ☐ N/A

Trench Depth: 20" inches

Trench Width: 3 feet

Line Spacing: 9 feet (O.C.)

Total line length: 327 feet

# of Lines: 5 @ Various feet

Depth of Media: 12 inches (Type) Arc 36

Depth of Cover: 8 inches

Distribution Device: Pressure Manifold

Bed Installation *(For Repair Installations ONLY.)* ☒ N/A

Bed Depth: _____ inches

Bed Width: _____ feet

Total line length: _____ feet

# of Lines: _____ @ _____ feet

Depth of Media: _____ inches (Type) _____

Depth of Cover: _____ inches

Distribution Device: _____

Water Supply Source

☒ Municipal ☐ Private Well ☐ Community Well

☐ Other _____

System Installation Setbacks

Distance from Building Foundation: 5 feet

Distance from Property Line: 10 feet

Distance from Water Supply Source: 10' feet water line not installed as of 1-14-18.


Inspection Dates

Tank(s) Inspected: 1-4-18

Excavation Inspected: 1-4-18

Pump & Controls Inspected: 1-4-18

SKETCH OF SYSTEM INSTALLATION
(As-Built Drawing) Glencroft Rd

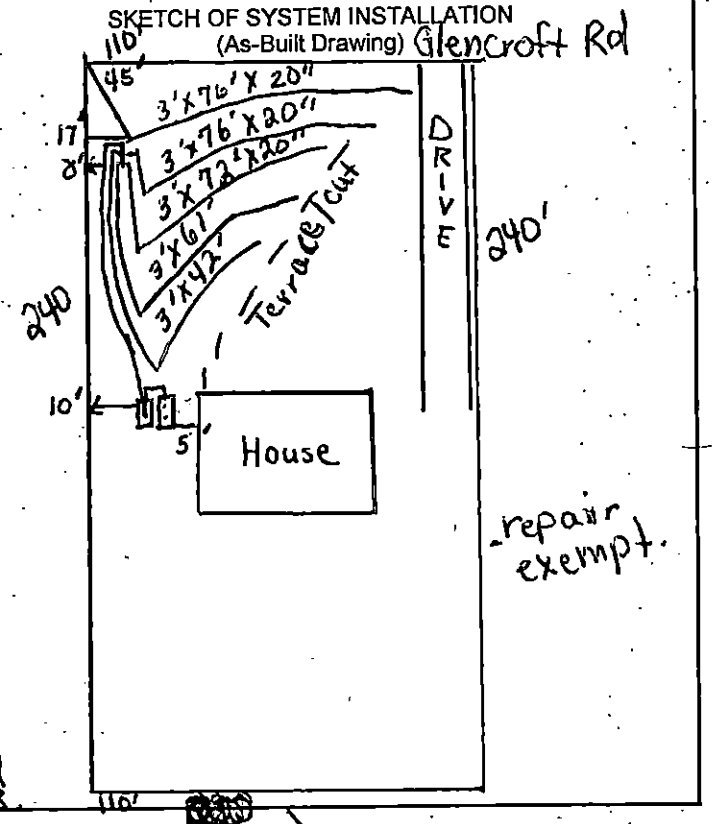

repair exempt.

The undersigned has inspected the Septic Tank System described above, and certifies it has been ☑ installed ☐ altered ☐ repaired ☐ as detailed in the plot above ☐ in accordance with the permit issued and meets the provisions of 15A NCAC 18A. 1900, "Laws and Rules for Sewage Treatment and Disposal Systems" in effect on the date of issuance of the permit. The issuance of this Operation Permit does not in any way guarantee that the system will operate properly or relieve any person now or hereafter owning, controlling, or using such system from any liability resulting from the failure of the system to operate properly. This document is issued subject to those restrictions and conditions shown on the permit(s) and the provisions of 15A NCAC 18A. 1900 in addition to those listed below under "Comments." This document shall be null and void if any information contained in the application is untrue or if any additions are made to the property which would increase the requirements for said system.

Notice: Disturbance of the designated repair area may result in the Suspension or Revocation of this permit.

Comments: System Classification & Type: III b / Arc 36 / P / NA / NA

Drive way must be relocated to property line.

DENR Authorized Agent: April Bumgarner Signature: April Bumgarner

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St., Suite 211 Charlotte, NC 28202
Phone: (980) 314-1680 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

OPERATION PERMIT for an
ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

File #: 14962 Permit #: 8514 Tax Parcel #: 139-051-18

Property Owner: Johnny Whitley

Job Location Address: 8842 Glencroft Rd

City: Mint Hill State: NC Zip Code: 28227

OPERATION PERMIT CONDITIONS:

I. Performance: System shall perform in accordance with 15A NCAC 18A .1961.

II. Monitoring: System shall be monitored as required by 15A NCAC 18A .1961.

III. Maintenance: Ground absorption sewage treatment and disposal systems shall be checked, and the contents of the septic tank removed, periodically from all compartments, to ensure proper operation of the system. The contents shall be pumped whenever the solids level is found to be more than 1/3 of the liquid depth in any compartment.

IV. Operation: System shall be operated in accordance with 15A NCAC 18A .1961.

System Classification: IIIb

*Operation Permits for Type V and VI systems expire five (5) years from the date of issuance (in accordance with Table V(a)). The system owner must contact GWS six (6) months prior to expiration for permit renewal.

Subsurface system operator required: Yes ☐ No ☒

☐ This type of system requires the system owner to maintain a contract with a certified operator to perform system inspection, maintenance, and reporting as required in 15A NCAC 18A .1961. and Table V(a). The system owner is responsible for all fees associated with these services.

☐ System does not require inspection by GWS on a routine frequency.

☒ System requires inspection by GWS once every five (5) years. The system owner is responsible for all fees associated with the inspection.

☐ System requires inspection by GWS once every three (3) years. The system owner is responsible for all fees associated with the inspection.

☐ System requires inspection by GWS once every twelve (12) months. The system owner is responsible for all fees associated with the inspection.

☐ System requires inspection by GWS once every six (6) months. The system owner is responsible for all fees associated with the inspection.

V. Other:

DENR Authorized Agent: April Bumgarner Date: 1-8-18

Signature: April Bumgarner

Supervisor/Administrative Professional Checklist

XS2004

New Septic ☒ New Well ☐ Use Existing ☐ Alteration ☐ Modified Plot Plan ☐

New Septic Fees Paid:

IP ($250.00) 12/14/15 EA Initials/Date

CA ($200.00) 1/3/17 LE Initials/Date

OP ($200.00) 1/3/17 LE Initials/Date

(CA and OP fees need to be paid before a building permit can be issued)

New Well Fee Paid: $550.00 _____ Initials/Date

Use Existing Fee Paid: $100.00 _____ Initials/Date

Alteration Fee Paid: $300.00 (Total) $200 (If use existing was paid)_____ Initials/Date

Modified Plot Plan Fee Paid: $100.00 _____ Initials/Date

Floor plans need to be submitted and reviewed before CA can be issued. ☑ Reviewed ☑ JM 1-4-17

OK to generate CA

This site is served by septic and well. Verify each is complete before final hold is released. ☐

Septic file completed. ☐ _____ Well file completed. ☐ _____

Send permit for signature. ☑ Signature received. ☑ _____

This septic system requires a certified operator contract before final hold is released. ☐

Certified operator contract is on file. ☐ _____

S

FEE: 200.00
DATE:1/6/2017

MECKLENBURG COUNTY
GROUNDWATER & WASTEWATER SERVICES

FILE NUMBER: 14962

PERMIT NUMBER: 30008514

PARCEL NUMBER: 13905118

JOB LOCATION INFORMATION

ADDRESS: 8842 GLENCROFT RD

CITY: CHARLOTTE **STATE: NC** **ZIP:** 28227

ISSUED TO: KATHERINE & JOHN WHITLEY

CONSTRUCTION AUTHORIZATION ISSUANCE DATE: 1/6/2017

CONSTRUCTION AUTHORIZATION CONDITIONS

1. WASTEWATER SYSTEM CONSTRUCTION AND INSTALLATION MUST MEET ALL CONDITIONS AND SPECIFICATIONS AS SET FORTH IN IMPROVEMENT PERMIT NUMBER 30008514, AND THE ATTACHED SITE PLAN WITH SYSTEM DETAILS. CONSTRUCTION AND INSTALLATION MUST ALSO MEET ALL REQUIREMENTS SET FORTH IN THE RULES GOVERNING SANITARY SEWAGE COLLECTION, TREATMENT, AND DISPOSAL AND ANY OTHER APPLICABLE RULES AND LAWS.

2. A PRE-CONSTRUCTION MEETING MUST BE SECURED PRIOR TO INSTALLATION OF THE SEPTIC TANK SYSTEM. THE INSTALLER OF THE SYSTEM SHALL BE A LICENSED SEPTIC TANK CONTRACTOR WITH THE NORTH CAROLINA ONSITE WASTEWATER CONTRACTOR INSPECTOR CERTIFICATION BOARD.

3. ANY ALTERATION IN SITE OR SOIL CONDITIONS (INCLUDING LOCATION OF STRUCTURES AND APPURTENANCES) OR MODIFICATION IN USE, DESIGN WASTEWATER FLOW, OR WASTEWATER CHARACTERISTICS AS SPECIFIED IN THE ASSOCIATED IMPROVEMENT PERMIT AND APPLICATION, MAY SUBJECT THIS CONSTRUCTION AUTHORIZATION AND ASSOCIATED PERMIT(S) TO REVOCATION.

4. THIS CONSTRUCTION AUTHORIZATION AS PROVIDED IN G.S. 130A-335(f) AND G.S. 130A-336(b) SHALL BE VALID FOR A PERIOD EQUAL TO THE VALIDITY OF THE IMPROVEMENT PERMIT, NOT TO EXCEED 60 MONTHS.

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St, Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

IMPROVEMENT PERMIT for a RESIDENTIAL ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

Permit #: **30008514** GWS File #: **14962** Tax Parcel #: **139-051-18**

- This IMPROVEMENT PERMIT is subject to revocation if site plans or the intended use change. There is to be NO grading, filling, or disturbance of the soil in the area of the septic tank system or repair area.
- CONSTRUCTION AUTHORIZATION must be obtained prior to receiving a Building Permit. The Construction Authorization is **NOT** transferable. Do not clear, grade, fill or disturb soil prior to obtaining a Construction Authorization.
- Domestic-type wastewater only. No industrial process wastewater may be discharged into the system.

I. This Improvement Permit Shall: Expire in Five (5) Years **Expiration Date (If Applicable):** 10/31/2021

Type of Installation: Residential - Modified Plot Plan Lot Number: 0

Structure Type: HOUSE Size (ft^2): 1950 # Bedrooms: 3 # Occupants: 6

Building Foundation: Water Supply: Municipal

II. Initial System Type: Pump to Accepted **System Classification:** IIIb

Initial System Specifications:

Design Flow (gpd):	360	LTAR (gpd/ft^2):	0.275	Septic Tank Size (gal):	1000	Pump Tank Size (gal):	1000
Trench Width (ft):	3	Trench Spacing (ft):	9	Absorption Area (ft^2):	982	Total Trench Length (ft):	327
Maximum Trench Depth (in):	24	Depth of Media (in):	12	Distribution Device:	Pressure Manifold		

III. Repair System Type: N/A **System Classification:**

Repair System Specifications:

Design Flow (gpd):	0	LTAR (gpd/ft^2):	0.0	Septic Tank Size (gal):	0	Pump Tank Size (gal):	0
Trench Width (ft):	0	Trench Spacing (ft):	0	Absorption Area (ft^2):	0	Total Trench Length (ft):	0
Maximum Trench Depth (in):	0	Depth of Media (in):	0	Distribution Device:	N/A		

IV. Permit Conditions/Comments:

(Please See the Following Page for Permit Conditions.)

The undersigned, an authorized agent of the STATE OF NORTH CAROLINA, certifies that the Department is issuing an IMPROVEMENT PERMIT for the above referenced property. This permit is being issued in accordance with the *Laws and Rules For Sewage Treatment, and Disposal Systems* and is subject to the following provisions:

- No work shall be conducted on the septic system until a Pre-Construction meeting has been completed by the Department.
- The septic system installer shall be a licensed septic contractor with the North Carolina Wastewater Contractor Inspector Certification Board.
- The permitted system shall be installed in accordance with the included PLOT PLAN.
- This IMPROVEMENT PERMIT is transferable.

Authorized Agent: April Bumgarner Owner/Legal Agent: _____
Print Name

Signature: April Bumgarner Signature: _____

Date Issued: 10/31/2016

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St, Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

IMPROVEMENT PERMIT for a RESIDENTIAL ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

Permit #: **30008514** GWS File #: **14962**

IV. Permit Conditions/Comments:

- This type of septic system requires an inspection once every 5 years by our office. The system owner is responsible for any fees, as determined by the Mecklenburg County Board of Commissioners, associated with this inspection.
- 100% repair area is not required for this property. However, the maximum feasible area shall be allocated for a repair area.
- All waterlines must be located a minimum of 10 ft. from any part of the septic system.
- Foundation drains shall be constructed not to discharge water onto or across any part of the septic system.
- The septic system shall be located at least 15 feet from any foundation drain.

The undersigned, an authorized agent of the STATE OF NORTH CAROLINA, certifies that the Department is issuing an IMPROVEMENT PERMIT for the above referenced property. This permit is being issued in accordance with the *Laws and Rules For Sewage Treatment and Disposal Systems* and is subject to the following provisions:

- No work shall be conducted on the septic system until a Pre-Construction meeting has been completed by the Department.
- The septic system installer shall be a licensed septic contractor with the North Carolina Wastewater Contractor Inspector Certification Board.
- The permitted system shall be installed in accordance with the included PLOT PLAN.
- This IMPROVEMENT PERMIT is transferable.

Authorized Agent: April Bumgarner


Signature: April Bumgarner

Date Issued: 10/31/2016

Owner/Legal Agent: _____
Print Name

Signature: _____

On-site Wastewater Improvement Permit Diagram

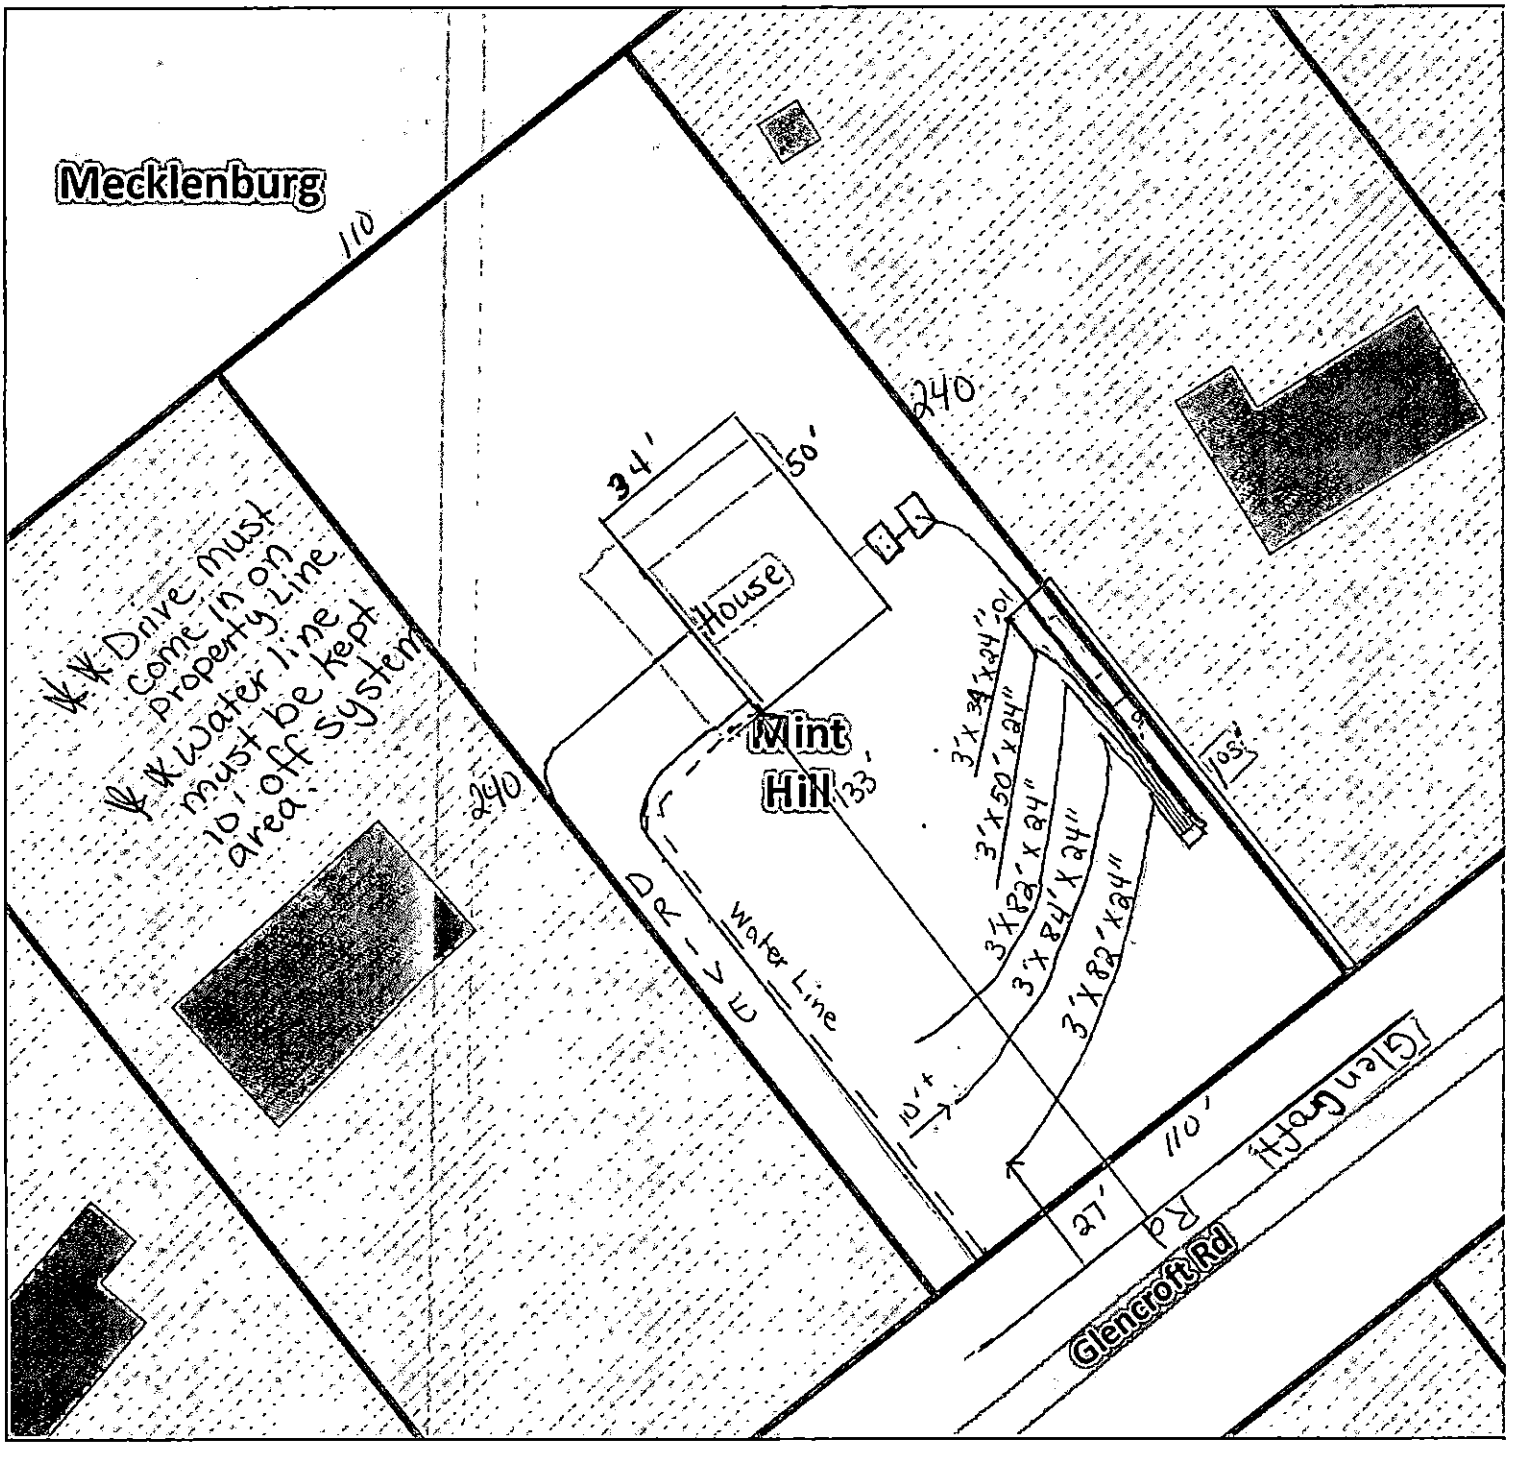

Mecklenburg County Health Department
Environmental Health - Groundwater and Wastewater Services

Permit #: 8514
PID #: 139-051-18
File #: 14962

Authorized Agent: April Bumgarner Date: 10-31-16

Owner/ Legal Agent: _____ Date: _____

1 inch = 40 fee
