Date Received April 12, 1977

APT No. 12191

T. C. No. 89-021-18

Map Date 12-10-75

MECKLENBURG COUNTY
DEPARTMENT OF ENVIRONMENTAL HEALTH

APPLICATION FOR SOIL INVESTIGATION

1) NAME OF OWNER Primm (LAST) Craig (FIRST) A. (MIDDLE)

2) ADDRESS OF OWNER Rt. 9 Box 390 Charlotte, N. C. ZIP 28208

3) PHONE NO. Home 399-9886 Office No.

4) LOCATION OF PROPERTY Sadler Road - (in county) (STREET OR COUNTY ROAD)

5) SUBDIVISION Paw Creek LOT NO. 18 BLOCK NO. ~~xx~~ 21

MAP BOOK NO 31 PAGE NO. 2

6) DEED REFERENCE. DEED BOOK 2343 PAGE NO. 383

Application is hereby made to the Mecklenburg County Department of Environmental Health for the conduct of a soil investigation and an on site inspection of the lot hereinabove described for the purpose of determining if the lot is suitable for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge.

Notes -

1- Copy of Survey Attached & Marked

2- Brick Colored Cloth Markers on Front-Left & Right of Property Fence Follows RH Side & Rear of Property Line

3- Stem Marked Soil Test Property Front.

7) ACCURATELY DIAGRAM & DIMENSION LOT

Craig A Primm
OWNER

EHO-5-74

Environmental Health Department's Copy

SOIL INVESTIGATION REPORT

Date of Investigation April 21, 1977 APT NO. 12/9 #

Owner Craig A. Price TL 031-02248

Location of Property Sulphur Rd Lot #8

Soil Properties	Soil Suitability Ratings			
	Soil 1	Soil 2	Soil 3	Soil 4
1. Soil Series	Cecil	Enon		
2. Soil Slope	suitable 2-6%	suitable 2-6%		
3. Soil Depth	suitable >48"	suitable 48"		
4. Soil Texture	Provisionally suitable clay	unsuitable 2-1 Expanding clay		
5. Soil Structure	Provisionally suitable blocky	unsuitable Massive		
6. Restrictive Horizons				
7. Soil Drainage	suitable water Table >6'	suitable water Table >6'		
8. Soil Permeability (Percolation Rate)	Provisionally suitable Moderate 60 min/in	unsuitable slow-very slow >120 min/in		
9. Other				
10. Overall Rating	Provisionally suitable	unsuitable		

Remarks:
Recommendations Based on this investigation, an adequate area of provisionally suitable soils was found for septic tank system installation was found on the lot. System design should be based on percolation rate of 60 min/in and system trenches in texture of soil


See diagram on back

William A. Marlin
Soil Scientist

WCC

3/16/75
EHD 539

DIAGRAM OF PROPERTY

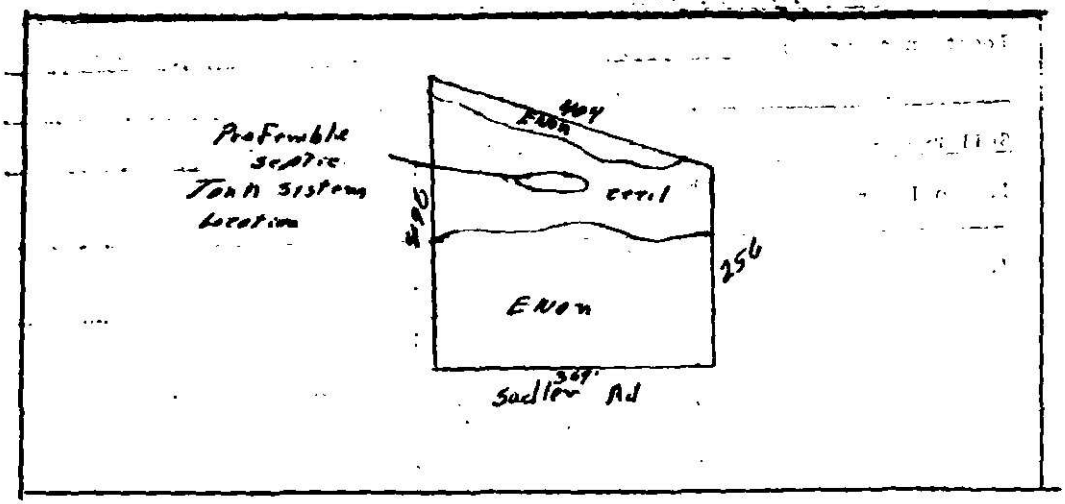

3/18/75

EMS 939

Serial No. 0675

PTR No. 12191

Date Issued April 26, 1977

T. C. No. 031-021-18

Map Date


MECKLENBURG COUNTY
DEPARTMENT OF ENVIRONMENTAL HEALTH
SOIL INVESTIGATION REPORT

NAME OF OWNER Primm (LAST) Craig (FIRST) A. (MIDDLE)

ADDRESS OF OWNER Rt. 9 Box 390, Charlotte, N.C. ZIP 28208

LOCATION OF PROPERTY 606 Sadler Road (STREET OR COUNTY ROAD)

SUBDIVISION LOT NO. 18 BLOCK NO. 21

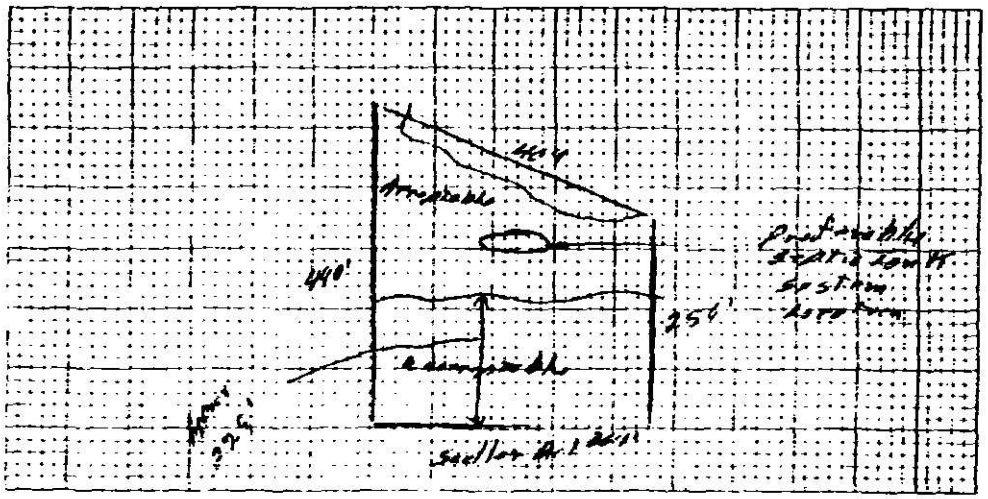

PLOT PLAN

This is to certify that a soil investigation and percolation investigation was made by the Mecklenburg County Department of Environmental Health personnel as described below. The soil investigation was conducted on that part of the lot as indicated on the above plot. Provisionally Suitable

The permeability rate determined by the investigation was 60 min/in. The said lot is approved for the installation of an individual septic tank sewage treatment system with subsurface, soil absorption effluent discharge, subject to the following terms and conditions:

A permit for the construction and operation of the system must be obtained from the Mecklenburg County Department of Environmental Health prior to the beginning of construction of the building to which the wastewater treatment system is to be a part.

2. The size of the septic tank and absorption area of system are to be determined by the Mecklenburg County Department of Environmental Health in accordance with the permeability rate obtained above, and on the size and type of building or number of bedrooms.

3. This approval is valid only for the system installed in the immediate area indicated as acceptable for system installation on the above plot.

4. This approval is void if any grading of the site or other activity disturbing the soil is performed on the lot which, in the opinion of the Mecklenburg County Department of Environmental Health renders the area indicated as acceptable for system installation unsuitable for installation, construction, alteration, and or repair of such a system.

This approval is granted based on the laws of the State of North Carolina and the rules and regulations of the North Carolina Department of Human Resources, Division of Health Services and the Mecklenburg County Health Commission which were in effect on the date of issuance and is void if at any time in the future, prior to completion of the system, these laws, rules and regulations are changed such that this approval would not have been granted had the new or revised laws, rules, and regulations been in effect on the issue date.

William A. Marlow
Soil Scientist

John M. Robinson
Environmental Health Director or Authorized Section Head

EHD-S-76

Environmental Health Department's Copy
