Date Received 7-5-79

APT No 7460

T. C No. 135-356-10

Map Date 9-5-73

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

APPLICATION FOR PERCOLATION TEST

1) NAME OF OWNER Bob McLemore & Co.
(LAST, FIRST, MIDDLE)

2) ADDRESS OF OWNER PO Box 25746, Charlotte ZIP 28212

3) PHONE NO. Home _____ Office 545-6111


4) LOCATION OF PROPERTY 4411 Quail Ridge Dr.
(STREET OR COUNTY ROAD)

5) SUBDIVISION Fairwood 5 LOT NO. 22A BLOCK NO. C

MAP BOOK NO _____ PAGE NO. _____

6) DEED REFERENCE: DEED BOOK _____ PAGE NO. _____

Application is hereby made to the Mecklenburg County Health Department for the conduct of a percolation test and an on site inspection of the lot hereinabove described for the purpose of determining if the lot is suitable for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge

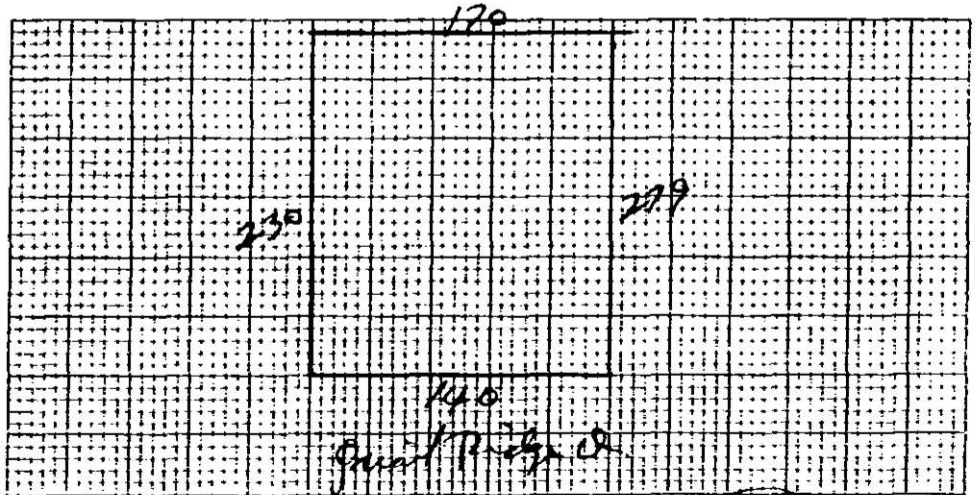

7) ACCURATELY DIAGRAM & DIMENSION LOT

OWNER

FORM NO. E-1-9-1-72

HEALTH DEPARTMENT'S COPY

MECKLENBURG COUNTY HEALTH DEPARTMENT
INTER-OFFICE COMMUNICATION

DATE: February 11, 1974

TO: John Adkisson
Environmentalist

FROM: W. Everette Lynn, Jr. WEL
Soil Scientist

SUBJECT: APT #7460 (Bob McLemore & Co.)
Lot No. 22-A, Block G, 4411 Quail Ridge Drive
Farmwood Subdivision
2-11-74

Soils were found to be of the Enon series. These soils have plastic and sticky clay subsoils which contain swelling clay minerals. These factors result in inadequately slow percolation rate and permeability.

Based on this investigation, it appears that the lot is unsuitable for installation of a conventional septic tank system.

WEL:jdg

MECKLENBURG COUNTY
Department of Public Health

1200 Blythe Boulevard
Charlotte, North Carolina 28203

Telephone 374-2113

Date Issued
1. 2-12-74
2. _____
3. _____

SDR No. 7460
T.C. No. 135-356-10
9-5-73

SITE DISAPPROVAL REPORT
INDIVIDUAL SEPTIC TANK SYSTEM WITH SUBSURFACE,
SOIL ABSORPTION, EFFLUENT DISCHARGE

NAME OF OWNER Bob McLemore & Co.

ADDRESS OF OWNER P.O. Box 25740 ZIP 28212

LOCATION OF LOT 4411 Quail Ridge Drive, Lot 22-A, Block G

The lot described above has been disapproved for the installation of an individual septic tank system with subsurface, soil absorption, effluent discharge due to the following:

FAILURE TO PASS PERCOLATION TEST (60 minutes per inch or less)

	Test No.	Date of Test	Percolation Rate
____	1.	_____	_____ min/in
____	2.	_____	_____ min/in
____	3.	_____	_____ min/in

X ON SITE INSPECTION REVEALED LOT TO BE UNSUITABLE FOR THE FOLLOWING REASON(S) 2-11-74 - Soils were found to be of the Enon series. These soils have plastic and sticky clay subsoils which contain swelling clay minerals. These factors result in inadequately slow percolation rate and permeability.

W. Forsythe Lyons Jr. John R. Hairston
Soil Scientist Environmentalist

(Stencil No.)
EHD 398
8/70

FORM NO.
E-19-8-14-70
