Date Received 6-1-73

APT No. 6397

T. C No. 15-043-50

Map Date 2-19-73 2/21/75

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

APPLICATION FOR PERCOLATION TEST

1) NAME OF OWNER Lane (LAST) D. (FIRST) R. (MIDDLE)

2) ADDRESS OF OWNER 2121 Linalda Court, Charlotte, N. C. ZIP 28214

3) PHONE NO Home 399-6142 Mintforest Office 889-7600


4) LOCATION OF PROPERTY ~~Mintwood~~ Drive (STREET OR COUNTY ROAD)

5) SUBDIVISION Mintwood Estates LOT NO. 4 BLOCK NO. --

MAP BOOK NO. 15 PAGE NO. 593

6) DEED REFERENCE DEED BOOK _____ PAGE NO. _____

Application is hereby made to the Mecklenburg County Health Department for the conduct of a percolation test and on on site inspection of the lot hereinabove described for the purpose of determining if the lot is suitable for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge.

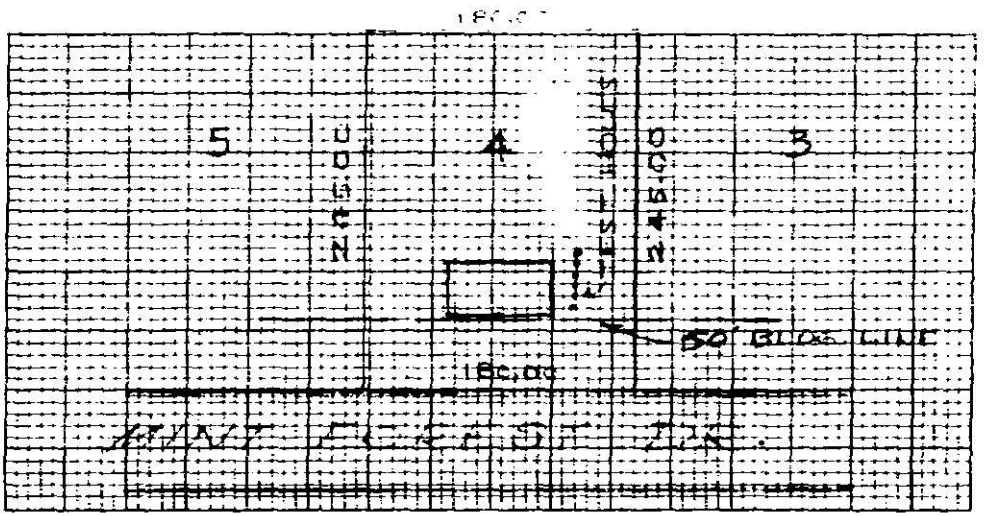

7) ACCURATELY DIAGRAM & DIMENSION LOT

D. R. Lane
OWNER

FORM NO. E-1-11-1-70

HEALTH DEPARTMENT'S COPY

SOIL INVESTIGATION REPORT

Date of Investigation 5-8-75 Apt. No. 6397

Owner O. K. Lane

Location of Property Lot No. 4, Mint Forest Dr.
TCN: 175-093-50

Soil Suitability Ratings

Soil Properties	Soil 1	Soil 2	Soil 3	Soil 4.
1. Soil Series	Cecil			
2. Soil Slope	Suitable 2-9%			
3. Soil Depth	Suitable >60"			
4. Soil Texture	Marginal clay			
5. Soil Structure	Marginal blocky			
6. Restrictive Horizons	—			
7. Soil Drainage	Suitable W.T. >60"			
8. Soil Permeability (Percolation Rate)	Marginal 60 min/in			
9. Other	—			
10. Overall Rating	Marginal			

Recommendations Approval - System design based on a perc. rate of 60 min/in.

See Diagram on Back

L. Everette Cyrus, Jr.
Soil Scientist

3/18/75
EHD 539

Serial No. 5203

PTR No 6397

Date Issued May 9, 1975

T C No 195-043-50

Map Date 2-21-75

Do Not Issue A Building Permit Based On This Form

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION


PERCOLATION TEST REPORT

NAME OF OWNER Lane (LAST) D. (FIRST) R. (MIDDLE)

ADDRESS OF OWNER 2121 Linalda Court, Charlotte, N. C. ZIP 28214

LOCATION OF PROPERTY Mintforest Drive (STREET OR COUNTY ROAD)

SUBDIVISION Mintwood Estates LOT NO 4 BLOCK NO

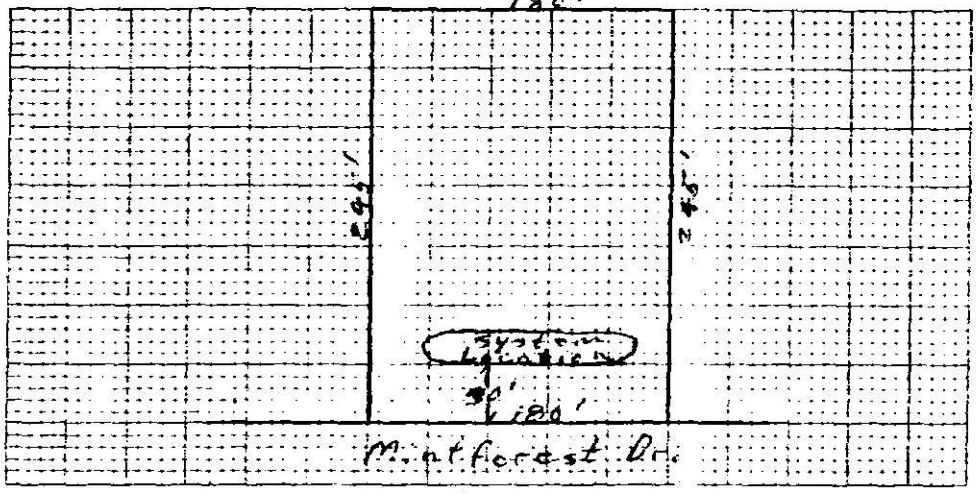

PLOT PLAN

This is to certify that a percolation test has been run and an on-site inspection made by the Mecklenburg County Health Department on the lot described above. The said test was conducted on that portion of the lot as indicated on above plot

The percolation rate determined by the test was *60Min./In. The subject lot is approved for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption effluent discharge subject to the following terms and conditions

1. A permit to install, construct, alter, or repair the specific system shall be obtained from the Mecklenburg County Health Department prior to the beginning of any construction of buildings, or of the wastewater treatment system on the subject lot.
2. The size of the septic tank wastewater treatment system which must be installed will be determined by the Health Department prior to installation based on the percolation rate obtained above, and on the size and type of building constructed thereon.
3. This approval is valid only if the system is installed in the immediate area where the percolation test was run.
4. This approval is void if any grading, filling, or construction (including the drilling of a well) is performed on the lot which, in the opinion of the Health Department, renders the area where the percolation test was run unsuitable for the installation, construction, alteration, and/or repair of such a system.

This approval is granted based on the laws of the State of North Carolina and the rules and regulations of the North Carolina State Board of Health and the Mecklenburg County Board of Health which were in effect on the date of issuance and is void if at any time in the future, prior to the completion of the system, these laws, rules, and regulations are changed such that this approval would not have been granted had the new or revised laws, rules, and regulations been in effect at the issue date.

*Results determined by soil analysis

W. Grattan Lyon, Jr. Soil Scientist

John R. Robinson

Director, Environmental Health Division or Authorized Section Head

FORM NO. E-2-9-1-72

HEALTH DEPARTMENT'S COPY
