Date Received 6-1-73

APT No. 6412

T. C. No.

Map Date

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

APPLICATION FOR PERCOLATION TEST

1) NAME OF OWNER Lane (LAST) D. (FIRST) R. (MIDDLE)

2) ADDRESS OF OWNER 2121 Linalda Court, Charlotte, N. C. ZIP 28214

3) PHONE NO. Home 399-6142 Office 889-7600


4) LOCATION OF PROPERTY Mintstone Drive (STREET OR COUNTY ROAD)

5) SUBDIVISION Mintwood Estates LOT NO. 19 BLOCK NO. --

MAP BOOK NO. 15 PAGE NO. 593

6) DEED REFERENCE. DEED BOOK PAGE NO.

Application is hereby made to the Mecklenburg County Health Department for the conduct of a percolation test and an on site inspection of the lot hereinabove described for the purpose of determining if the lot is suitable for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge.

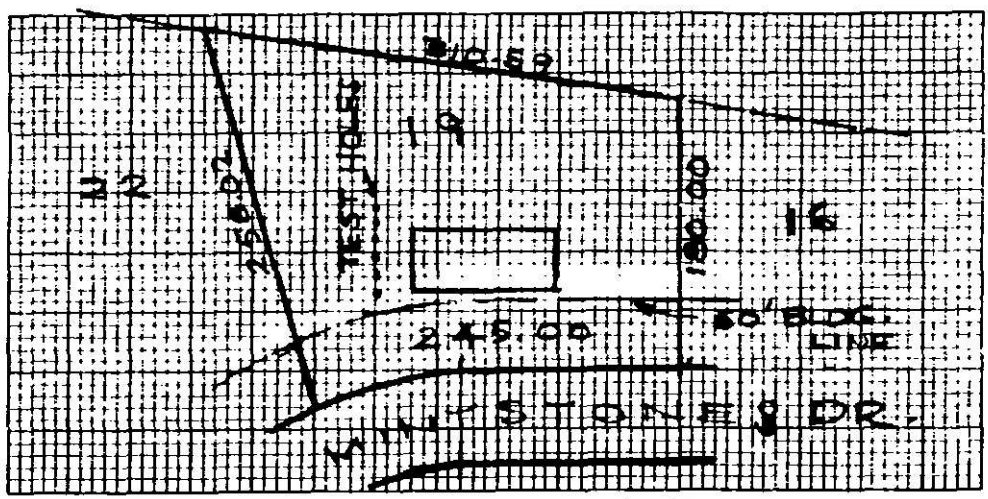

7) ACCURATELY DIAGRAM & DIMENSION LOT

OWNER D. R. Lane

FORM NO. E-1-11-1-70

HEALTH DEPARTMENT'S COPY

Serial No. 3505

PTR No. 6412

Date Issued August 22, 1973

T. C. No. 195-042-02

Map Date 2-14-73

Do Not Issue A Building Permit Based On This Form

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION


PERCOLATION TEST REPORT

NAME OF OWNER Lane (LAST) D. (FIRST) R. (MIDDLE)

ADDRESS OF OWNER 2121 Linalda Court ZIP 28214

LOCATION OF PROPERTY Mintstone Drive (STREET OR COUNTY ROAD)

SUBDIVISION Mintwood Estates LOT NO. 19 BLOCK NO.

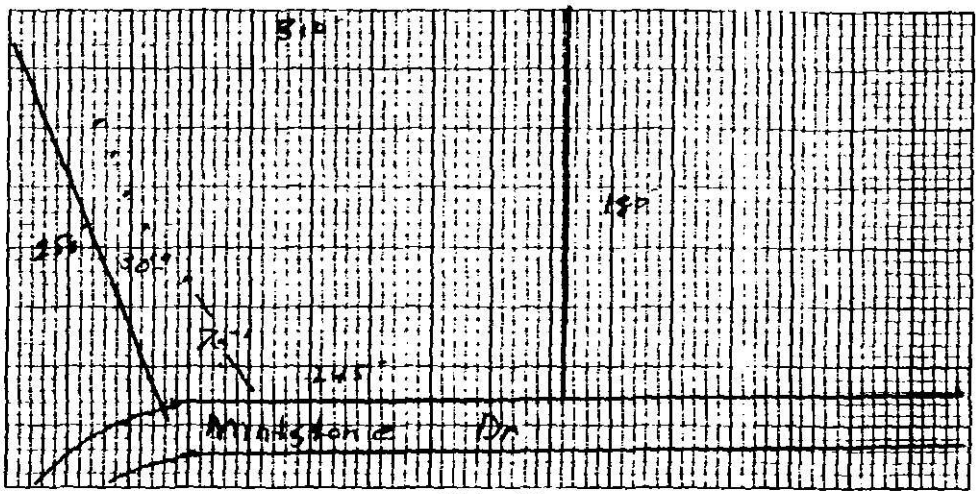

PLOT PLAN

This is to certify that a percolation test has been run and on on-site inspection made by the Mecklenburg County Health Department on the lot described above. The said test was conducted on that portion of the lot as indicated on above plot.

The percolation rate determined by the test was 55 min/in The said lot is approved for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption effluent discharge subject to the following terms and conditions:

1. A permit to install, construct, alter, or repair the specific system shall be obtained from the Mecklenburg County Health Department prior to the beginning of any construction of buildings, or of the wastewater treatment system on the said lot.
2. The size of the septic tank wastewater treatment system which must be installed will be determined by the Health Department prior to installation based on the percolation rate obtained above, and on the size and type of building constructed thereon.
3. This approval is valid only if the system is installed in the immediate area where the percolation test was run.
4. This approval is void if any grading, filling, or construction (including the drilling of a well) is performed on the lot which, in the opinion of the Health Department, renders the area where the percolation test was run unsuitable for the installation, construction, alteration, and/or repair of such a system.

This approval is granted based on the laws of the State of North Carolina and the rules and regulations of the North Carolina State Board of Health and the Mecklenburg County Board of Health which were in effect on the date of issuance and is void if at any time in the future, prior to the completion of the system, these laws, rules, and regulations are changed such that this approval would not have been granted had the new or revised laws, rules, and regulations been in effect on the issue date.

John R. Hobson

Director, Environmental Health Division or Authorized Section Head

FORM NO. E-2-4-1-71

HEALTH DEPARTMENT'S COPY
