Date Received 6.6.23

APT No. 6428

T. C. No.

Map Date

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

APPLICATION FOR PERCOLATION TEST

CAMELOT, INC.

1) NAME OF OWNER --Byrum-- --Porter-- --B.--
LAST FIRST MIDDLE

2) ADDRESS OF OWNER 1716 Johnston Bldg., Charlotte, N.C. ZIP 28281

3) PHONE NO. Home 537-8073 Office 332-8134


4) LOCATION OF PROPERTY Camelot Drive, Providence Twp., Mecklenburg County, NC.
STREET OR COUNTY ROAD

5) SUBDIVISION Camelot LOT NO. 26,27,28 BLOCK NO. A

MAP BOOK NO. 11 PAGE NO. 257

6) DEED REFERENCE. DEED BOOK 2952 PAGE NO 100

Application is hereby made to the Mecklenburg County Health Department for the conduct of a percolation test and an on site inspection of the lot hereinabove described for the purpose of determining if the lot is suitable for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge

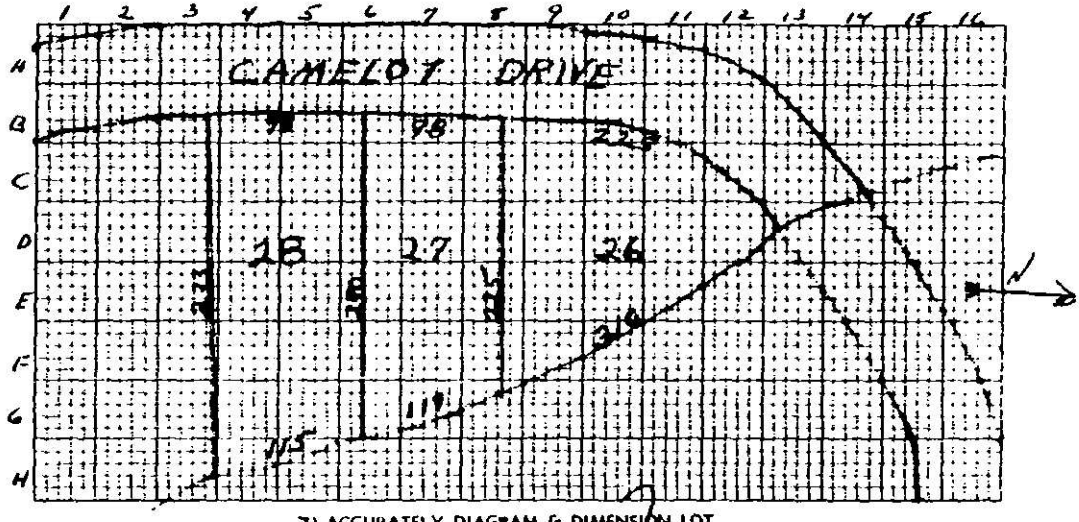

7) ACCURATELY DIAGRAM & DIMENSION LOT

CAMELOT, INC.

OWNER Porter B. Byrum, President

FORM NO E-1-9-1-72

HEALTH DEPARTMENT'S COPY

MECKLENBURG COUNTY
Department of Public Health
1200 Blythe Boulevard
Charlotte, North Carolina 28203

Telephone 374-2113

Date Issued
1. June 13, 1973
2. _____
3. _____

SITE DISAPPROVAL REPORT
INDIVIDUAL SEPTIC TANK SYSTEM WITH SUBSURFACE, SOIL ABSORPTION, EFFLUENT DISCHARGE

SDR No. 6428
T.C. No. _____

NAME OF OWNER Camelot, Inc.

ADDRESS OF OWNER 1716 Johnston Building ZIP 28218

LOCATION OF LOT Camelot Drive, Lots 26,27,28 in Block A

The lot described above has been disapproved for the installation of an individual septic tank system with subsurface, soil absorption, effluent discharge due to the following:

FAILURE TO PASS PERCOLATION TEST (60 minutes per inch or less)

	Test No.	Date of Test	Percolation Rate
X	1.	6-11-73	125 min/in
____	2.	_____	_____ min/in
____	3.	_____	_____ min/in

____ ON SITE INSPECTION REVEALED LOT TO BE UNSUITABLE FOR THE FOLLOWING REASON(S) _____

Thomas R. Ward
Environmentalist

(Stencil No.)
EHD 398
8/70

FORM NO.
E-19-8-14-70

Serial No. 3296

PTR No. 6428

T C. No. 227-095-26,27,28

Date Issued July 6, 1973

Map Date 2-14-73

Do Not Issue A Building Permit Based On This Form

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION


PERCOLATION TEST REPORT

NAME OF OWNER Camelot, Inc
LAST FIRST MIDDLE

ADDRESS OF OWNER 1716 Johnston Building, Charlotte ZIP 28201

LOCATION OF PROPERTY Camelot Drive
STREET OR COUNTY ROAD

SUBDIVISION Camelot LOT NO 26,27,28 BLOCK NO A

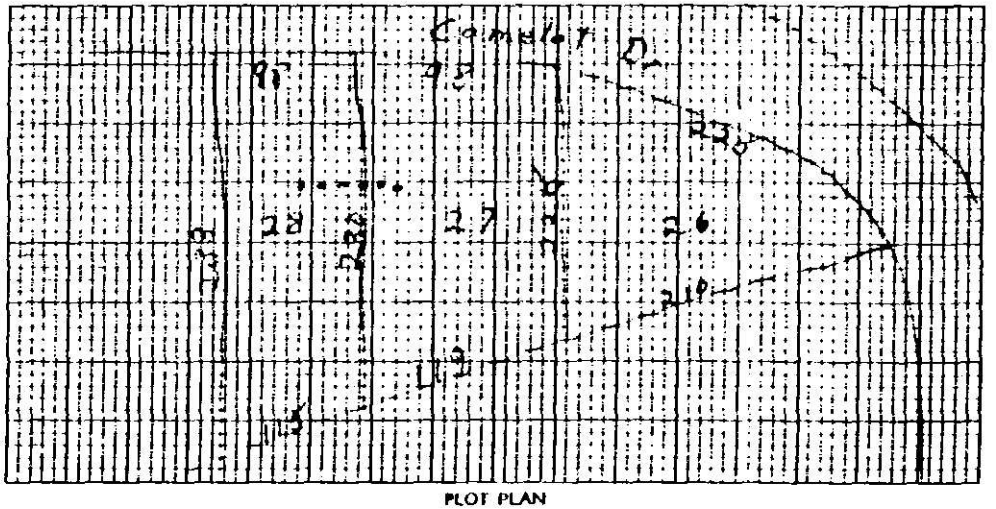

PLOT PLAN

This is to certify that a percolation test has been run and an on-site inspection made by the Mecklenburg County Health Department on the lot described above. The said test was conducted on that portion of the lot as indicated on above plot

The percolation rate determined by the test was 60 min/in The said lot is approved for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption effluent discharge subject to the following terms and conditions:

1. A permit to install, construct, alter, or repair the specific system shall be obtained from the Mecklenburg County Health Department prior to the beginning of any construction of buildings, or of the wastewater treatment system on the said lot.
2. The size of the septic tank wastewater teratment system which must be installed will be determined by the Health Department prior to installation based on the percolation rate obtained above, and on the size and type of building constructed thereon
3. This approval is valid only if the system is installed in the immediate area where the percolation test was run.
4. This approval is void if any grading, filling, or construction (including the drilling of a well) is performed on the lot which, in the opinion of the Health Department, renders the area where the percolation test was run unsuitable for the installation, construction, alteration, and/or repair of such a system

This approval is granted based on the laws of the State of North Carolina and the rules and regulations of the North Carolina State Board of Health and the Mecklenburg County Board of Health which were in effect on the date of issuance and is void if at any time in the future, prior to the completion of the system, these laws, rules, and regulations are changed such that this approval would not have been granted had the new or revised laws, rules, and regulations been in effect on the issue date.

Director, Environmental Health Division or
Authorized Section Head

FORM NO. E-2-4-1-71

HEALTH DEPARTMENT'S COPY

Date Received 10/6/75

APT No. 10133

T. C. No. 227-095-27

Map Date

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

George Wilkinson
9623 Nations Ford Rd
28215

APPLICATION FOR PERCOLATION TEST

1) NAME OF OWNER Camelot, Inc.
(LAST / FIRST / MIDDLE)

2) ADDRESS OF OWNER 1716 Johnston Building, Charlotte, N.C. ZIP 28281

3) PHONE NO. Home _____ Office 332-8134


4) LOCATION OF PROPERTY Camelot Drive
(STREET OR COUNTY ROAD)

5) SUBDIVISION Camelot LOT NO. 27 BLOCK NO. A

MAP BOOK NO. 11 PAGE NO. 257

6) DEED REFERENCE: DEED BOOK 2952 PAGE NO. 100

Application is hereby made to the Mecklenburg County Health Department for the conduct of a percolation test and an on site inspection of the lot hereinabove described for the purpose of determining if the lot is suitable for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge.

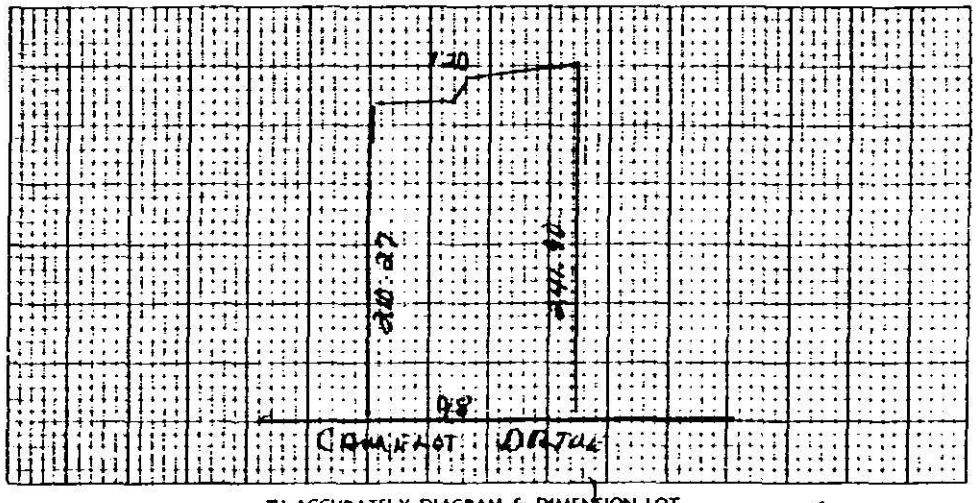

7) ACCURATELY DIAGRAM & DIMENSION LOT

CAMELOT, INC.

OWNER Frank O'Brien President

FORM NO. E1-11-3M-6-75

HEALTH DEPARTMENT'S COPY

SOIL INVESTIGATION REPORT

Date of Investigation October 10, 1975 APT NO. 70133

Owner Camelot Drive

Location of Property Camelot Lot no. 27 Block A

Soil Properties	Soil Suitability Ratings: Soil 1	Soil 2	Soil 3	Soil 4
1. Soil Series	Cecil		Chewacla	
2. Soil Slope	marginal 15-30%		—	
3. Soil Depth	suitable >48"		—	
4. Soil Texture	marginal clayey		—	
5. Soil Structure	marginal subK		—	
6. Restrictive Horizons	—		—	
7. Soil Drainage	marginal 60min/in		unsuitable seasonal high w.t. <18"	
8. Soil Permeability (Percolation Rate)	suitable w.t. 76"		unsuitable floods	
9. Other	—		—	
10. Overall Rating	marginal		unsuitable	

from surface


Recommendations Based on this investigation, the lot is recommended for approval for installation of a septic tank system. System design should be based on a percolation rate of 60min/in. Care should be taken in placing the system due to steep topography.

See diagram on back

W. Edward Casavant
Soil Scientist

3/18/75
EMD 539
wk

DIAGRAM OF PROPERTY

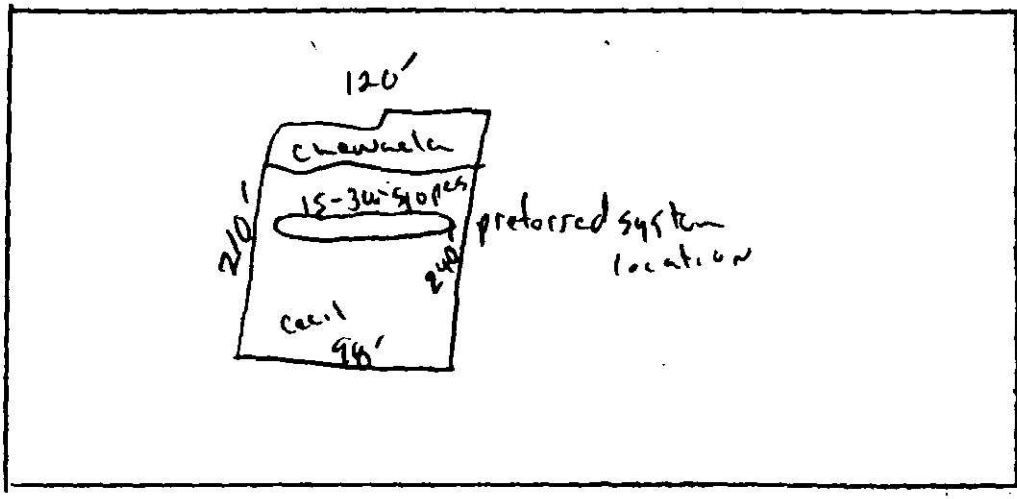

3/18/75

EHD 539

Serial No. 5718

PTR No 10133

T C No 227-095-27

Date Issued 10/13/75

Map Date -

Do Not Issue A Building Permit Based On This Form

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION


PERCOLATION TEST REPORT

NAME OF OWNER Camelot, Inc.
(LAST, FIRST, MIDDLE)

ADDRESS OF OWNER 1716 Johnston Building, Charlotte, N.C. ZIP 28281

LOCATION OF PROPERTY Camelot Drive
(STREET OR COUNTY ROAD)

SUBDIVISION Camelot LOT NO 27 BLOCK NO. A

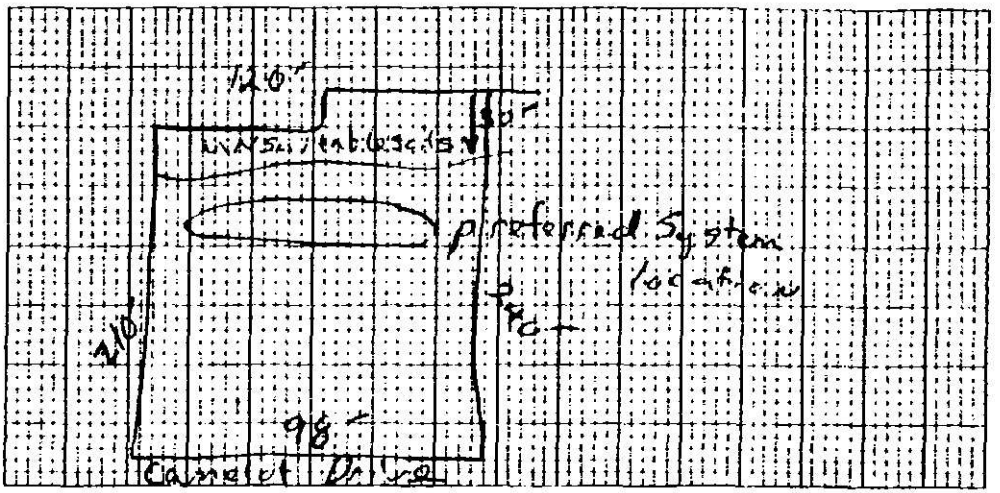

PLOT PLAN

This is to certify that a percolation test has been run and an on-site inspection made by the Mecklenburg County Health Department on the lot described above. The said test was conducted on that portion of the lot as indicated on above plot.

The percolation rate determined by the test was *60Min./In. The said lot is approved for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption effluent discharge subject to the following terms and conditions:

1. A permit to install, construct, alter, or repair the specific system shall be obtained from the Mecklenburg County Health Department prior to the beginning of any construction of buildings, or of the wastewater treatment system on the said lot.
2. The size of the septic tank wastewater treatment system which must be installed will be determined by the Health Department prior to installation based on the percolation rate obtained above, and on the size and type of building constructed thereon.
3. This approval is valid only if the system is installed in the immediate area where the percolation test was run.
4. This approval is void if any grading, filling, or construction (including the drilling of a well) is performed on the lot which, in the opinion of the Health Department, renders the area where the percolation test was run unsuitable for the installation, construction, alteration, and/or repair of such a system.

This approval is granted based on the laws of the State of North Carolina and the rules and regulations of the North Carolina State Board of Health and the Mecklenburg County Board of Health which were in effect on the date of issuance and is void if at any time in the future, prior to the completion of the system, these laws, rules, and regulations are changed such that this approval would not have been granted had the new or revised laws, rules, and regulations been in effect on the issue date.

*Results determined by soil analysis

W. Edward Carswell Soil Scientist

John R. Atkisson

Director, Environmental Health Division or Authorized Section Head

FORM NO. E-2-9-1-72

HEALTH DEPARTMENT'S COPY

Date Received 10/10/75

APT No. 6428

T. C. No. 227-095-26

Map Date ——

Copy to: George W. Whitman
9023 Wotawa Dr.
Charlotte N.C.
28213

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

APPLICATION FOR PERCOLATION TEST

1) NAME OF OWNER Camelot, Inc.
(LAST / FIRST / MIDDLE)

2) ADDRESS OF OWNER 1716 Johnston Building, Charlotte, N.C. ZIP 28281

3) PHONE NO. Home _____ Office 332-8134


4) LOCATION OF PROPERTY Camelot Drive
(STREET OR COUNTY ROAD)

5) SUBDIVISION Camelot LOT NO 26 BLOCK NO. A

MAP BOOK NO 11 PAGE NO. 257

6) DEED REFERENCE DEED BOOK 2952 PAGE NO. 100

Application is hereby made to the Mecklenburg County Health Department for the conduct of a percolation test and an on site inspection of the lot hereinabove described for the purpose of determining if the lot is suitable for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge.

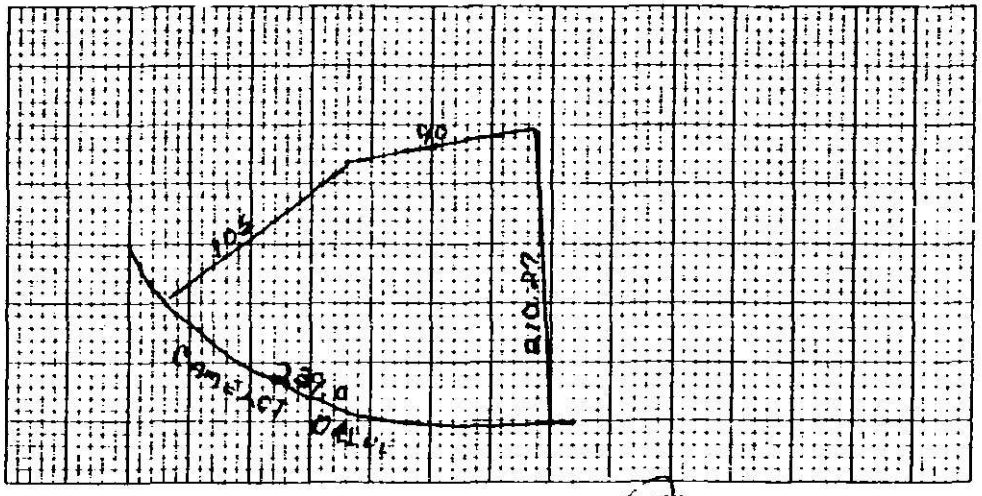

7) ACCURATELY DIAGRAM & DIMENSION LOT

CAMELOT, INC.

OWNER President

FORM NO E1-11-3M-6-75

HEALTH DEPARTMENT'S COPY

SOIL INVESTIGATION REPORT

Date of Investigation October 10, 1975 APT NO. 6428

Owner Camelot, Inc.

Location of Property Camelot Dr. lot no. 26 Block A

Soil Suitability Ratings TCN 227-095-26

Soil Properties	Soil 1	Soil 2	Soil 3	Soil 4
1. Soil Series	Cecil		Chewacla	
2. Soil Slope	marginal 15-30%		—	
3. Soil Depth	suitable >48"		—	
4. Soil Texture	marginal clayey		—	
5. Soil Structure	marginal subA		—	
6. Restrictive Horizons	—		—	
7. Soil Drainage	suitable W.T. 76"		unsuitable seasonal	high W.T. @ 10" from surface
8. Soil Permeability (Percolation Rate)	marginal 60 min/in		unsuitable floods	
9. Other	—		—	
10. Overall Rating	marginal		unsuitable	


Recommendations Based on this investigation, the lot is recommended for approval for installation of a septic tank system. System design should be based on a percolation rate of 60 min/in. Care should be taken on installation due to steepness of topography

See diagram on back

W. Edward Casavant
Soil Scientist

3/18/75
EHD 539

DIAGRAM OF PROPERTY

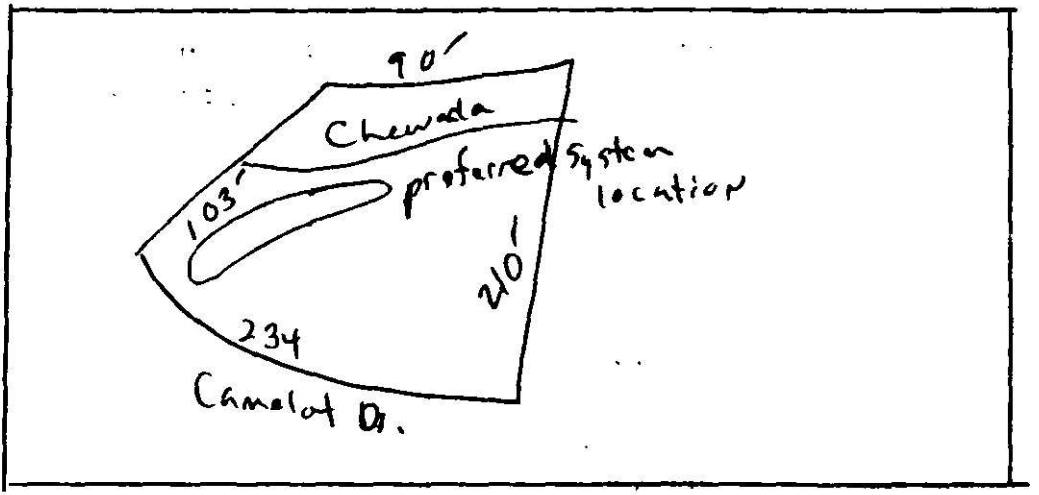

3/18/75

EMD 539

Serial No. 5719

PTR No. 6428

Date Issued 10/13/75

T C No. 227-095-26

Map Date -

Do Not Issue A Building Permit Based On This Form

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION


PERCOLATION TEST REPORT

NAME OF OWNER Camelot Inc. (LAST / FIRST / MIDDLE)

ADDRESS OF OWNER 1716 Johnston Building, Charlotte, N.C. ZIP 28281

LOCATION OF PROPERTY Camelot Drive (STREET OR COUNTY ROAD)

SUBDIVISION Camelot LOT NO 26 BLOCK NO. A

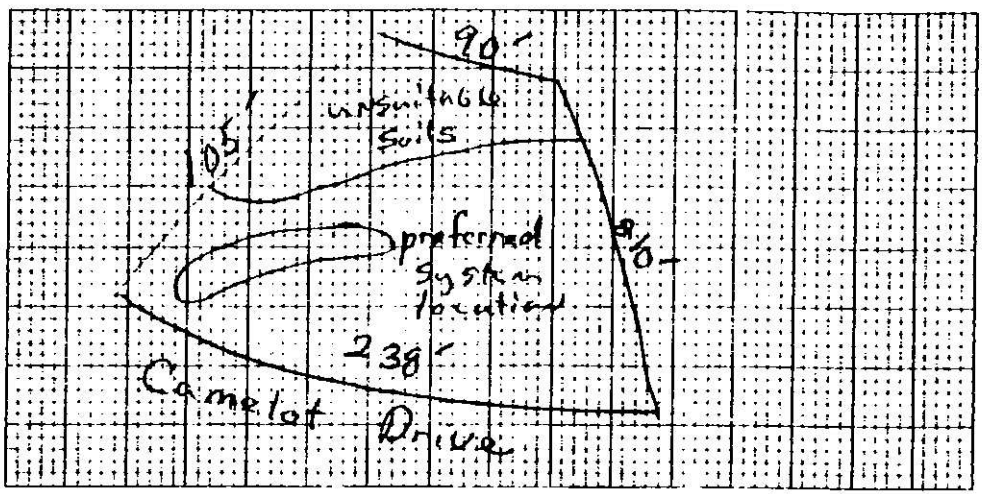

PLOT PLAN

This is to certify that a percolation test has been run and an on-site inspection made by the Mecklenburg County Health Department on the lot described above. The said test was conducted on that portion of the lot as indicated on above plot.

The percolation rate determined by the test was *60Min./In. The said lot is approved for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption effluent discharge subject to the following terms and conditions:

1. A permit to install, construct, alter, or repair the specific system shall be obtained from the Mecklenburg County Health Department prior to the beginning of any construction of buildings, or of the wastewater treatment system on the said lot.
2. The size of the septic tank wastewater treatment system which must be installed will be determined by the Health Department prior to installation based on the percolation rate obtained above, and on the size and type of building constructed thereon.
3. This approval is valid only if the system is installed in the immediate area where the percolation test was run.
4. This approval is void if any grading, filling, or construction (including the drilling of a well) is performed on the lot which, in the opinion of the Health Department, renders the area where the percolation test was run unsuitable for the installation, construction, alteration, and/or repair of such a system.

This approval is granted based on the laws of the State of North Carolina and the rules and regulations of the North Carolina State Board of Health and the Mecklenburg County Board of Health which were in effect on the date of issuance and is void if at any time in the future, prior to the completion of the system, these laws, rules, and regulations are changed such that this approval would not have been granted had the new or revised laws, rules, and regulations been in effect on the issue date.

*results determined by soil analysis

W. Edward Casewant
Soil Scientist

John R. Johnson
Director, Environmental Health Division or
Authorized Section Head

FORM NO. E-2-9-1-72

HEALTH DEPARTMENT'S COPY

Date Received 12/18/75

APT No. 6428

T. C. No. 277-095-26 42

Map Date

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

APPLICATION FOR PERCOLATION TEST

1) NAME OF OWNER Wightman & Company
(LAST / FIRST / MIDDLE)

2) ADDRESS OF OWNER P.O. Box 456 ZIP 28079

3) PHONE NO. Home 596 3489 Office 847 5596


4) LOCATION OF PROPERTY C. Banker Dr. (STREET OR COUNTY ROAD)

5) SUBDIVISION C Banker Dr LOT NO. 26 (1327) BLOCK NO. A

MAP BOOK NO 11 PAGE NO. 257

6) DEED REFERENCE: DEED BOOK PAGE NO.

Application is hereby made to the Mecklenburg County Health Department for the conduct of a percolation test and an on site inspection of the lot hereinabove described for the purpose of determining if the lot is suitable for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge.

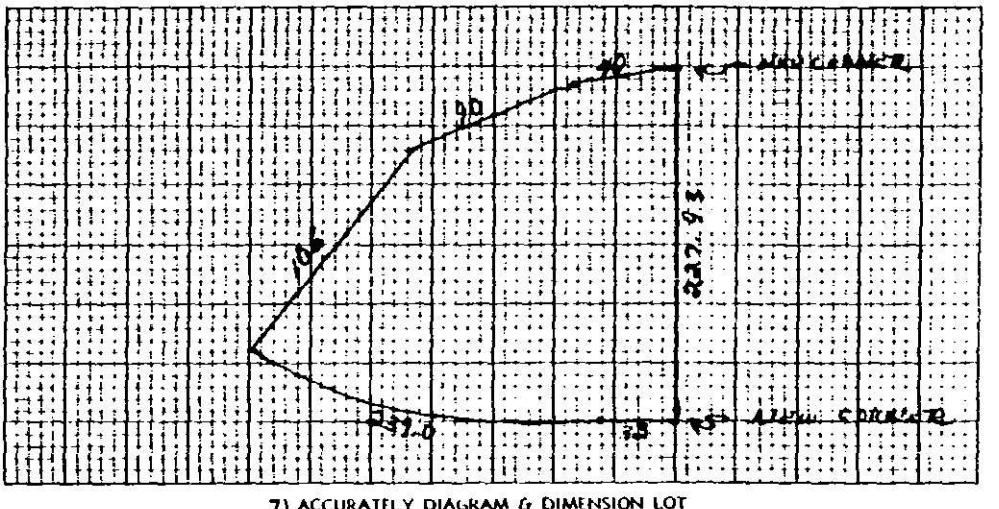

7) ACCURATELY DIAGRAM & DIMENSION LOT

by George E. Wightman Pres
OWNER

FORM NO. E1-11-3M-6-75

HEALTH DEPARTMENT'S COPY

SOIL INVESTIGATION REPORT

Date of Investigation December 15, 1975 APT NO. 6428

Owner Wightman & Company

Location of Property Camelot Drive lot no. 26 Block A

Soil Suitability Ratings TCN 227-095-26, 27

Soil Properties	Soil 1	Soil 2	Soil 3	Soil 4
1. Soil Series	Cecil	Cecil	Chewacla	
2. Soil Slope	acceptable 10-20%	unacceptable >30.%	—	
3. Soil Depth	acceptable >48"	same	—	
4. Soil Texture	acceptable clayey	same	—	
5. Soil Structure	acceptable subangular blocky	same	—	
6. Restrictive Horizons	—	—	—	
7. Soil Drainage	acceptable water table >60"	acceptable water table >60"	unacceptable water table <16" from surface	
8. Soil Permeability (Percolation Rate)	acceptable 60min/in	acceptable 60min/in	unacceptable poorly drained	
9. Other	—	—	unacceptable floods	
10. Overall Rating	acceptable	unacceptable	unacceptable	


Recommendations Based on this investigation the lot is recommended for approval for installation of a septic tank system. ~~Said~~ System design should be based on a percolation rate of 60min./in. Note! part of lot 27 has been incorporated into lot 26

See diagram on back

W. Edward Casavant
Soil Scientist

3/18/75
EHD 539

DIAGRAM OF PROPERTY

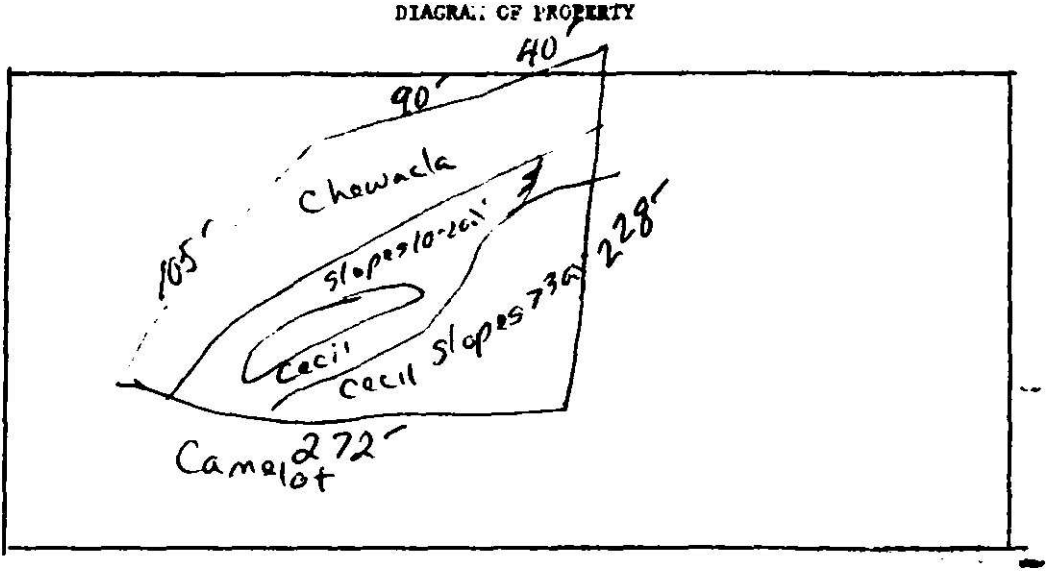

3/18/75

EMD 539
