

4645 MATTHEWS-MINT HILL RD

13537104

8/14/08

marliwr

Groundwater and Wastewater Services File Imaging Project
May 2007
Barcode Font = IDAutomationHC39M

CERTIFICATE OF COMPLETION/OPERATION PERMIT

HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON ST., SUITE 211
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 17558 DATE: 9-12-96

TC: 135-371-04 ☐ L ☐ CRT

SERIAL Nº 16786

Name of Owner John F. Hackenberg Juris.: _____

Address of Property 4645 Matthews-Mint Hill Rd

Inspection Data:

Tank Material existing

Total Length of Drainfield 280'

Number of Lines 5 in 1 @ 56'

Cover Depth 12"

Water Supply Source priv well

Distance to Water Source > 100'

Excavation Inspected 9.12

Tank(s) Inspected N/A

Wash Line Inspected N/A

High Water Alarm Inspected N/A

PLOT

Design 1996 alteration, Type III Inws 93-2, 840 sf, cecil-like CTR# 82

The undersigned has inspected the Septic Tank System described above, and certifies it has been

☐ installed or constructed ☑ altered or repaired

☐ in accordance with the permit issued ☐ as detailed in the plot above

and meets the provisions of 15A NCAC 18A. 1900, "Laws And Rules For Sewage Treatment and Disposal Systems" in effect on the date of issuance of the permit. This issuance of this

☐ Certificate of Completion ☑ Operation Permit

does not in any way guarantee that the system will operate properly or relieve any person now or hereafter owning, controlling, or using such system from any liability resulting from the failure of the system to operate properly. This document is issued subject to those restrictions and conditions shown on the permit(s) and the provisions of 15A NCAC 18A. 1990 in addition to those listed below under "COMMENTS." This document shall be null and void if any information contained in the application is untrue or if any additions are made to the property which would increase the requirements for said system.

Notice: Disturbance of the designated repair area may result in the suspension/revocation of this permit.

COMMENTS: Type III chambered system Inws 93-2 (alteration) 3 to a 4 bedroom house - alteration is designed to feed original bed first with spill over to new bed - flow can be adjusted with D-Boxes that are installed.

Jerry D. Thompson Jr. E.S.
Environmental Health Specialist

Mecklenburg County services are available without regard to ethnic origin, sex, or disability.

2400

INSTALLATION, CONSTRUCTION, ALTERATION, AND/OR REPAIR APPROVAL


HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON ST., SUITE 211
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 19558 DATE: 8-28-96

TC: 135-371-04 ☐ L

SERIAL Nº 16895

Permission is hereby given to _____ Install or Construct, ✓ Alter or Repair the individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge as specified herein at the described location. This permit is granted based upon the information supplied in the application dated 8-14-96. All work shall be completed on or before 9-28-96, after which date this permit shall be null and void. The system shall meet all of the construction requirements of 15A NCAC 18A. 1900 which are in effect on the date of the granting of this permit. A Certificate of Completion or an Operation Permit must be obtained from the Mecklenburg County Health Department before any system can be covered up or placed into service. The issuance of this permit does not in any way guarantee that the system anticipated to be constructed will operate properly, or relieve any person now or hereafter owning, controlling or using such system from any liability resulting from the failure of the system to operate properly.

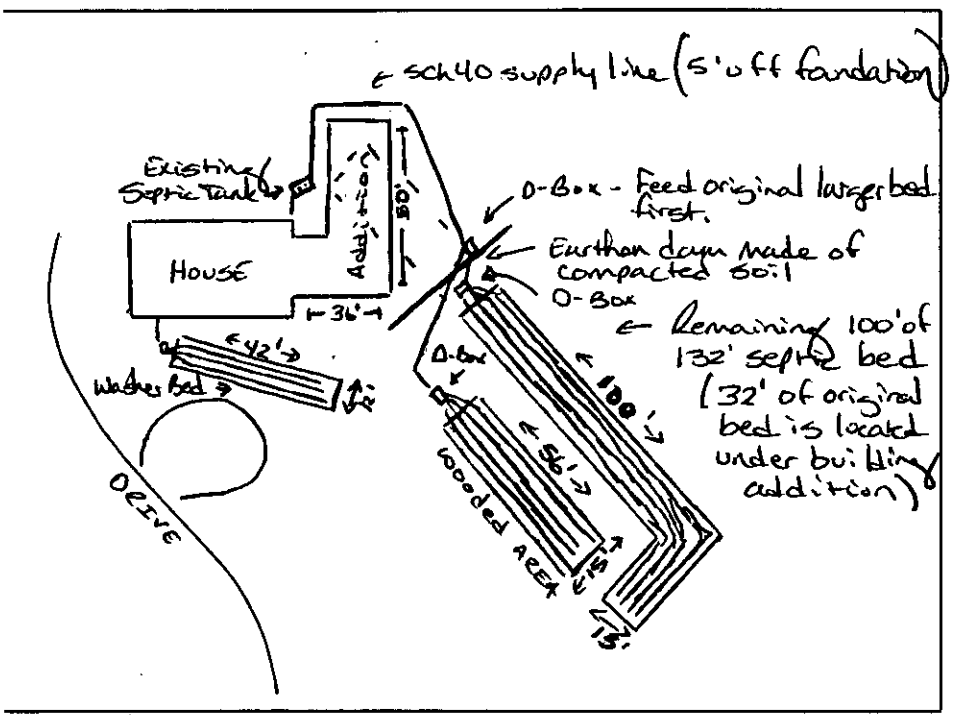

← To Matthews Mint Hill Rd. PLOT OF SYSTEM

Liquid Capacity of Septic Tank 1500 existing gallons

Liquid Capacity of Dosing Tank N/A gallons

Tank Construction PCC

Trench Depth 24" - as shallow as possible

Absorption and/or Nitrification Lines:

Trench Width 16 feet

Trench Walls Scored and Porous Yes

Total Line Length 280 feet

Number of Lines 5 in 1

Depth of Stone N/A inches

Distance from House 5 feet

Distance from Property Line 10 feet

Distance from Well 100 feet (Community)

NOTICE: This system shall not be installed while soils are in a wet condition.

NAME OF OWNER John F. Hackenberg

LOCATION OF PROPERTY 4645 Matthews Mint Hill Road

Comments: Type III g - any state approved system with a 25% reduction in line length. 4 bedroom house with a 1 bedroom addition - cut off 30' of septic bed - re-route supply line - install 15'x56' innovative bed feeding original system first.

Ramy B. Thompson, J. E.H.S.
Environmental Health Specialist

WHITE - HEALTH DEPARTMENT's COPY • CANARY - E.H.S. COPY • PINK - OWNER OR AGENT's COPY

INSTALLATION, CONSTRUCTION, ALTERATION, AND/OR REPAIR APPROVAL


HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON ST., SUITE 211
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 17558 DATE: 8-28-96

TC: 135-371-04 ☐ L

SERIAL NO 16895

Permission is hereby given to _____ Install or Construct, ✓ Alter or Repair the individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge as specified herein at the described location. This permit is granted based upon the information supplied in the application dated 8-14-96. All work shall be completed on or before 9-28-96, after which date this permit shall be null and void. The system shall meet all of the construction requirements of 15A NCAC 18A. 1900 which are in effect on the date of the granting of this permit. A Certificate of Completion or an Operation Permit must be obtained from the Mecklenburg County Health Department before any system can be covered up or placed into service. The issuance of this permit does not in any way guarantee that the system anticipated to be constructed will operate properly, or relieve any person now or hereafter owning, controlling or using such system from any liability resulting from the failure of the system to operate properly.

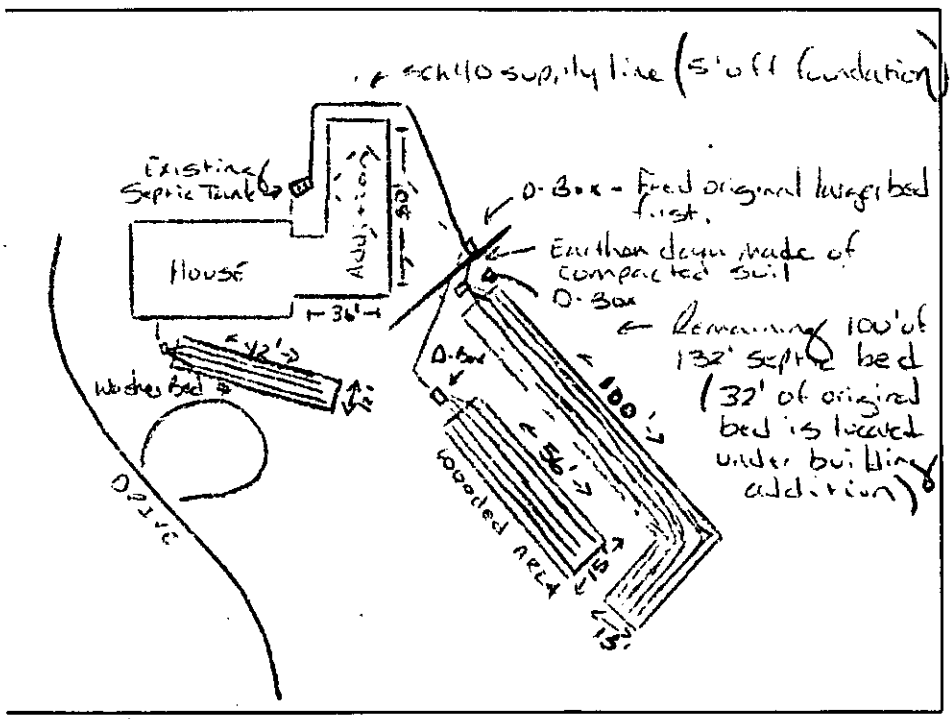

To Matthews/Mint Hill Rd.

PLOT OF SYSTEM

Liquid Capacity of Septic Tank 1500 existing gallons

Liquid Capacity of Dosing Tank N/A gallons

Tank Construction RC

Trench Depth 24" - as shallow as possible

Absorption and/or Nitrification Lines:

Trench Width 15 feet

Trench Walls Scored and Porous Yes

Total Line Length 280 feet

Number of Lines 5 in 1

Depth of Stone N/A inches

Distance from House 5 feet

Distance from Property Line 10 feet

Distance from Well 100 feet (Community)

NOTICE: This system shall not be installed while soils are in a wet condition.

NAME OF OWNER John F. Hackenberg

LOCATION OF PROPERTY 4645 Matthews Mint Hill Road

Comments: Type III-5 - only state approved systems with a 25% reduction in line length. 4 bedroom house with a 1 bedroom addition - cut off 30' of septic bed - re-route supply line - install 15'x5' innovative bed feeding original system first.

Kenny B. Whitaker R.E.H.S.
Environmental Health Specialist

WHITE - HEALTH DEPARTMENT's COPY • CANARY - E.H.S. COPY • PINK - OWNER OR AGENT's COPY

Ck # 4745

FEE: 200.00 **AUTHORIZATION FOR WASTEWATER SYSTEM CONSTRUCTION**
DATE: 8-14-96 **VOID SIXTY (60) MONTHS FROM DATE OF ISSUANCE**

DATE: 8-28-96 **PERMIT NO:** 17558
PARCEL NO: 135-371-04

JOB LOCATION ADDRESS: 4645 Matthews - Mint Hill Rd
PROPERTY OWNER: John F. Hackenberg
BUILDING CONTRACTOR: Dave Scholl
SUBDIVISION NAME: N/A
AUTHORIZATION ISSUED BY: Larry B. Thompson Jr. LS **DATE:** 8-28-96
DEHNR/AUTHORIZED AGENT

AUTHORIZATION CONDITIONS

1. WASTEWATER SYSTEM CONSTRUCTION AND INSTALLATION MUST MEET ALL CONDITIONS AND SPECIFICATIONS AS SET FORTH IN IMPROVEMENT PERMIT NO. 17558, AND THE ATTACHED SITE PLAN WITH SYSTEM DETAILS. CONSTRUCTION AND INSTALLATION MUST ALSO MEET ALL REQUIREMENTS SET FORTH IN THE RULES GOVERNING SANITARY SEWAGE COLLECTION, TREATMENT, AND DISPOSAL AND ANY OTHER APPLICABLE RULES AND LAWS.

2. AN INSTALLATION, CONSTRUCTION, ALTERATION AND/OR REPAIR APPROVAL MUST BE SECURED **PRIOR** TO INSTALLATION OF THE SEPTIC TANK SYSTEM. THE INSTALLER OF THE SYSTEM SHALL BE A REGISTERED SEPTIC TANK CONTRACTOR WITH MECKLENBURG COUNTY HEALTH DEPARTMENT.

3. ANY ALTERATION IN SITE OR SOIL CONDITIONS (INCLUDING LOCATION OF STRUCTURES AND APPURTENANCES) OR MODIFICATION IN USE, DESIGN WASTEWATER FLOW, OR WASTEWATER CHARACTERISTICS AS SPECIFIED IN THE ASSOCIATED IMPROVEMENT PERMIT AND APPLICATION, MAY SUBJECT THIS AUTHORIZATION AND ASSOCIATED PERMIT(S) TO REVOCATION.

4. OTHER CONDITIONS: _____

OWNER CERTIFICATION

I CERTIFY THAT THERE HAVE BEEN NO ALTERATIONS IN SITE OR SOIL CONDITIONS OR MODIFICATIONS TO FACILITY, WASTEWATER FLOW, OR WASTEWATER CHARACTERISTICS FROM THOSE SPECIFIED IN THE ORIGINAL APPLICATION OR ASSOCIATED IMPROVEMENT PERMIT UNLESS AUTHORIZED IN WRITING BY THE MECKLENBURG COUNTY HEALTH DEPARTMENT. I ALSO UNDERSTAND THAT ANY SUCH ALTERATIONS, MODIFICATIONS, OR FALSE INFORMATION ARE GROUNDS FOR REVOCATION OF PERMITS AND AUTHORIZATION TO CONSTRUCT.

David D. Scholl - Contractor 9-11-96
SIGNATURE OF OWNER/OWNER'S REPRESENTATIVE DATE

406 DIGITAL page → 513-0824

FEE: 200.00 CK# 4775 DATE: 8/14/96

APPLICATION FOR IMPROVEMENT PERMIT FOR RESIDENTIAL SITE INDIVIDUAL WATER AND WASTEWATER SYSTEMS PROGRAM

Contractor DAVE SCHOLL 364-1101 [ ] CRT

TYPE APPLICATION: ___ NEW SYSTEM ✓ EXPANSION/ ALTERATION OF EXISTING SYSTEM ___ REPAIR OF EXISTING SYSTEM

NORTH CAROLINA
DEPARTMENT OF ENVIRONMENT,
HEALTH, AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

FILE #: 17558

PROPERTY INFORMATION (FROM ENGINEERING FORM) FOR JOB LOCATION:

TAX/PARCEL NUMBER: 135-371-04

STREET ADDRESS: 4645 Matthews Mint Hill Rd

SUBDIVISION OR MOBILE HOME PARK NAME:

LOT NUMBER:

TYPE OF BUILDING (CHECK ONE):

___ SINGLE MOBILE HOME(S)
___ DOUBLE WIDE (D)
✓ HOUSE (H)
___ MODULAR HOME (M)
___ MULTIPLE FAMILY (U)
___ OTHER (O)

TOWNSHIP (CHECK ONE):

___ 0 MECKLENBURG
___ 1 CHARLOTTE
___ 2 DAVIDSON
___ 3 CORNELIUS
___ 4 PINEVILLE
✓ 5 MATTHEWS
___ 6 HUNTERSVILLE
___ 7 MINT HILL

HEATED SQUARE FOOTAGE:

NUMBER OF BEDROOMS: 4 | NUMBER OF OCCUPANTS: 2

CLOSING DATE _____

FOUNDATION FOR RESIDENCE:

___ WITHOUT BASEMENT ON SLAB
✓ CRAWL SPACE
___ WITH BASEMENT /PLUMBING
___ WITH BASEMENT /NO PLUMBING

IF EXPANSION/ALTERATION OF EXISTING SYSTEM, DESCRIBE THE PROPOSED BUILDING ADDITION: Expansion Rm

New wing addition to existing house | BRm | Bath | Lndry Rm

WILL THERE BE A HOME BUSINESS IN THE RESIDENCE: ___ YES ✓ NO TYPE: _____

WATER SUPPLY (CHECK ONE):

✓ COMMUNITY (C)
___ MUNICIPAL (M)
___ PRIVATE WELL (P)
___ SHARED WELL (S)
___ OTHER 'SPRINGS' (O)

IF ANY OF THE FOLLOWING ARE LOCATED ON THE PROPERTY, PLEASE SHOW LOCATION ON PLAT:

BURIED CABLES, LANDFILLS, STUMPHOLES ✓ YES ___ NO
EXISTING WASTEWATER SYSTEMS ✓ YES ___ NO
EASTMENTS OR RIGHT-OF-WAYS ___ YES ✓ NO
WELL, SPRINGS OR WATERLINES ✓ YES ___ NO
DESIGNATED WETLANDS ___ YES ✓ NO


PROPERTY OWNER:	LEGAL AGENT FOR PROPERTY OWNER, IF APPLICABLE:
NAME: Hackenbag John F. (LAST) (FIRST) (MI)	NAME: (LAST) (FIRST) (MI)
ADDRESS: 4645 Matthews Mint Hill Rd.	DAYTIME PHONE: ( ) —
CITY: Matthews STATE: NC ZIP: 28105	
DAYTIME PHONE: 704 545-7362	

WHAT DATE WAS THE PROPERTY ORIGINALLY DEEDED AND RECORDED? August 1982

An Improvement Permit is subject to suspension or revocation if site plans or the intended use change or if information submitted in this application is falsified or changed. The undersigned, owner, or legal agent for the owner, of the property described above as the "Job Location" has read the foregoing application, acknowledges that the contents of same are true, and authorizes agents of the Mecklenburg County Health Department to enter onto the property for the purpose of processing this request.

SIGNED: John F. Hackenbag DATE: 8-14-96

MECKLENBURG COUNTY HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
c/o HAL MARSHALL CTR., SUITE 211, 700 N. TRYON ST., CHARLOTTE, N.C. 28202., (704) 336-5102

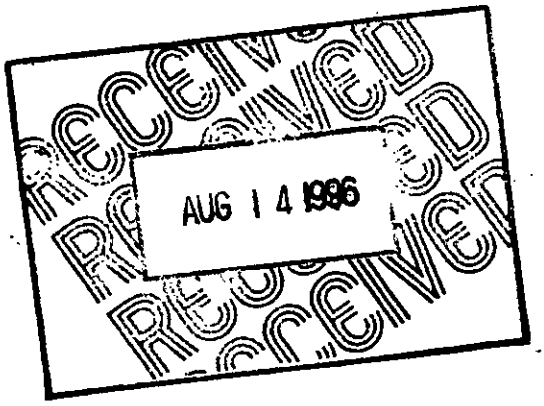
RECEIVED
AUG 14 1996
RECEIVED

Permit Number: 17558 Tax Number: 135-371-04

- The IMPROVEMENT PERMIT is subject to revocation if site plans or the intended use change. There is to be NO grading, filling or disturbance of the soil in the area of the septic tank system or repair area.
- CONSTRUCTION AUTHORIZATION must be obtained prior to receiving a Building Permit. The Construction Authorization is NOT transferable. Do not clear, grade, fill or disturb soil prior to obtaining a Construction Authorization.
- Domestic-type wastewater only. No industrial process wastewater may be discharged into the system.

Basement	___ Yes	✓ No	___ Partial Basement	
Type Primary Wastewater System Type (circle one): I (II) III IV V VI	✓ Conventional ___ Prefabricated, permeable block panel system ___ Shallow Placed Conventional	___ Low Pressure Pipe ___ Large Diameter Pipe ___ Fill ___ Other	___ Innovative or Experimental: ___ IWWS-93-1 ___ IWWS-93-2 ___ IWWS-94-1	
___ Long-term acceptance rate	460 Max gallons/day wastewater flow original	___ Absorption Area (sq ft)	___ Trench spacing (min. on centers)	
N/A (community) Serviced by private well	1500 Gallon septic tank	___ Total trench length (ft)	___ Maximum trench depth (At least 12" of provisionally suitable soil must remain between trench bottom and unsuitable soil conditions)	
4 Bedrooms in residence adding 5th	N/A Gallon pump tank	___ Depth of stone		
Any surface waters present:	Type:	Minimum separation distance:		
Site modifications required:				
Additional Conditions: System Alteration - adding bedroom / addition will be over a portion of septic drainfield. Cutting off bed underneath building addition - re-route supply line around addition - add 15'w x 56'2 x 24"deep innovative alteration feeding original bed first				
Repair Area System Type Type (circle one): I II (III) IV V VI	___ Conventional ___ Prefabricated, permeable block panel system ___ Shallow Placed Conventional	___ Low Pressure Pipe ___ Large Diameter Pipe ___ Fill ___ Other	✓ Innovative or Experimental: ___ IWWS-93-1 ___ IWWS-93-2 ___ IWWS-94-1	
640 Absorption Area (Sq ft) 280 Total Trench Length (Ft)	N/A Depth of Stone Trench	N/A Trench spacing (min. on centers)	24" Maximum Trench Depth	
For existing system, enter the year originally installed: 1982				

The undersigned, an authorized agent of the MECKLENBURG COUNTY HEALTH DEPARTMENT, certifies that the Department has approved the Request for the Job Location contained in this document. This approval is granted in accordance with the provisions of Laws and Rules For Sewage, Treatment and Disposal in effect at the time of issuance of the permit and is subject to the following provisions:

- No work shall be conducted on the septic tank system until an Installation, Construction, Alteration and/or Repair Approval is granted by this Department
- This Improvement permit is transferable.

Larry B. Thompson Jr., L.S. 8-28-96
DEHNR Authorized Agent Date

David D. Scholl contractor 9-11-96
Owner/Agent Signature Date

MECKLENBURG COUNTY
HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
c/o HAL MARSHALL CTR.
SUITE 211
700 N. TRYON ST.
CHARLOTTE, N.C. 28202.
(704) 336-5102

NORTH CAROLINA DEPARTMENT OF
ENVIRONMENTAL, HEALTH,
AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

IWWS-100195


PROPOSED PLOT PLAN

HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON STREET
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 17558

TC: _____

Draw in and name all roads adjoining the property. Draw in and accurately dimension the lot concerned. Accurately indicate property boundaries proposed and/or existing structures and driveways, underground utilities, and wells and springs within 100 feet of the proposed building or drainfield.

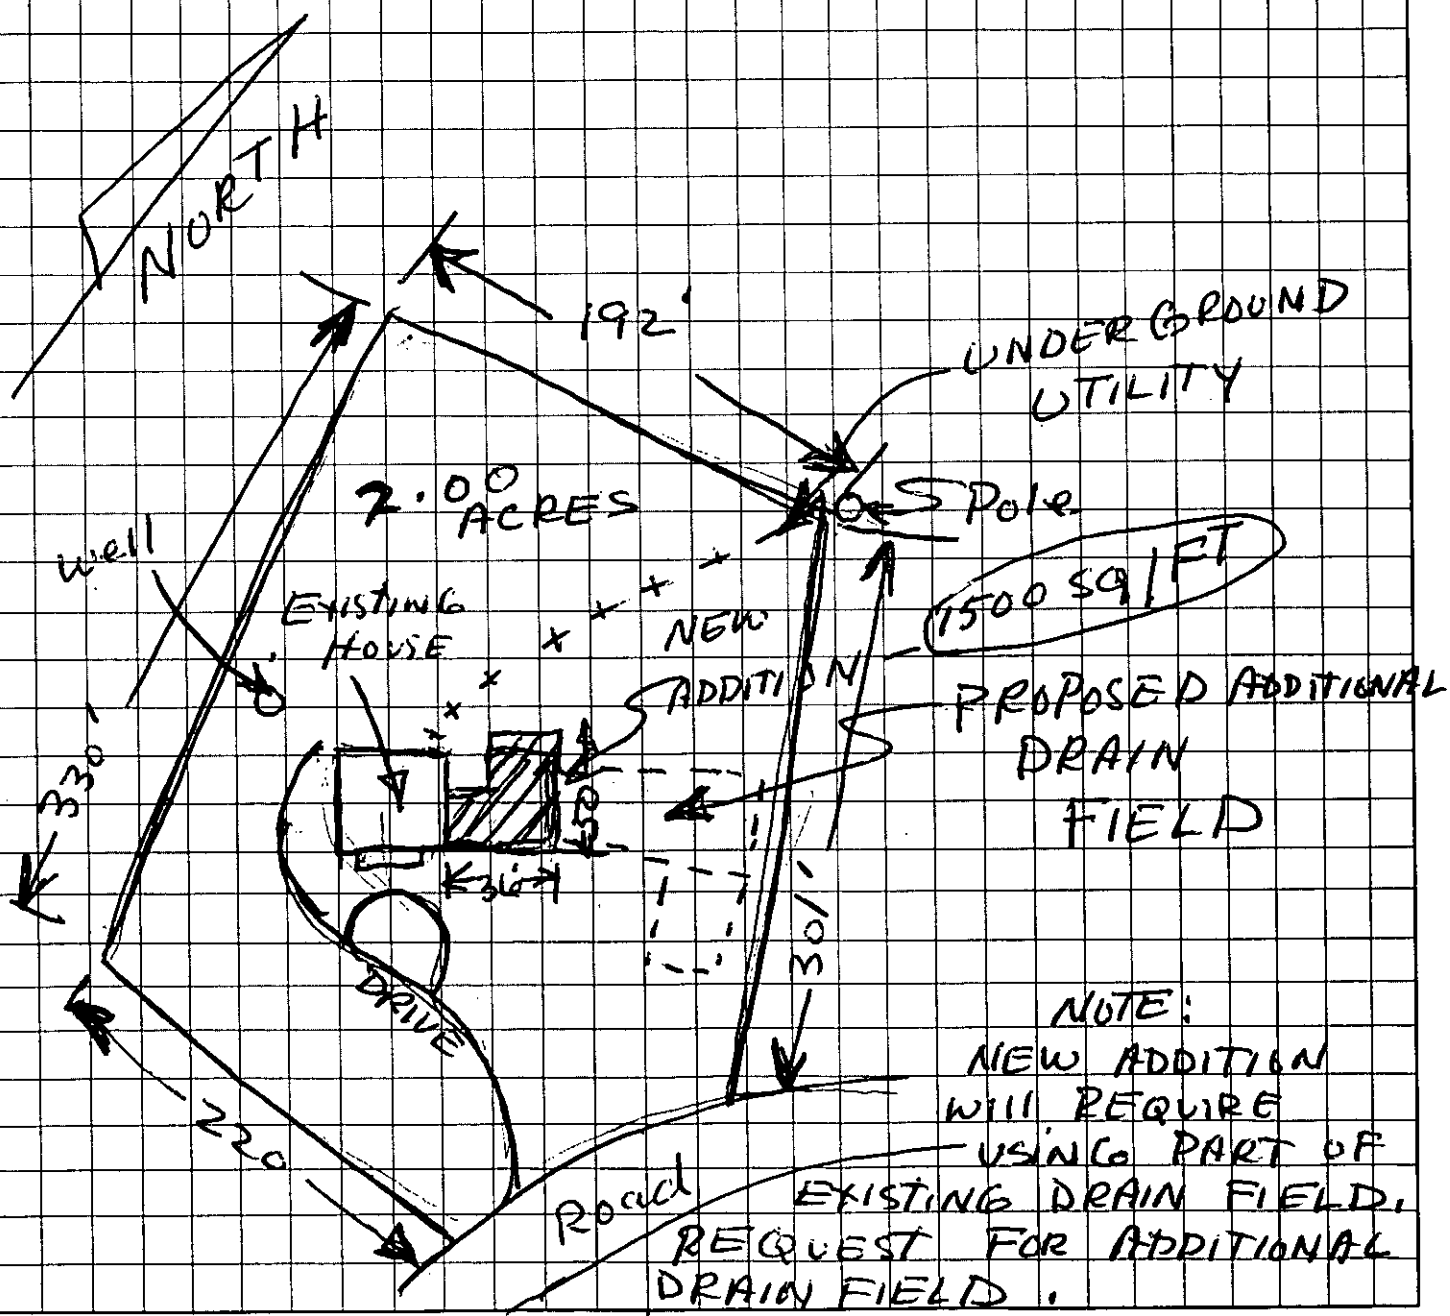

John F. Hockenberry
OWNER/AGENT SIGNATURE

DATE 8-14-96

APPROVAL DATE _____

White - Health Department's Copy Canary - E.H.S. Copy Pink - Owner's Copy
