B

Date Received 8 2 73

APT No 6782

T C No _____

Map Date _____

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

APPLICATION FOR PERCOLATION TEST

1) NAME OF OWNER Williams, JR. (LAST) James (FIRST) HARLEY (MIDDLE)

2) ADDRESS OF OWNER 2415 Midland Ave. ZIP 28208

3) PHONE NO. Home 394-2933 Office 399-0486


4) LOCATION OF PROPERTY Lot 19, Pine Oaks Drive (off Beam Rd.) (STREET OR COUNTY ROAD)

5) SUBDIVISION Wippoorwill Hills LOT NO 19 BLOCK NO. _____

MAP BOOK NO 7 PAGE NO 271

6) DEED REFERENCE DEED BOOK 2279 PAGE NO 539

Application is hereby made to the Mecklenburg County Health Department for the conduct of a percolation test and an on site inspection of the lot hereinabove described for the purpose of determining if the lot is suitable for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge

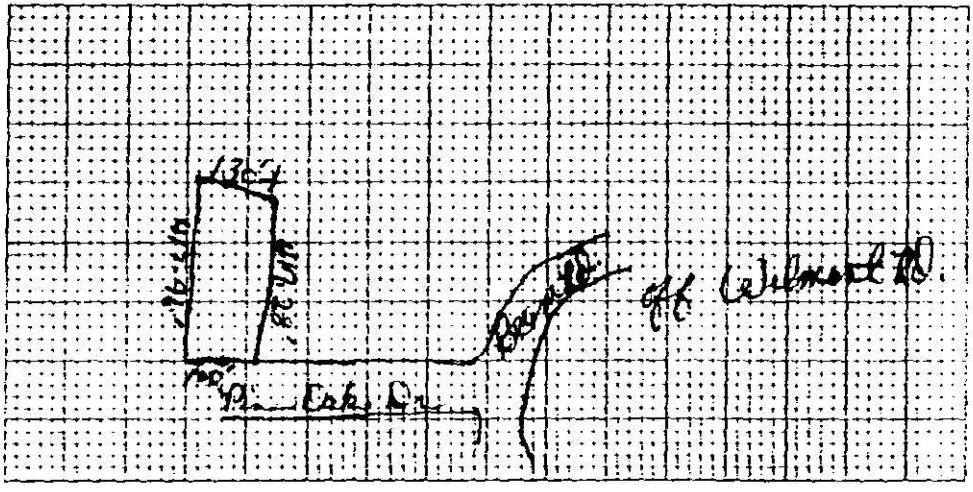

7) ACCURATELY DIAGRAM & DIMENSION LOT

Mrs James Williams
OWNER

FORM NO E-1-8-1-72

HEALTH DEPARTMENT'S COPY

MECKLENBURG COUNTY
Department of Public Health
1200 Blythe Boulevard
Charlotte, North Carolina 28203

Telephone 374-2113

Date Issued
1. August [illegible], 1973
2. _____
3. _____

SITE DISAPPROVAL REPORT
INDIVIDUAL SEPTIC TANK SYSTEM WITH SUBSURFACE,
SOIL ABSORPTION, EFFLUENT DISCHARGE

SDR No. 9732
T.C. No. _____

NAME OF OWNER [illegible] James Parler

ADDRESS OF OWNER [illegible] ZIP 28208

LOCATION OF LOT [illegible]

The lot described above has been disapproved for the installation of an individual septic tank system with subsurface, soil absorption, effluent discharge due to the following:

FAILURE TO PASS PERCOLATION TEST (60 minutes per inch or less)

	Test No.	Date of Test	Percolation Rate
X	1.	[illegible]	[illegible] min/in
____	2.	_____	_____ min/in
____	3.	_____	_____ min/in

____ ON SITE INSPECTION REVEALED LOT TO BE UNSUITABLE FOR THE FOLLOWING REASON(S) _____

_____

_____

_____

[illegible]
Environmentalist

(Stencil No.)
EHD 398

FORM NO.
E-19-8-14-70

MECKLENBURG COUNTY HEALTH DEPARTMENT
INTER-OFFICE COMMUNICATION

DATE: August 10, 1973

TO: Luther Bridgeman
Environmentalist

FROM: W. Everette Lynn, Jr. W.E.L.
Soil Scientist

SUBJECT: Pine Oaks Drive, Lot 19
APT #6782 (Williams)

8-8-73 Soils on the rear of the lot (away from Pine Oaks Drive) were of the Mecklenburg and Enon series. These soils have very plastic and sticky clay subsoils which contain swelling clay minerals. This results in inadequately slow perc. and permeability. The perc. test was run in this area. A small area of Cecil was located immediately on the front of the lot. It is recommended that another perc. be conducted in this area of Cecil so that there is no question about system location.

Serial No. 3535

PTR No. 6782

T C No 141-053-01

Map Date 5-11-73

Date Issued August 24, 1973

Do Not Issue A Building Permit Based On This Form

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION


PERCOLATION TEST REPORT

NAME OF OWNER Williams, Jr. (LAST) James (FIRST) Harley (MIDDLE)

ADDRESS OF OWNER 2415 Midland Avenue ZIP 28208

LOCATION OF PROPERTY Pine Oaks Drive (STREET OR COUNTY ROAD)

SUBDIVISION Whippoorwill Hills LOT NO 19 BLOCK NO.

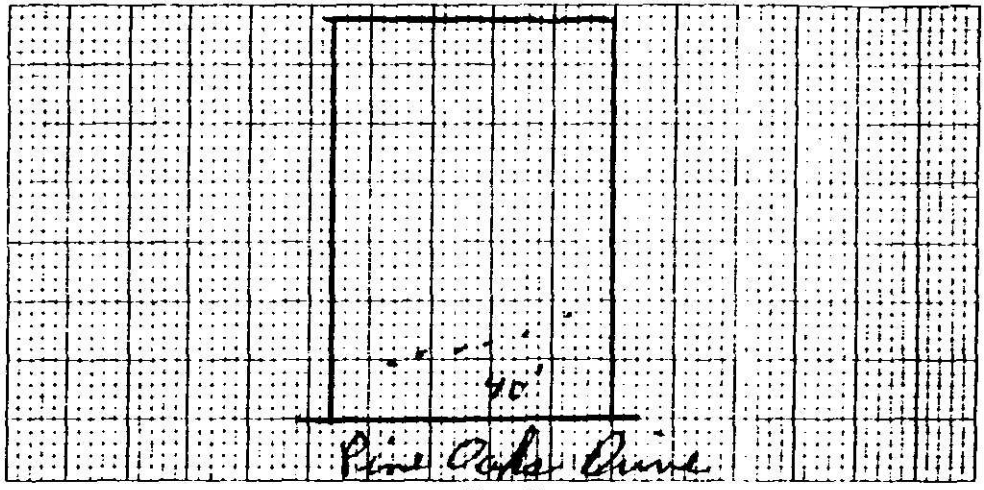

PLOT PLAN

This is to certify that a percolation test has been run and an on site inspection made by the Mecklenburg County Health Department on the lot described above. The said test was conducted on that portion of the lot as indicated on above plot

The percolation rate determined by the test was 60 min/in The said lot is approved for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption effluent discharge subject to the following terms and conditions

1. A permit to install, construct after, or repair the specific system shall be obtained from the Mecklenburg County Health Department prior to the beginning of any construction of buildings, or of the wastewater treatment system on the said lot.
2. The size of the septic tank wastewater teratment system which must be installed will be determined by the Health Department prior to installation based on the percolation rate obtained above and on the size and type of building constructed thereon
3. This approval is valid only if the system is installed in the immediate area where the percolation test was run.
4. This approval is void if any grading, filling, or construction (including the drilling of a well) is performed on the lot which, in the opinion of the Health Department, renders the area where the percolation test was run unsuitable for the installation, construction, alteration, and/or repair of such a system

This approval is granted based on the laws of the State of North Carolina and the rules and regulations of the North Carolina State Board of Health and the Mecklenburg County Board of Health which were in effect on the date of issuance and is void if at any time in the future, prior to the completion of the system, these laws, rules, and regulations are changed such that this approval would not have been granted had the new or revised laws, rules, and regulations been in effect on the issuedate

John R Robinson

Director, Environmental Health Division or Authorized Section Head

FORM NO E-2 4 1-71

HEALTH DEPARTMENT'S COPY
