

11201 COBLE RD

13934105

4/14/08

marliwr

Groundwater and Wastewater Services File Imaging Project
May 2007
Barcode Font = IDAutomationHC39M

CERTIFICATE OF COMPLETION/OPERATION PERMIT

HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
1200 BLYTHE BOULEVARD
CHARLOTTE, NC 28203
PHONE (704) 376-4603

FILE: 884 A DATE: 5-19-94

TC: 139-341-05 ☐ L ☐ CRT

SERIAL Nº 15400

Name of Owner Fred Saunders / Performance Investment Brokerage Juris.:

Address of Property 11201 Cobb Rd.

Inspection Data:

Tank Material PCC

Total Length of Drainfield 400'

Number of Lines 5 @ 80'

Cover Depth 6"-16"

Water Supply Source well

Distance to Water Source 74'

Excavation Inspected 5-19-94

Tank(s) Inspected 5-19-94

Wash Line Inspected —

High Water Alarm Inspected —

PLOT

Design: 1994, conv, 1500gst, 1200sqft, 12" stone georgeville CTR# RCS 90

The undersigned has inspected the Septic Tank System described above, and certifies it has been

☒ installed or constructed ☐ altered or repaired

☒ in accordance with the permit issued ☐ as detailed in the plot above

and meets the provisions of 10 NCAC 10A .1900, "Laws And Rules For Sanitary Sewage Collection, Treatment, And Disposal" in effect on the date of issuance of the permit. The issuance of this

☒ Certificate of Completion ☐ Operation Permit

does not in any way guarantee that the system will operate properly or relieve any person now or hereafter owning, controlling, or using such system from any liability resulting from the failure of the system to operate properly. This document is issued subject to those restrictions and conditions shown on the permit(s) and the provisions of ~~10 NCAC 10A .1900~~ 15A 18A in addition to those listed below under "COMMENTS." This document shall be null and void if any information contained in the application is untrue or if any additions are made to the property which would increase the requirements for said system.

COMMENTS: 3 bedroom. Do not set any bldg foundation within 5' of any part of septic tank system. Type II

T. Walker for S. Daniel
5/23/94

Susan Saleeby
Environmentalist

Mecklenburg County services are available without regard to ethnic origin, sex, or disability.

Called 5/16/94 Mut 5/16/94 APPROVAL

INSTALLATION, CONSTRUCTION, ALTERATION, AND/OR REPAIR PERMIT


HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
1200 BLYTHE BOULEVARD
CHARLOTTE, NC 28203
PHONE (704) 376-4603

FILE: 884A DATE: 5/16/94

TC: 139-341-05 ☐ L

SERIAL Nº 15996

Permission is hereby given to ✓ Install or Construct, _____ Alter or Repair the individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge as specified herein at the described location. This permit is granted based upon the information supplied in the application dated 9-16-93. All work shall be completed on or before 5/30/94, after which date this permit shall be null and void. The system shall meet all of the construction requirements of 10 NCAC 10A .1900 which are in effect on the date of the granting of this permit. A Certificate of Completion or an Operation Permit must be obtained from the Mecklenburg County Health Department before any system can be covered up or placed into service. The issuance of this permit does not in any way guarantee that the system anticipated to be constructed will operate properly, or relieve any person now or hereafter owning, controlling or using such system from any liability resulting from the failure of the system to operate properly.

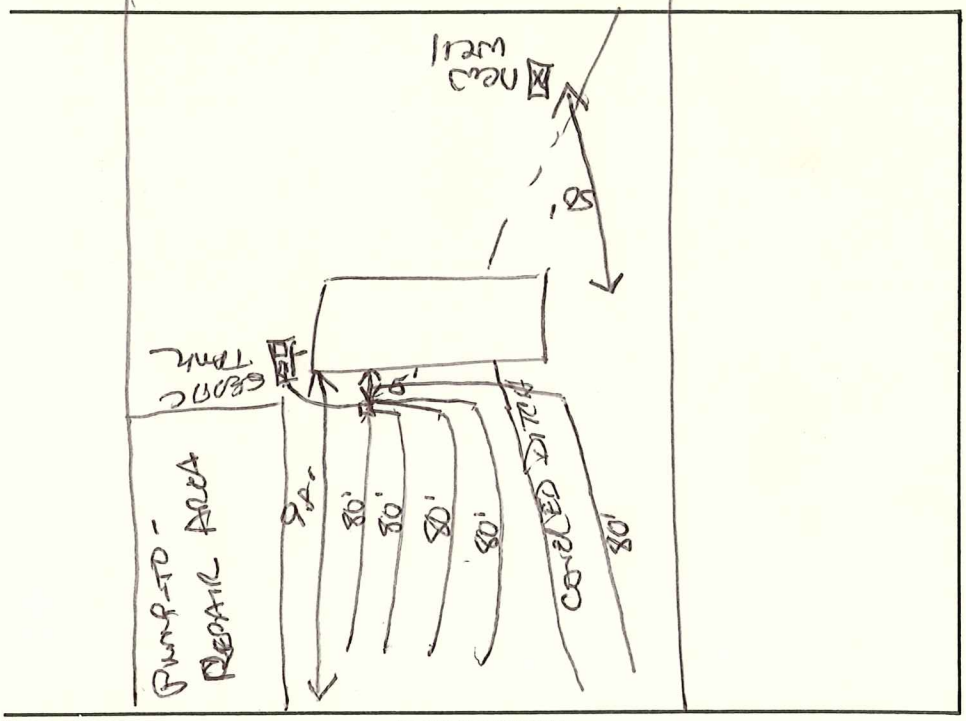

PLOT OF SYSTEM

Liquid Capacity of Septic Tank 1500 gallons

Liquid Capacity of Dosing Tank — gallons

Tank Construction PCC

Absorption and/or Nitrification Lines:

Trench Width 3 feet

Total Line Length 400 feet

Number of Lines 5

Depth of Stone 12" inches

Distance from House 5' feet

Distance from Property Line 10' feet

Distance from Well 50' feet

NAME OF OWNER Fred Saunders / Performance Investment Brokerage

LOCATION OF PROPERTY 11201 Coble Rd.

Comments: maximum trench 28", 6"-16" trench cover, well shall be 50' to 100' from any part of the septic tank system. Keep off covered ditch. Pump-to-conventional repair. System moved to accomodate well installation.

P. Walker for J Daniel 5/19/94
Division or Section Head

Jonathan Powell, R.S.
Environmentalist

* If this permit is for the installation or construction of a new system, it must be signed by the division or a section head of the Mecklenburg County Health Department in order to be valid. Only the signature of the Environmentalist is required where an existing system is being altered or repaired.

INSTALLATION, CONSTRUCTION, ALTERATION, AND/OR REPAIR PERMIT


HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
1200 BLYTHE BOULEVARD
CHARLOTTE, NC 28203
PHONE (704) 376-4603

FILE: 884 A DATE: 9-16-93

TC: 139-341-05 ☐ L

SERIAL № 15592

Permission is hereby given to X Install or Construct, _____ Alter or Repair the individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge as specified herein at the described location. This permit is granted based upon the information supplied in the application dated 9-16-93. All work shall be completed on or before 11-1-93, after which date this permit shall be null and void. The system shall meet all of the construction requirements of 10 NCAC 10A .1900 which are in effect on the date of the granting of this permit. A Certificate of Completion or an Operation Permit must be obtained from the Mecklenburg County Health Department before any system can be covered up or placed into service. The issuance of this permit does not in any way guarantee that the system anticipated to be constructed will operate properly, or relieve any person now or hereafter owning, controlling or using such system from any liability resulting from the failure of the system to operate properly.

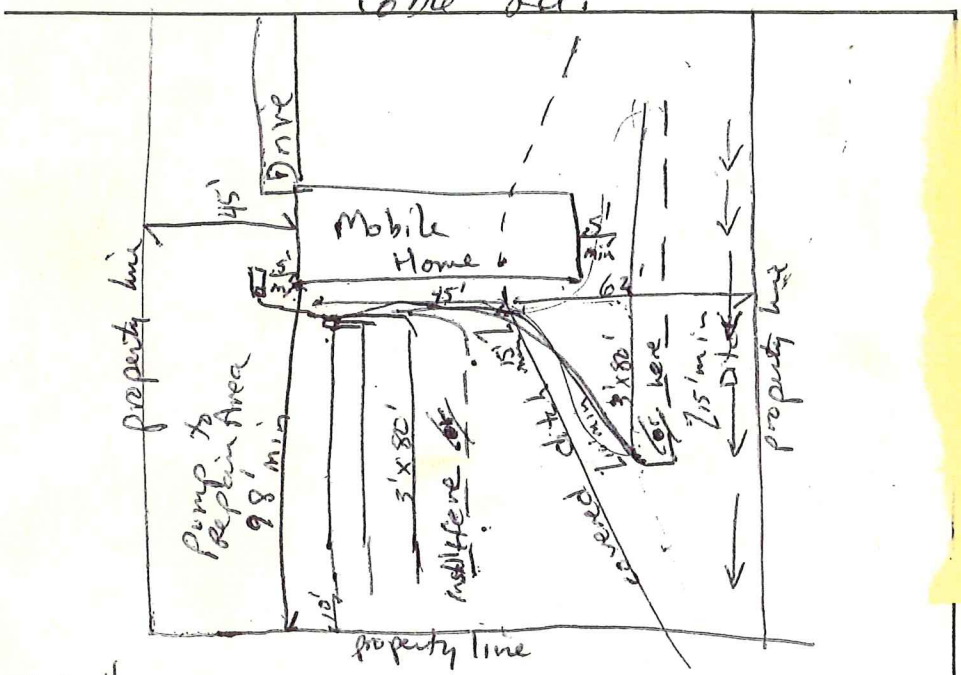

PLOT OF SYSTEM

This file is with the microfiche bunch - Sue

_____ gallons

_____ gallons

_____

...es:

_____ feet

_____ feet

...'each

_____ inches

_____ feet

Property Line 10' min feet

Distance from Well 50' min feet preferably 100' min (well not in yet)

trench bottom max 28"

min 9' on center

6"-16" soil cover

NAME OF OWNER Fred Sanders / Performance Investment Brokerage Inc

LOCATION OF PROPERTY 11201 Cobb Rd.

Comments: Pump to Repair Area. Keep well min 50', preferably 100', from any part of septic system. Set mobile home to accomodate septic tank system. Keep off of covered ditch as shown. Some grading was done on lot.

Judy J. Rizer for S David
Division or Section Head

Susan Gatewood
Environmentalist

* If this permit is for the installation or construction of a new system, it must be signed by the division or a section head of the Mecklenburg County Health Department in order to be valid. Only the signature of the Environmentalist is required where an existing system is being altered or repaired.

WHITE - HEALTH DEPARTMENT'S COPY • CANARY - ENVIRONMENTALIST'S COPY • PINK - OWNER OR AGENT'S COPY

INSTALLATION, CONSTRUCTION, ALTERATION, AND/OR REPAIR PERMIT


HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
1200 BLYTHE BOULEVARD
CHARLOTTE, NC 28203
PHONE (704) 376-4603

FILE: 884 A DATE: 9-16-93

TC: 139-341-05 ☐ L

SERIAL Nº 15592

Permission is hereby given to X Install or Construct, _____ Alter or Repair the individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge as specified herein at the described location. This permit is granted based upon the information supplied in the application dated 9-16-93. All work shall be completed on or before 11-1-93, after which date this permit shall be null and void. The system shall meet all of the construction requirements of 10 NCAC 10A .1900 which are in effect on the date of the granting of this permit. A Certificate of Completion or an Operation Permit must be obtained from the Mecklenburg County Health Department before any system can be covered up or placed into service. The issuance of this permit does not in any way guarantee that the system anticipated to be constructed will operate properly, or relieve any person now or hereafter owning, controlling or using such system from any liability resulting from the failure of the system to operate properly.

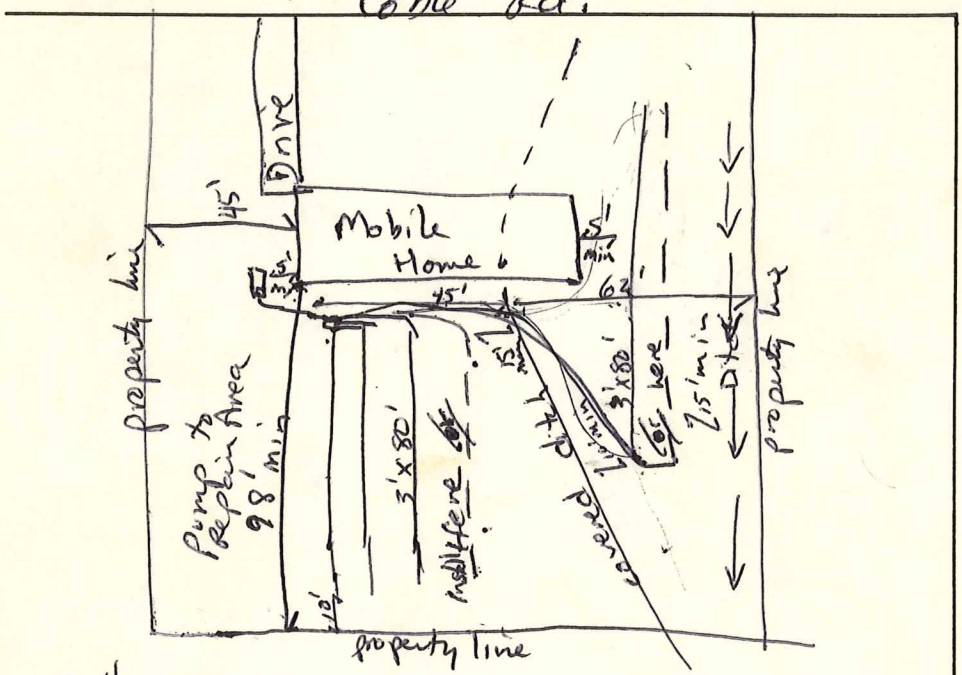

PLOT OF SYSTEM

Liquid Capacity of Septic Tank 1500 gallons

Liquid Capacity of Dosing Tank ____ gallons

Tank Construction PCC

Absorption and/or Nitrification Lines:

Trench Width 3' feet

Total Line Length 400' feet

Number of Lines 5 at 80' each

Depth of Stone 12" inches

Distance from House 5' feet

Distance from Property Line 10' min feet

Distance from Well 50' min feet
preferably 100' min
(well not in yet)

6"-16" soil cover

trench bottom max 28"

min 9' on center

NAME OF OWNER Fred Sanders / Performance Investment Brokerage Inc.

LOCATION OF PROPERTY 11201 Coble Rd.

Comments: Pump to Repair Area. Keep well min 50', preferably 100', from any part of septic system. Set mobile home to accomodate septic tank system. Keep off of covered ditch as shown. Some grading was done on lot.

Judy J. Rizer for J Daniel
Division or Section Head

Susan Gatewood
Environmentalist

* If this permit is for the installation or construction of a new system, it must be signed by the division or a section head of the Mecklenburg County Health Department in order to be valid. Only the signature of the Environmentalist is required where an existing system is being altered or repaired.

WHITE - HEALTH DEPARTMENT'S COPY • CANARY - ENVIRONMENTALIST'S COPY • PINK - OWNER OR AGENT'S COPY
