

PHILLIPS TRACE

12/26/2007

duponbj

Groundwater and Wastewater Services File Imaging Project

May 2007

Barcode Font = IDAutomationHC39M

FEE: _____ **AUTHORIZATION FOR WASTEWATER SYSTEM CONSTRUCTION**
DATE: _____ **VOID SIXTY (60) MONTHS FROM DATE OF ISSUANCE**

DATE: 4-30-97 PERMIT NO: 1762-B
PARCEL NO: 215-25-99-10

JOB LOCATION ADDRESS: Phillips Rd
PROPERTY OWNER: Roger Martin
BUILDING CONTRACTOR: " "
SUBDIVISION NAME: Phillips Trace
AUTHORIZATION ISSUED BY: _____ DATE: _____
DEHNR AUTHORIZED AGENT

AUTHORIZATION CONDITIONS

1. WASTEWATER SYSTEM CONSTRUCTION AND INSTALLATION MUST MEET ALL CONDITIONS AND SPECIFICATIONS AS SET FORTH IN IMPROVEMENT PERMIT NO. 1762-B, AND THE ATTACHED SITE PLAN WITH SYSTEM DETAILS. CONSTRUCTION AND INSTALLATION MUST ALSO MEET ALL REQUIREMENTS SET FORTH IN THE RULES GOVERNING SANITARY SEWAGE COLLECTION, TREATMENT, AND DISPOSAL AND ANY OTHER APPLICABLE RULES AND LAWS.

Mr Stanes 5/1/02
Prospective Buyer
821-7180

Permit expired 4/30/02

What needs to be done to proceed now?

Need application & current pd now & start over

w/$720 fee

Prop

TION AND/OR REPAIR APPROVAL MUST
E SEPTIC TANK SYSTEM. THE
ISTERED SEPTIC TANK CONTRACTOR
RTMENT.

NS (INCLUDING LOCATION OF
FICATION IN USE, DESIGN
ACTERISTICS AS SPECIFIED IN THE
LICATION, MAY SUBJECT THIS
TO REVOCATION.

ons

TION

ATIONS IN SITE OR SOIL CONDITIONS
ER FLOW, OR WASTEWATER
THE ORIGINAL APPLICATION OR
UTHORIZED IN WRITING BY THE
T. I ALSO UNDERSTAND THAT ANY
E INFORMATION ARE GROUNDS FOR
N TO CONSTRUCT.

5-5-97
DATE


PROPOSED PLOT PLAN

HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON STREET
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: _____

TC: _____

Draw in and name all roads adjoining the property. Draw in and accurately dimension the lot concerned. Accurately indicate property boundaries proposed and/or existing structures and driveways, underground utilities, and wells and springs within 100 feet of the proposed building or drainfield.

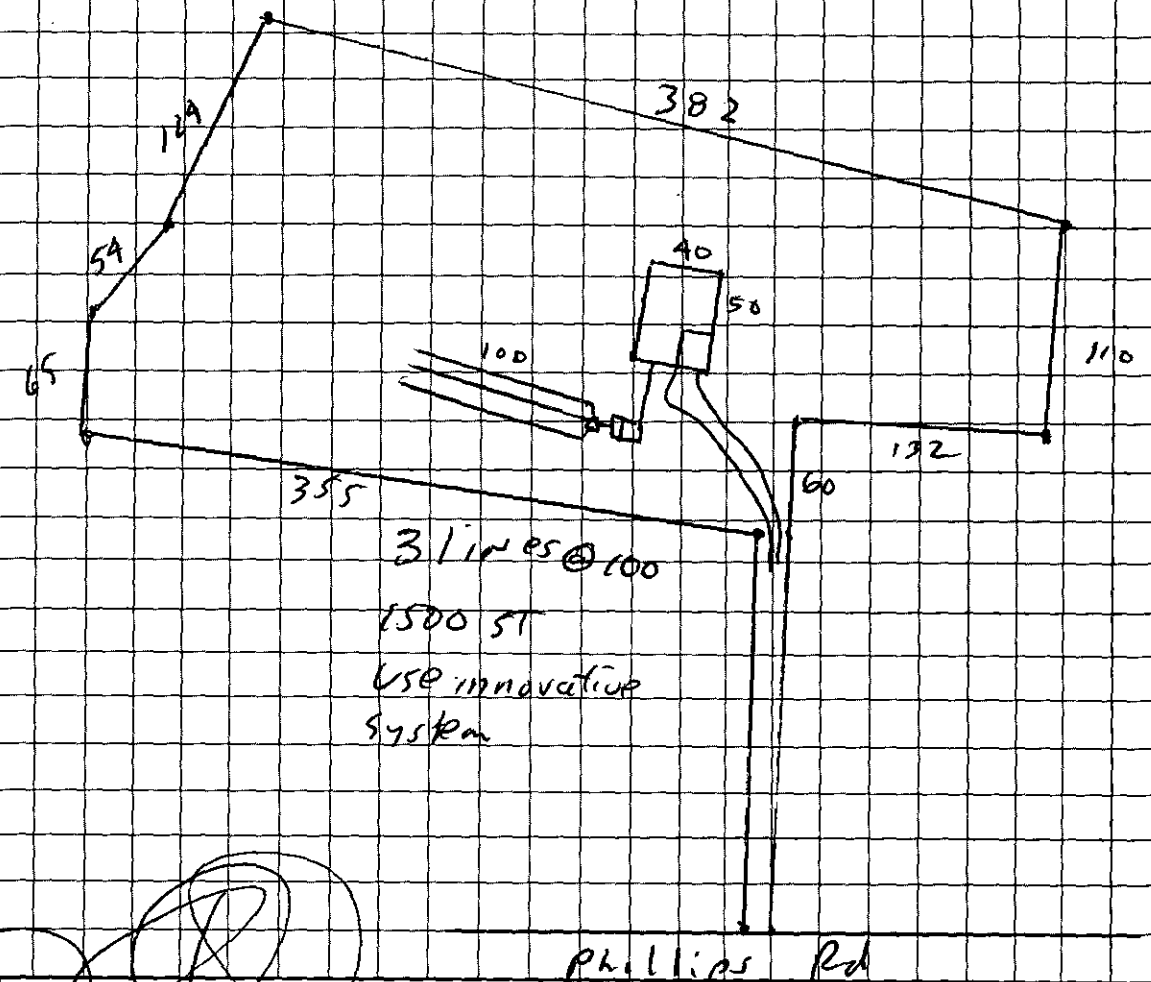

OWNER/AGENT SIGNATURE

DATE 5-5-97

APPROVAL DATE _____

White - Health Department's Copy Canary - E.H.S. Copy Pink - Owner's Copy

Permit Number: 1762-B

CONDITIONS OF IMPROVEMENT PERMIT

Tax Number: 215-135 99A

- The IMPROVEMENT PERMIT is subject to revocation if site plans or the intended use change. There is to be NO grading, filling or disturbance of the soil in the area of the septic tank system or repair area.
- CONSTRUCTION AUTHORIZATION must be obtained prior to receiving a Building Permit. The Construction Authorization is NOT transferable. Do not clear, grade, fill or disturb soil prior to obtaining a Construction Authorization.
- Domestic-type wastewater only. No industrial process wastewater may be discharged into the system.

Basement	___ Yes	✓ No	___ Partial Basement	
Type Primary Wastewater System Type (circle one): I II (III) IV V VI	___ Conventional ___ Prefabricated, permeable block panel system ___ Shallow Placed Conventional	___ Low Pressure Pipe ___ Large Diameter Pipe ___ Fill ___ Other	✓ Innovative or Experimental: ___ IWWS-93-1 ___ IWWS-93-2 ___ IWWS-94-1	
3 Long-term acceptance rate	360 Max gallons/day wastewater flow	900 Absorption Area (sq ft)	9 Trench spacing (min. on centers)	
No Serviced by private well	1500 Gallon septic tank	300 Total trench length (ft)	24" Maximum trench depth (At least 12" of provisionally suitable soil must remain between trench bottom and unsuitable soil conditions)	
3 Bedrooms in residence	✓ Gallon pump tank	✓ Depth of stone		
Any surface waters present: No Type:		Minimum separation distance:		
Site modifications required:				
Additional Conditions: See plan - Ref: Recovery of abandoned Low pressure drainfield to Newly platted building lots with new septic systems at Oakcroft Subdivison, Mecklenburg County, N.C.				
Repair Area System Type Type (circle one): I II (III) IV V VI	___ Conventional ___ Prefabricated, permeable block panel system ___ Shallow Placed Conventional	___ Low Pressure Pipe ___ Large Diameter Pipe ___ Fill ___ Other	✓ Innovative or Experimental: ___ IWWS-93-1 ___ IWWS-93-2 ___ IWWS-94-1	
900 Absorption Area (Sq ft) 300 Total Trench Length (Ft)	✓ Depth of Stone Trench	9 Trench spacing (min. on centers)	24" Maximum Trench Depth	
For existing system, enter the year originally installed:				

The undersigned, an authorized agent of the MECKLENBURG COUNTY HEALTH DEPARTMENT, certifies that the Department has approved the Request for the Job Location contained in this document. This approval is granted in accordance with the provisions of Laws and Rules For Sewage, Treatment and Disposal in effect at the time of issuance of the permit and is subject to the following provisions:

- No work shall be conducted on the septic tank system until an Installation, Construction, Alteration and/or Repair Approval is granted by this Department
- This Improvement permit is transferable.

DEHNR Authorized Agent — Date: 4-30-97

Owner/Agent Signature — Date: 5-5-97

MECKLENBURG COUNTY
HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
c/o HAL MARSHALL CTR.
SUITE 211
700 N. TRYON ST.
CHARLOTTE, N.C. 28202.
(704) 336-5102


NORTH CAROLINA DEPARTMENT OF
ENVIRONMENTAL, HEALTH,
AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

Toney C. Jacobs & Associates, Inc.
Consulting Soil Scientists
NCRCPS ARCPACS

168 Broadbill Drive
Mooresville, NC 28115
Phone (704) 663-6905
Fax (704) 662-9845

April 15, 1997



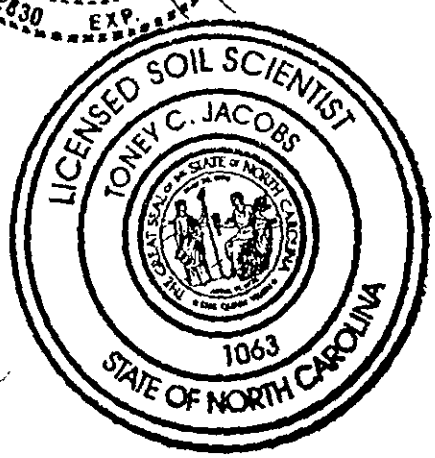

To: Mr. Roger Martin
P. O. Box 23071
Charlotte, N. C. 28212

Mr. Kelly Randall, R. S.
Mecklenburg County Health Dept.
Charlotte, N. C.

Mr. Bill Marlin, Soil Scientist
Mecklenburg County Health Dept.
Charlotte, N. C.

Mr. Tim Bannister
Tri-County Wastewater Management
712 S. Hayne St.
Monroe, N. C. 28112

From: Toney C. Jacobs, CPSS

Ref: Recovery of abandoned Low pressure drainfield to newly platted building lots with new septic systems at Oakcroft Subdivision, Mecklenburg County, N. C.

Introduction

Oakcroft was developed with a community LPP between 1987 and 1992. North State Utilities installed and operated the system until taken over by the N.C. Utilities Commission in September 1993. The NCUC contracted with Tri-County Wastewater Management who operated the ground absorption system until 1995. In 1995 CMUD began servicing Tri-County for the existing lines and the LPP system was abandoned. After this, the area where the drainfield was placed became available for lot development and was purchased by

Roger Martin of Charlotte. Due to CMUD policy, 7 new lots cannot be added to the public sewer. This is certainly not what the developer wants, but must live with.

My scope of services was to investigate what was on site and present a plausible plan to 1) keep water from moving across lot lines to neighboring property via old lines, 2) prevent old system from interfering with new systems yet to be permitted and installed, and 3) illustrate to the Health Department what added measures or precautions should be incorporated into permitting. We believe that the "as built" can be accurately overlaid on the new plat.

The site has very good "as built" drawing of old LPP field lines. These were done by LandDesign of Charlotte and were checked in the field by Tim Bannister and myself. Tri-County Waste Water operated the system after North State failed and Tim has a good working knowledge of the surface components of the system.

Fieldwork

On April 2, 1997 two trenches approximately 100' and 50' were opened beside of new lot lines 2,3 and 4,5, respectively (Plate 1-1, 2-1, 2-2). Both of these crossed numerous pipes (1-1, 2-3) and one supply manifold line (2-3). Thirteen photographs from the trench and area were made to serve as exhibits for this report. Depths to the bottom of each pipe and trench were measured (1-1,1-2, 3-1). Special attention was given to compaction or void spaces around the supply manifold pipe (2-2).


Observations

1. Pipe depths ranged from 10" to 15". Trench depth for LPP laterals ranged from 12" to 16".
2. The manifold was 30" deep and no channels or voids existed around the pipe.
3. The quantity and size of stone was disappointing for a system (1-3, 3-1). Stone was fine material and quantity was very limited (3-3). The storage capacity per foot of pipe was minimal (1-3, 3-1).
4. The trenches measured 6" wide (1-3); however, each time the backhoe opened the ditch across a line this old line was very obvious.
5. There are observation wells for system monitoring at the site (3-2).
6. In April 1997 there were no organic or slime materials associated with the lines (1-2, 1-3, 3-1). An original copy of each picture is enclosed with the report so that the county can accurately see soil colors. These photos also illustrate the absence of the slime layer.

Recommendations

This is for each lot where LPP pipes are located. This procedure to be carried anywhere within 25' of LPP old lines.

1. A 24" trench 8'-10' off the property line will be excavated 24" deep with any roots and old pipes cut even with the sidewalls and removed from trench (see illustration).
2. The trench sidewalls will be heavily dusted with powdered Wyoming Bentonite clay. This is available from most well drillers or well driller supply houses and currently costs about $7.75/50 lb. bag.
3. Backfill the trench with clay or heavy clay loam subsoil. This does not mean topsoil or saprolite material. This must be tamped with tamping machine, backhoe bucket, or backhoe tires in combination with the bucket.
4. The new systems should be placed at normal system depths. New lines will run on contour much the same as old LPP lines. Any distribution lines should be tamped within one foot of new trench.
5. The monitoring wells should be filled following 2C rules and properly reported.
6. The developer, Roger Martin, has agreed by this report to have a management contract on all lots for the first year of operation. This contract is for any Type 2, 3, and naturally 4 systems. This contact would be with Tri-County Wastewater and Tim Bannister would know both what and where to look should problems arise. Just by house and lot size discussed in the field, many of these systems will be Type 3 and 4.
7. Soils work will be by MCHD and each system designed individually as permit is requested.

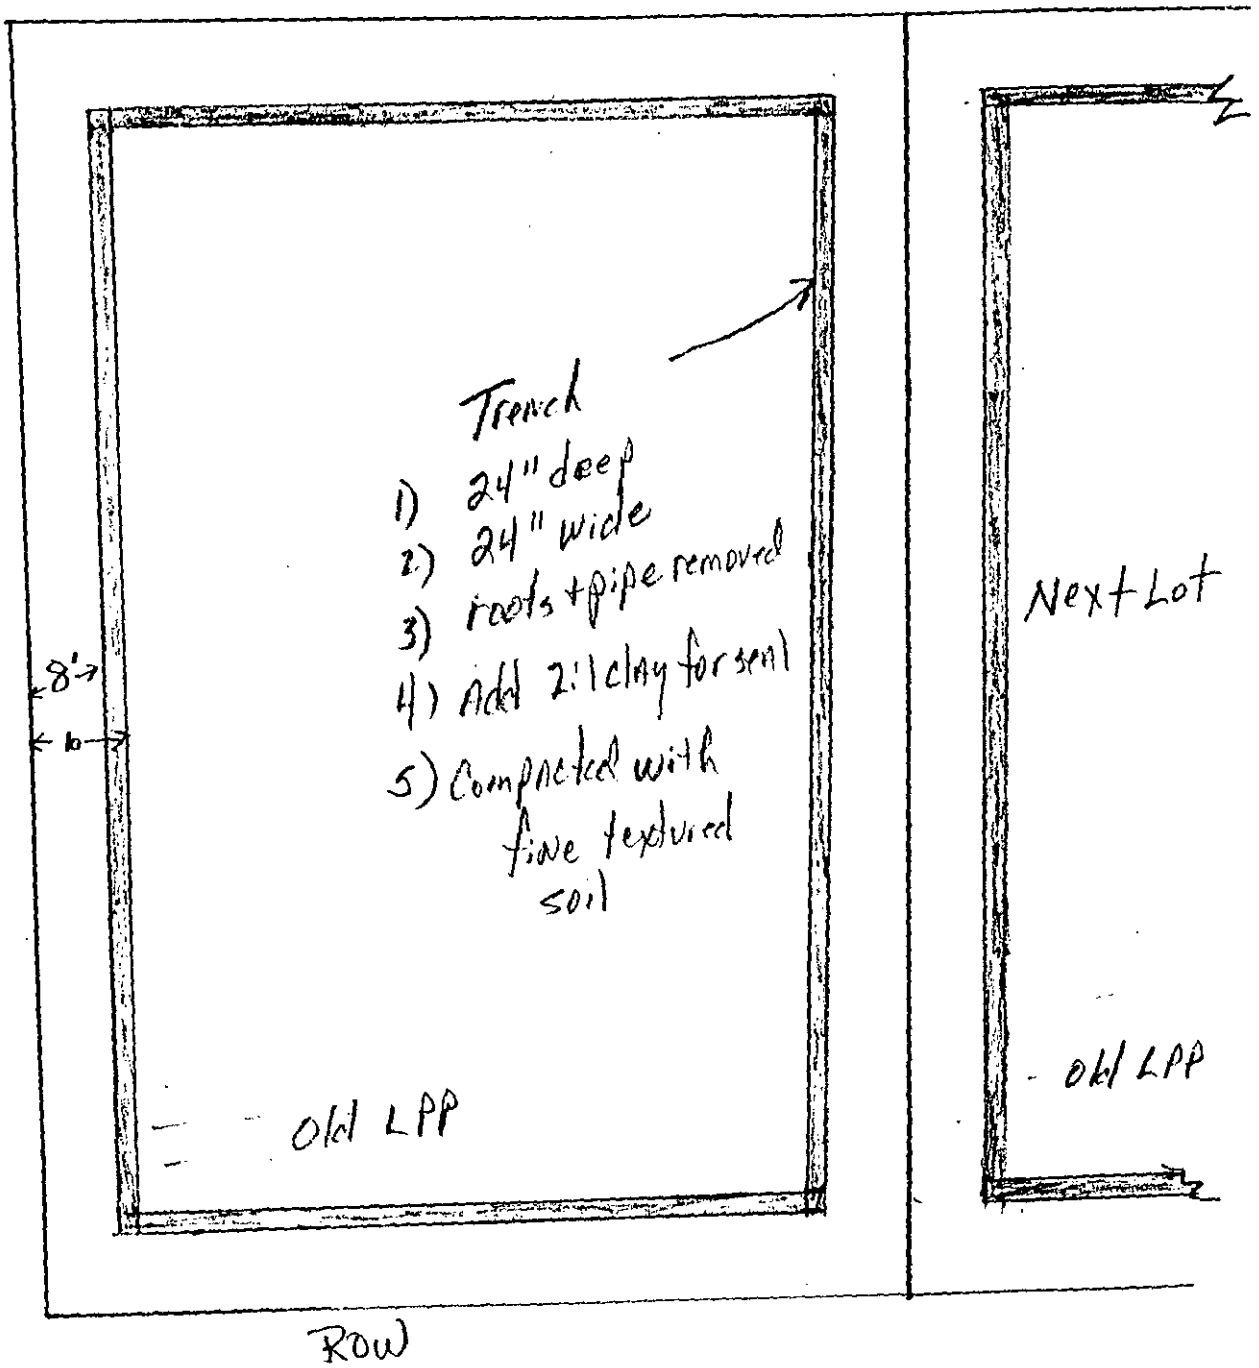
Trench
1) 24" deep
2) 24" wide
3) roots + pipe removed
4) Add 2:1 clay for soil
5) Compacted with fine textured soil
8'
10
Old LPP
Next Lot
Old LPP
ROW

Street



Plate 1-1

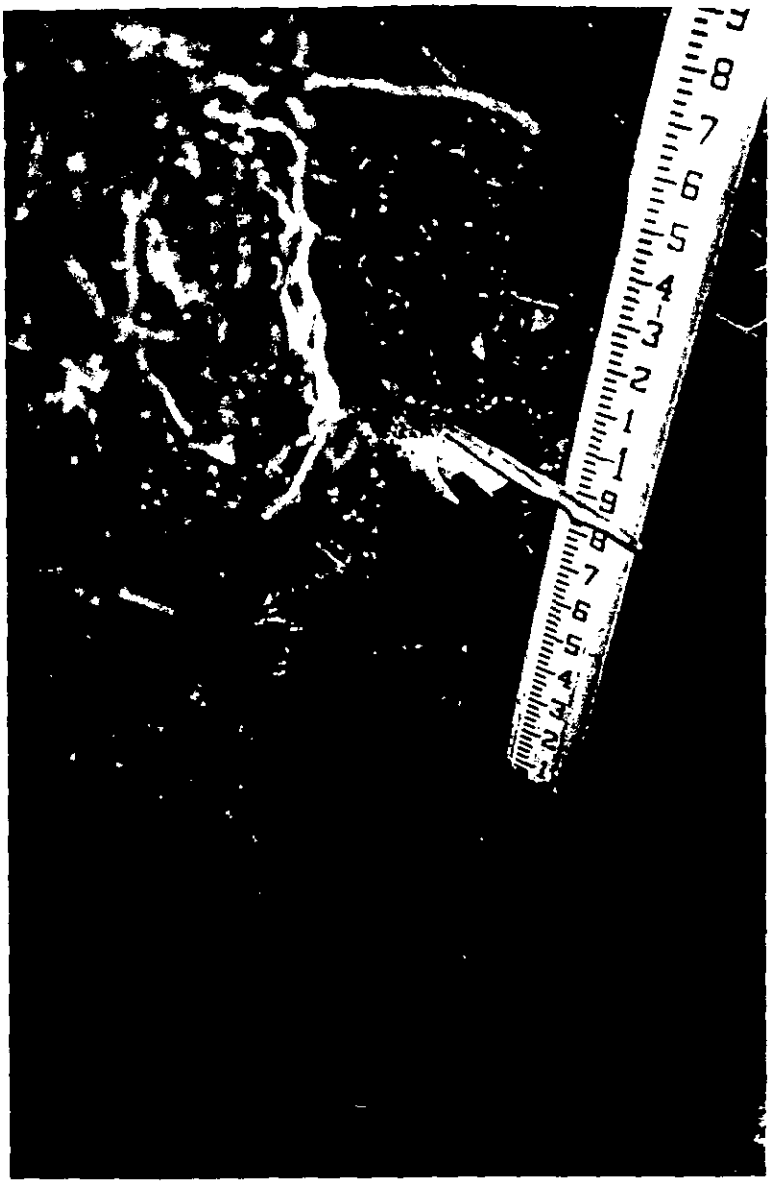


Plate 1-2



Plate 1-3



Plate 2-1



Plate 2-2

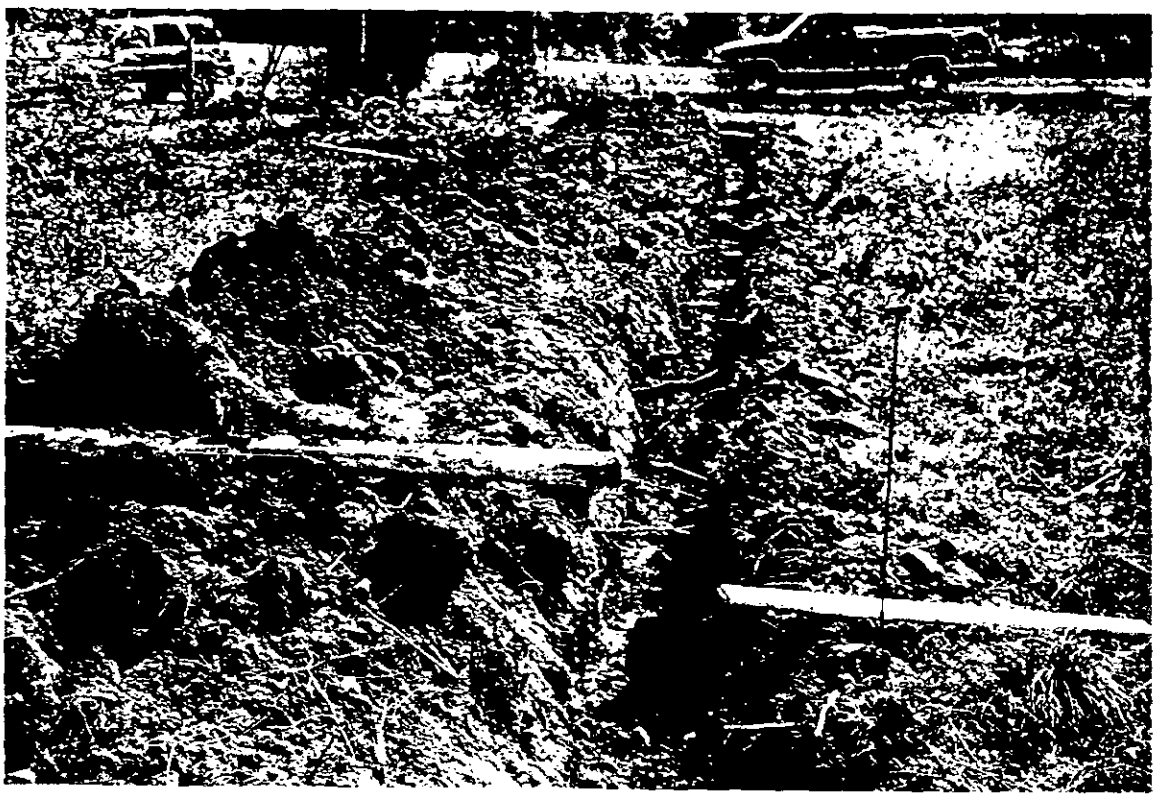


Plate 2-3



Plate 3-1



Plate 3-2

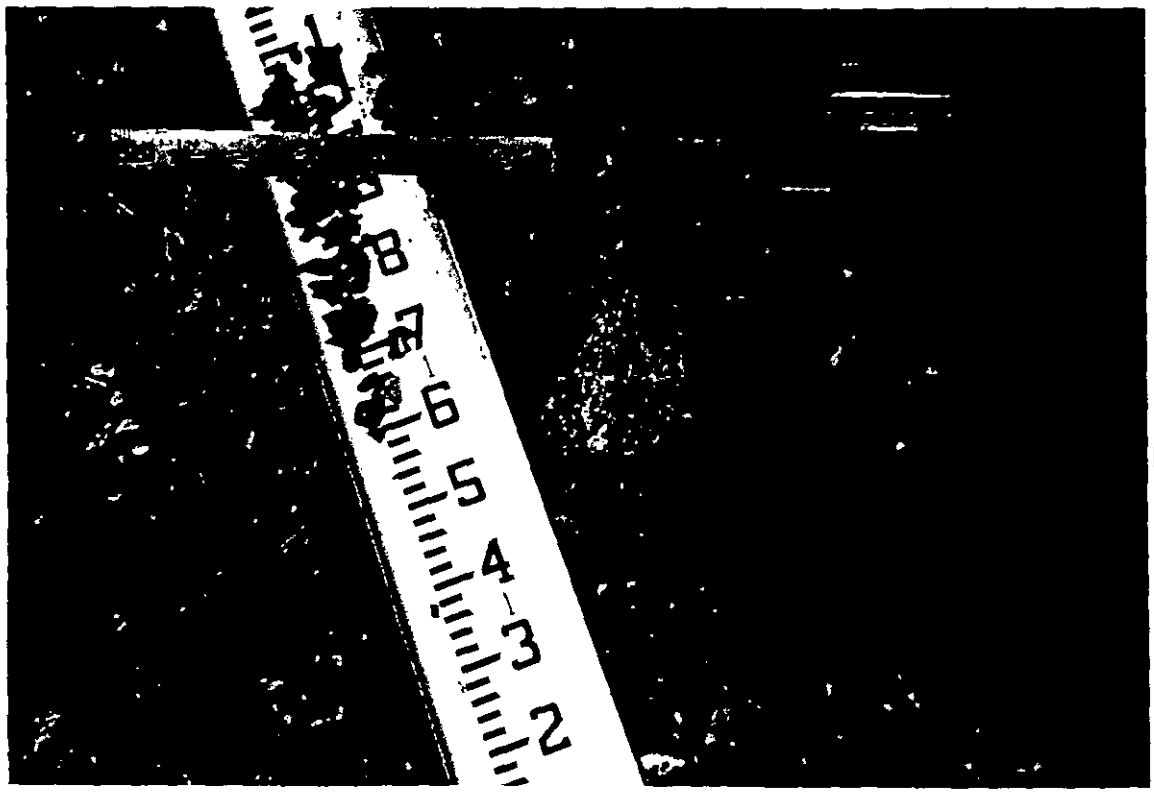


Plate 3-3

Mecklenburg County
Health Department

March 24, 1997

Mr. Roger Martin
P. O. Box 23071
Charlotte, NC 28227

Re: Phillips Road
File: 1762B
Parcel: 215-135-99PO

Dear Mr. Martin:

Receipt of your Application for Improvement Permit for the above referenced property is acknowledged. A soil evaluation and a site visit have been conducted. The results of the evaluation indicated that the site is **UNSUITABLE** under Rule .1945 **AVAILABLE SPACE.** For this reason your Application for Improvement Permit is denied. A possible way to develop the site exists under Rule .1948(d) which reads as follows:

> A site classified as **UNSUITABLE** may be used for a ground absorption sewage treatment and disposal system specifically identified in Rules .1955, .1956, or .1957 of this Section or a system approved under Rule .1969 if written documentation, including engineering, hydrogeologic, geologic or soil studies, indicates to the local health department that the proposed system can be expected to function satisfactorily. Such sites shall be reclassified as **PROVISIONALLY SUITABLE** if the local health department determines that the substantiating data indicate that:
> (1) a ground absorption system can be installed so that the effluent will be non-pathogenic, non-infectious, non-toxic, and non-hazardous;
> (2) the effluent will not contaminate ground or surface water; and
> (3) the effluent will not be exposed on the ground surface or be discharged to surface waters where it could come in contact with people, animals, or vectors.

The State shall review the substantiating data if requested by the local health department.

Please be advised that you have the right to an informal review by this department. You also have the right to appeal under G.S. 130A-24, and to have the appeal held in Mecklenburg County.

If you have any questions regarding this matter, please call me at 336-5575.

Sincerely,

Kelly Randall, R.S., Soil Scientist
Individual Water and Wastewater Systems

DEPARTMENT OF ENVIRONMENT, HEALTH, AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

2400

PROPERTY ID #: #2 17629
COUNTY: PO 215-135-99
Sheet ___ of ___ Lot #7

SOIL/SITE EVALUATION *for* ON-SITE WASTEWATER SYSTEM

OWNER: Roger Shaden Marlin
APPLICANT: _____
DATE EVALUATED: _____
ADDRESS: PO Box 23071, Charlotte
APPLICATION DATE: _____
PROPERTY SIZE: Approx 2.0
PROPOSED FACILITY: residence
PROPOSED DESIGN FLOW (.1949): 360gpd
PROPERTY RECORDED: _____
LOCATION OF SITE: off Phillippi Road
WATER SUPPLY: ☐ Private ☑ Public ☐ Well ☐ Spring ☐ Other _____
EVALUATION METHOD: ☑ Auger Boring ☐ Pit ☐ Cut
TYPE OF WASTEWATER: ☑ Sewage ☐ Industrial Process ☐ Mixed

PROFILE #	Clonts 5-106 .1940 LANDSCAPE POSITION/ SLOPE %	HORIZON DEPTH (IN.)	SOIL MORPHOLOGY (.1941) .1941 STRUCTURE/ TEXTURE	.1941 CONSISTENCE/ MINERALOGY	OTHER PROFILE FACTORS .1942 SOIL WETNESS/ COLOR	.1943 SOIL DEPTH	.1956 SAPRO CLASS	.1944 RESTR HORIZ	PROFILE CLASS & LT.
1	LS	0-6"	gr/cl	Fv/SEXP/SS/SP	746" TO soil wetness	46"	N/A	None	.39/F2 IV PS
		6-46"	SBK/c	Fi/SEXP/SP					
2	LS	0-4"	gr/cl	Fv/SEXP/SS/SP	746" TO soil wetness	46"	N/A	None	.39/F2 IV PS
		4-46"	SBK/c	Fi/SEXP/SP					
3	LS	0-3"	gr/cl	Fv/SEXP/SS/SP	736" TO soil wetness	36"	N/A	None	.39/F2 IV PS
		3-36"	SBK/c	Fi/SEXP/SP					
4	LS	0-5"	gr/cl	Fv/SEXP/SS/SP	746" TO soil wetness	46"	N/A	None	.39/F2 IV PS
		5-46"	SBK/c	Fi/SEXP/SP					

DESCRIPTION	INITIAL SYSTEM	REPAIR SYSTEM
Available Space (.1945)	us	us
System Type(s)		

OTHER FACTORS (.1946): _____
SITE CLASSIFICATION (.1948): recommendable
EVALUATED BY: W.R. Marlin 3-17-97
OTHER(S) PRESENT: LSS

DEPARTMENT OF ENVIRONMENT, HEALTH, AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

PROPERTY ID #: _____ of _____
COUNTY: _____

SOIL/SITE EVALUATION
for ON-SITE WASTEWATER SYSTEM

= 1
17628

OWNER: _____ APPLICANT: _____
ADDRESS: _____ APPLICATION DATE: _____ DATE EVALUATED: _____
PROPOSED FACILITY: _____ PROPOSED DESIGN FLOW (.1949): _____ PROPERTY SIZE: App. 2.0
LOCATION OF SITE: _____ PROPERTY RECORDED: _____
WATER SUPPLY: ☐ Private ☐ Public ☐ Well ☐ Spring ☐ Other _____
EVALUATION METHOD: ☐ Auger Boring ☐ Pit ☐ Cut
TYPE OF WASTEWATER: ☐ Sewage ☐ Industrial Process ☐ Mixed

PROFILE #	.1940 LANDSCAPE POSITION/ SLOPE %	HORIZON DEPTH (IN.)	SOIL MORPHOLOGY (.1941) .1941 STRUCTURE/ TEXTURE	.1941 CONSISTENCE/ MINERALOGY	OTHER PROFILE FACTORS .1942 SOIL WETNESS/ COLOR	.1943 SOIL DEPTH	.1956 SAPRO CLASS	.1944 RESTR HORIZ	PROFILE CLASS & LT
5	LS	0-5"	gr/cl	Fv/SEXP/SS/SP	746" TO Soil Wetness	46"	N/A	None	1a/Fz IV DS
		5-46"	SBK/C	Fi/SEXP/S/P					
6	LS	0-4"	gr/cl	Fv/SEXP/SS/SP	743" TO Soil Wetness	43"	N/A	None	1a/Fz IV DS
		4-43"	SBK/C	Fi/SEXP/S/P					
3									
4									

DESCRIPTION	INITIAL SYSTEM	REPAIR SYSTEM
Available Space (.1945)		
System Type(s)		

OTHER FACTORS (.1946): _____
SITE CLASSIFICATION (.1948): _____
EVALUATED BY: _____
OTHER(S) PRESENT: _____

COMMENTS: 100% Repair

LEGEND

use the following standard abbreviations

LANDSCAPE POSITION	GROUP	SOIL TEXTURE	CONVENTIONAL .1955 LTAR	LPP .1957 LTAR	MINERALOGY/ CONSISTENCE	STRUCTURE
C (Concave Slope)	I	S (Sand)	1.2 - 0.8	0.6 - 0.4	NEXP (Non-expansive)	G (Single Grain)
V (Convex Slope)		LS (Loamy Sand)			SEXP (Slightly Expansive)	M (Massive)
(Drainage Way)					EXP (Expansive)	CR (Crumb)
S (Debris Slump)	II	SL (Sandy Loam)	0.8 - 0.6	0.4 - 0.3		GR (Granular)
P (Flood Plain)		L (Loam)				SBK (Subangular Blocky)
S (Foot Slope)						ABK (Angular Blocky)
(Head Slope)	III	SI (Silt)	0.6 - 0.3	0.3 - 0.15		PL (Platy)
(Linear Slope)		SICL (Silty Clay Loam)				PR (Prismatic)
(Nose Slope)		CL (Clay Loam)				
(Ridge)		SCL (Sandy Clay Loam)			MOIST	WET
(Shoulder Slope)		SLC (Silt Loam Clay)				
(Terrace)					VFR (Very Friable)	NS (Non-sticky)
	IV	SC (Sandy Clay)	0.4 - 0.1	0.2 - 0.05	FR (Friable)	SS (Slightly Sticky)
		SIC (Silty Clay)			FI (Firm)	S (Sticky)
					VFI (Very Firm v. Very Sticky)	VS (Very Sticky)
		O (Organic)	None		EFI (Extremely Firm)	NP (Non-plastic)
						SP (Slightly Plastic)
						P (Plastic)
						VP (Very Plastic)

NOTES


HORIZON DEPTH	In inches below natural soil surface
DEPTH OF FILL	In inches from land surface
RESTRICTIVE HORIZON	Thickness and depth from land surface
SAPROLITE	S(suitable) or U(unsuitable)
SOIL WETNESS	Inches from land surface to free water or inches from land surface to soil colors with chroma 2 or less - record Munsell color chip designation
CLASSIFICATION	S (Suitable), PS (Provisionally Suitable), or U (Unsuitable)

Evaluation of saprolite shall be by pits.

Long-term Acceptance Rate (LTAR): gal/day/ft²

Show profile locations and other site features (dimensions, reference or benchmark, and North).

1762 B

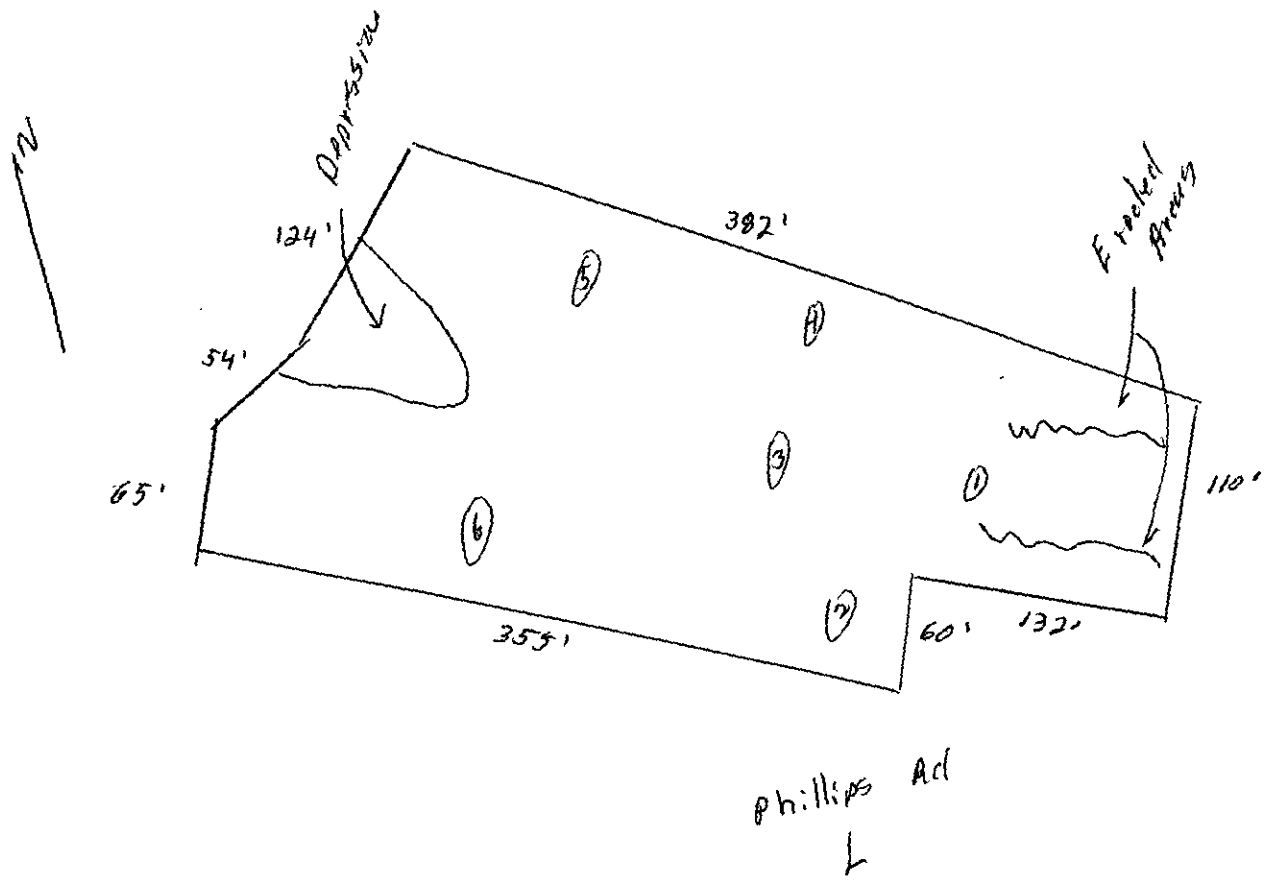

FEE: 100.00

DATE: 2-14-97

CK # 3232 9dw

APPLICATION FOR IMPROVEMENT PERMIT FOR RESIDENTIAL SITE INDIVIDUAL WATER AND WASTEWATER SYSTEMS PROGRAM

[ ] CRT

TYPE APPLICATION: ✓ NEW SYSTEM __ EXPANSION/ ALTERATION OF EXISTING SYSTEM __ REPAIR OF EXISTING SYSTEM

NORTH CAROLINA
DEPARTMENT OF ENVIRONMENT,
HEALTH, AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

FILE #: 17623

PROPERTY INFORMATION (FROM ENGINEERING FORM) FOR JOB LOCATION:

TAX/PARCEL NUMBER: P.O. 215-135-99

STREET ADDRESS: Phillips Rd.

SUBDIVISION OR MOBILE HOME PARK NAME: Phillips Trace

LOT NUMBER: 7

TYPE OF BUILDING (CHECK ONE):

__ SINGLE MOBILE HOME(S)
__ DOUBLE WIDE (D)
✓ HOUSE (H)
__ MODULAR HOME (M)
__ MULTIPLE FAMILY (U)
__ OTHER (O)

TOWNSHIP (CHECK ONE):

__ 0 MECKLENBURG
__ 1 CHARLOTTE
__ 2 DAVIDSON
__ 3 CORNELIUS
__ 4 PINEVILLE
✓ 5 MATTHEWS
__ 6 HUNTERSVILLE
__ 7 MINT HILL

HEATED SQUARE FOOTAGE: 1500

NUMBER OF BEDROOMS: 3 NUMBER OF OCCUPANTS: 4

CLOSING DATE Pre-Construction

FOUNDATION FOR RESIDENCE:

__ WITHOUT BASEMENT
__ ON SLAB
✓ CRAWL SPACE
__ WITH BASEMENT /PLUMBING
__ WITH BASEMENT /NO PLUMBING

IF EXPANSION/ALTERATION OF EXISTING SYSTEM, DESCRIBE THE PROPOSED BUILDING ADDITION:

WILL THERE BE A HOME BUSINESS IN THE RESIDENCE: __ YES ✓ NO TYPE: _____

WATER SUPPLY (CHECK ONE):

__ COMMUNITY (C)
✓ MUNICIPAL (M)
__ PRIVATE WELL (P)
__ SHARED WELL (S)
__ OTHER 'SPRINGS' (O)

IF ANY OF THE FOLLOWING ARE LOCATED ON THE PROPERTY, PLEASE SHOW LOCATION ON PLAT:

BURIED CABLES, LANDFILLS, STUMPHOLES __ YES ✓ NO
EXISTING WASTEWATER SYSTEMS __ YES ✓ NO
EASTMENTS OR RIGHT-OF-WAYS __ YES ✓ NO
WELL, SPRINGS OR WATERLINES __ YES ✓ NO
DESIGNATED WETLANDS __ YES ✓ NO

PROPERTY OWNER:

NAME: (LAST) Martin (FIRST) Charles (MI) Roger

ADDRESS: P.O. Box 23071

CITY: Char STATE: N.C. ZIP: 28227

DAYTIME PHONE: (704 - 545-9461

LEGAL AGENT FOR PROPERTY OWNER, IF APPLICABLE:

NAME: (LAST) (FIRST) (MI)

DAYTIME PHONE: ( ) -

WHAT DATE WAS THE PROPERTY ORIGINALLY DEEDED AND RECORDED? 1-13-97

An Improvement Permit is subject to suspension or revocation if site plans or the intended use change or if information submitted in this application is falsified or changed. The undersigned, owner, or legal agent for the owner, of the property described above as the "Job Location" has read the foregoing application, acknowledges that the contents of same are true, and authorizes agents of the Mecklenburg County Health Department to enter onto the property for the purpose of processing this request.

SIGNED: _____ DATE: 2-15-97

MECKLENBURG COUNTY HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
c/o HAL MARSHALL CTR., SUITE 211, 700 N. TRYON ST., CHARLOTTE, N.C. 28202., (704) 336-5102

PROPOSED PLOT PLAN


Lot #7

HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON STREET
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 1762B

TC: 215-135-99PO

Draw in and name all roads adjoining the property. Draw in and accurately dimension the lot concerned. Accurately indicate property boundaries proposed and/or existing structures and driveways, underground utilities, and wells and springs within 100 feet of the proposed building or drainfield.

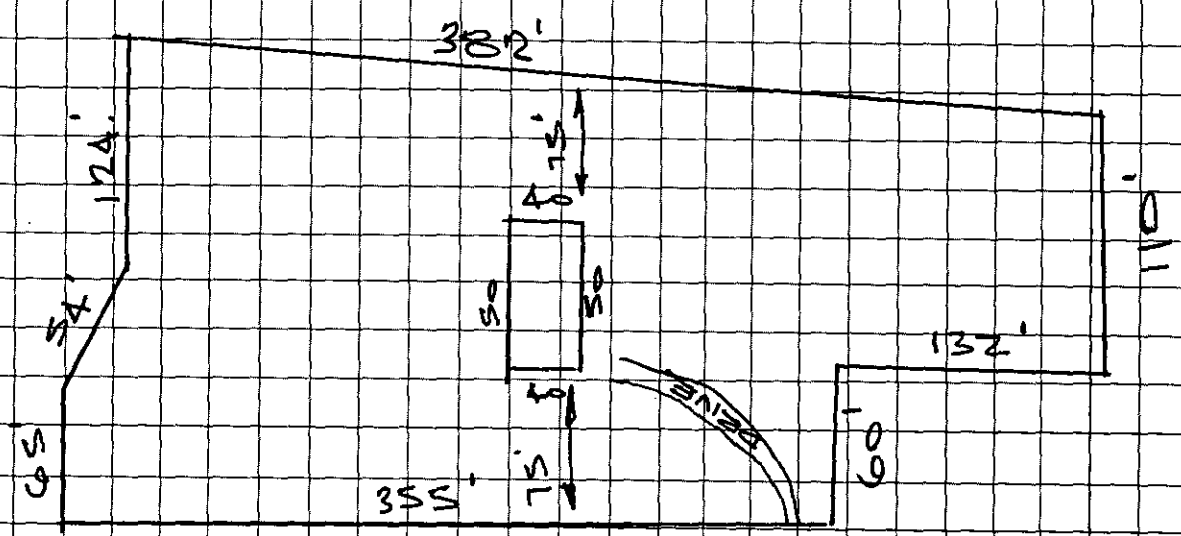

87,639 ft

2.01 acres.

15' EASEMENT

OWNER/AGENT SIGNATURE

DATE 2-15-96

APPROVAL DATE _____

White - Health Department's Copy

Canary - E.H.S. Copy

Pink - Owner's Copy
