

14517 PHILLIPS RD

21525412

12/26/2007

duponbj

Groundwater and Wastewater Services File Imaging Project
May 2007
Barcode Font = IDAutomationHC39M

CERTIFICATE OF COMPLETION/OPERATION PERMIT

HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON ST., SUITE 211
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 1760 B DATE: 09-01-99

TC: 215-135-9990 ☒ L ☒ CRT

SERIAL Nº 18129

Name of Owner Roger Martin Juris.:

Address of Property 14517 Phillips Rd.

Inspection Data:

Tank Material PCC

Total Length of Drainfield 300'

Number of Lines 4 @ 75'

Cover Depth 12"

Water Supply Source Mun.

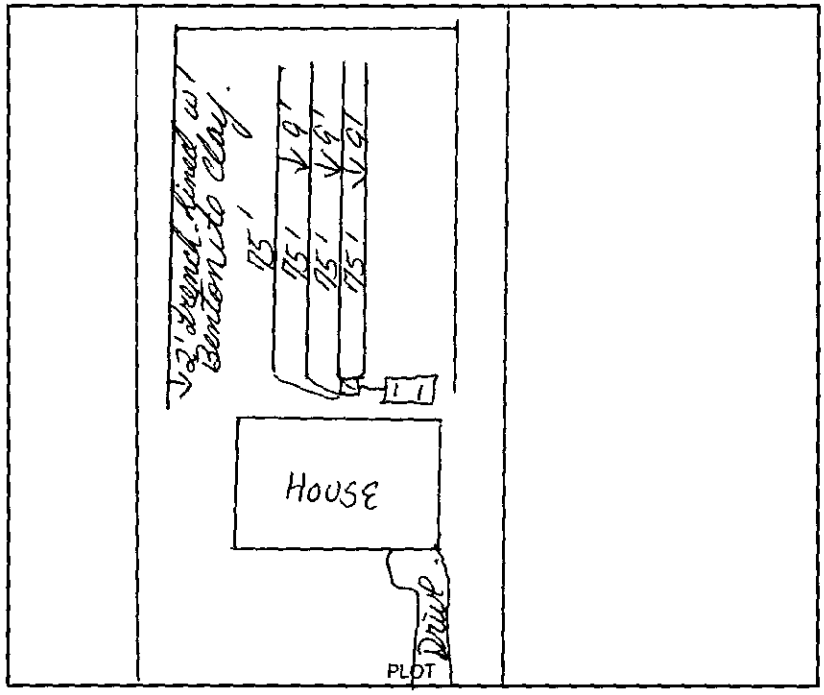
Distance to Water Source >50'

Excavation Inspected 09-01-99

Tank(s) Inspected 09-01-99

Wash Line Inspected N/A

High Water Alarm Inspected N/A



Design 1500ST INV 900SFT P.S. CTR# Norwood.

The undersigned has inspected the Septic Tank System described above, and certifies it has been

☒ installed or constructed ☐ altered or repaired

☐ in accordance with the permit issued ☒ as detailed in the plot above

and meets the provisions of 15A NCAC 18A. 1900, "Laws And Rules For Sewage Treatment and Disposal Systems" in effect on the date of issuance of the permit. This issuance of this

☐ Certificate of Completion ☒ Operation Permit

does not in any way guarantee that the system will operate properly or relieve any person now or hereafter owning, controlling, or using such system from any liability resulting from the failure of the system to operate properly. This document is issued subject to those restrictions and conditions shown on the permit(s) and the provisions of 15A NCAC 18A. 1990 in addition to those listed below under "COMMENTS." This document shall be null and void if any information contained in the application is untrue or if any additions are made to the property which would increase the requirements for said system.

Notice: Disturbance of the designated repair area may result in the suspension/revocation of this permit.

COMMENTS: Type III a system designed for a (3) bedroom design unit Type III a Repair Area.

Joshua R. Sellers R.S.
Environmental Health Specialist

Mecklenburg County services are available without regard to ethnic origin, sex, or disability.

INSTALLATION, CONSTRUCTION, ALTERATION, AND/OR REPAIR APPROVAL

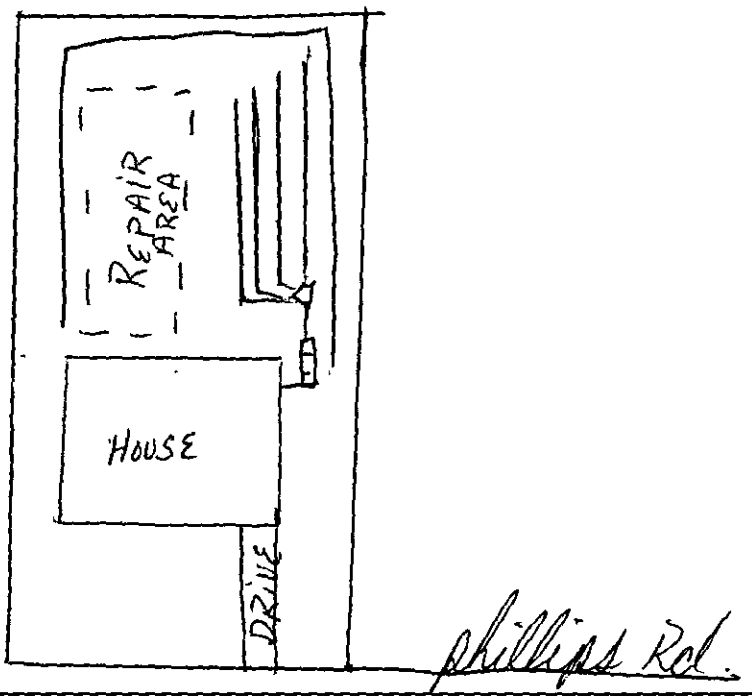
HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON ST., SUITE 211
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 1760B DATE: 08-31-99

TC: 215-135-99 POX

SERIAL

Permission is hereby given to ✓ Install or Construct, _____ Alter or Repair the individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge as specified herein at the described location. This permit is granted based upon the information supplied in the application dated 02-15-97. All work shall be completed on or before 08-31-00, after which date this permit shall be null and void. The system shall meet all of the construction requirements of 15A NCAC 18A. 1900 which are in effect on the date of the granting of this permit. A Certificate of Completion or an Operation Permit must be obtained from the Mecklenburg County Health Department before any system can be covered up or placed into service. The issuance of this permit does not in any way guarantee that the system anticipated to be constructed will operate properly, or relieve any person now or hereafter owning, controlling or using such system from any liability resulting from the failure of the system to operate properly.



PLOT OF SYSTEM

Liquid Capacity of Septic Tank 1500 gallons

Liquid Capacity of Dosing Tank N/A gallons

Tank Construction PCC

Trench Depth 24"

Absorption and/or Nitrification Lines:

Trench Width 3 feet

Trench Walls Scored and Porous yes

Total Line Length 300' feet

Number of Lines 4@75'

Depth of Stone N/A inches

Distance from House >5' feet

Distance from Property Line >10' feet

Distance from Well Public H2O feet

NOTICE: This system shall not be installed while soils are in a wet condition.

NAME OF OWNER Roger Martin

LOCATION OF PROPERTY 14517 Phillips Rd

Comments: 1500 ST 300 SFT INU Type III G system designed for 3 bedroom design unit Type III G Repair Area Trench 2' wide 2' deep lined w/ Bentonite clay to Enclose Septic Area, as per approved plan. Agreement forms need to be filed.

Joshua K. Sellers R.S.
Environmental Health Specialist

WHITE - HEALTH DEPARTMENT's COPY • CANARY - E.H.S. COPY • PINK - OWNER OR AGENT's COPY

Mecklenburg County
Health Department

TELECOPIER TRANSMITTAL COVER SHEET

NOTICE

THE INFORMATION CONTAINED IN THIS TELECOPY MAY BE PRIVILEGED AND/OR CONFIDENTIAL AND IS INTENDED ONLY FOR THE USE OF THE PERSON TO WHOM IT IS ADDRESSED. IF THE READER OF THIS MESSAGE IS NOT THE INTENDED RECIPIENT (OR SUCH RECIPIENT'S EMPLOYEE OR AGENT), YOU ARE HEREBY NOTIFIED NOT TO READ, DISTRIBUTE OR COPY THE MATERIALS ATTACHED HERETO WITHOUT THE PRIOR WRITTEN CONSENT OF THE SENDER. IF YOU HAVE RECEIVED THIS TELECOPY IN ERROR, PLEASE NOTIFY THE SENDER BY TELEPHONE CALL AND RETURN THE ORIGINAL TELECOPY TO US BY MAIL AND WE WILL REIMBURSE YOU FOR THE REQUIRED POSTAGE. THANK YOU.

TO: CATHY @ RCS TELECOPIER # 289-5500

FROM: D. Hall DATE _____

NUMBER OF PAGES TRANSMITTED: _____ (including cover sheet)

COMMENTS:

If you do not receive all pages, please call us as soon as possible at the following number: (704)336-5102.

[ ] Original will not follow [ ] Original will follow via:

[ ] U.S. Mail [ ] Hand Delivery [ ] _____

Environmental Health Division
700 North Tryon Street • Suite 211 • Charlotte, North Carolina 28202-2236

ck # 1111 100

FEE: 200.00 **AUTHORIZATION FOR WASTEWATER SYSTEM CONSTRUCTION**
DATE: 4/16/98 **VOID SIXTY (60) MONTHS FROM DATE OF ISSUANCE**

DATE: 9-30-97 PERMIT NO: 1760-B
PARCEL NO: 215-135-99 PO

JOB LOCATION ADDRESS: 1457 Phillips Rd
PROPERTY OWNER: Roger Martin
BUILDING CONTRACTOR: " "
SUBDIVISION NAME: Phillips Trace
AUTHORIZATION ISSUED BY: [signature] DATE:
DEHNR AUTHORIZED AGENT

AUTHORIZATION CONDITIONS

1. WASTEWATER SYSTEM CONSTRUCTION AND INSTALLATION MUST MEET ALL CONDITIONS AND SPECIFICATIONS AS SET FORTH IN IMPROVEMENT PERMIT NO. 1760-B, AND THE ATTACHED SITE PLAN WITH SYSTEM DETAILS. CONSTRUCTION AND INSTALLATION MUST ALSO MEET ALL REQUIREMENTS SET FORTH IN THE RULES GOVERNING SANITARY SEWAGE COLLECTION, TREATMENT, AND DISPOSAL AND ANY OTHER APPLICABLE RULES AND LAWS.

2. AN INSTALLATION, CONSTRUCTION, ALTERATION AND/OR REPAIR APPROVAL MUST BE SECURED **PRIOR** TO INSTALLATION OF THE SEPTIC TANK SYSTEM. THE INSTALLER OF THE SYSTEM SHALL BE A REGISTERED SEPTIC TANK CONTRACTOR WITH MECKLENBURG COUNTY HEALTH DEPARTMENT.

3. ANY ALTERATION IN SITE OR SOIL CONDITIONS (INCLUDING LOCATION OF STRUCTURES AND APPURTENANCES) OR MODIFICATION IN USE, DESIGN WASTEWATER FLOW, OR WASTEWATER CHARACTERISTICS AS SPECIFIED IN THE ASSOCIATED IMPROVEMENT PERMIT AND APPLICATION, MAY SUBJECT THIS AUTHORIZATION AND ASSOCIATED PERMIT(S) TO REVOCATION.

4. OTHER CONDITIONS: See plan and conditions

OWNER CERTIFICATION

I CERTIFY THAT THERE HAVE BEEN NO ALTERATIONS IN SITE OR SOIL CONDITIONS OR MODIFICATIONS TO FACILITY, WASTEWATER FLOW, OR WASTEWATER CHARACTERISTICS FROM THOSE SPECIFIED IN THE ORIGINAL APPLICATION OR ASSOCIATED IMPROVEMENT PERMIT UNLESS AUTHORIZED IN WRITING BY THE MECKLENBURG COUNTY HEALTH DEPARTMENT. I ALSO UNDERSTAND THAT ANY SUCH ALTERATIONS, MODIFICATIONS, OR FALSE INFORMATION ARE GROUNDS FOR REVOCATION OF PERMITS AND AUTHORIZATION TO CONSTRUCT.

[signature] 5.5-97
SIGNATURE OF OWNER/OWNER'S REPRESENTATIVE DATE

Permit Number: 1760-B

CONDITIONS OF IMPROVEMENT PERMIT

Tax Number: 215-135-99

- The IMPROVEMENT PERMIT is subject to revocation if site plans or the intended use change. There is to be NO grading, filling or disturbance of the soil in the area of the septic tank system or repair area.
- CONSTRUCTION AUTHORIZATION must be obtained prior to receiving a Building Permit. The Construction Authorization is NOT transferable. Do not clear, grade, fill or disturb soil prior to obtaining a Construction Authorization.
- Domestic-type wastewater only. No industrial process wastewater may be discharged into the system.

Basement	___ Yes	✓ No	___ Partial Basement	
Type Primary Wastewater System Type (circle one): I II III IV V VI	___ Conventional ___ Prefabricated, permeable block panel system ___ Shallow Placed Conventional	___ Low Pressure Pipe ___ Large Diameter Pipe ___ Fill ___ Other	✓ Innovative or Experimental: ___ IWWS-93-1 ___ IWWS-93-2 ___ IWWS-94-1	
.3 Long-term acceptance rate	360 Max gallons/day wastewater flow	900 Absorption Area (sq ft)	9 Trench spacing (min. on centers)	
No Serviced by private well	1500 Gallon septic tank	300 Total trench length (ft)	24" Maximum trench depth (At least 12" of provisionally suitable soil must remain between trench bottom and unsuitable soil conditions)	
3 Bedrooms in residence	✓ Gallon pump tank	✓ Depth of stone		
Any surface waters present: No Type:		Minimum separation distance:		
Site modifications required:				
Additional Conditions: See plan: Ref: Recovery of abandoned Low pressure drainfield to newly platted building lots with new septic systems at Oakcroft Subdivison, Mecklenburg County. NC.				
Repair Area System Type Type (circle one): I II III IV V VI	___ Conventional ___ Prefabricated, permeable block panel system ___ Shallow Placed Conventional	___ Low Pressure Pipe ___ Large Diameter Pipe ___ Fill ___ Other	___ Innovative or Experimental: ___ IWWS-93-1 ___ IWWS-93-2 ___ IWWS-94-1	
___ Absorption Area (Sq ft) ___ Total Trench Length (Ft)	___ Depth of Stone Trench	___ Trench spacing (min. on centers)	___ Maximum Trench Depth	
For existing system, enter the year originally installed:				

The undersigned, an authorized agent of the MECKLENBURG COUNTY HEALTH DEPARTMENT, certifies that the Department has approved the Request for the Job Location contained in this document. This approval is granted in accordance with the provisions of Laws and Rules For Sewage, Treatment and Disposal in effect at the time of issuance of the permit and is subject to the following provisions:

- No work shall be conducted on the septic tank system until an Installation, Construction, Alteration and/or Repair Approval is granted by this Department
- This Improvement permit is transferable.

DEHNR Authorized Agent — Date

Owner/Agent Signature — Date 5-5-97

MECKLENBURG COUNTY
HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
c/o HAL MARSHALL CTR.
SUITE 211
700 N. TRYON ST.
CHARLOTTE, N.C. 28202.
(704) 336-5102

NORTH CAROLINA DEPARTMENT OF
ENVIRONMENTAL, HEALTH,
AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

PROPOSED PLOT PLAN


HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON STREET
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 1760-B

TC: 215-135-99-PO

Draw in and name all roads adjoining the property. Draw in and accurately dimension the lot concerned. Accurately indicate property boundaries proposed and/or existing structures and driveways, underground utilities, and wells and springs within 100 feet of the proposed building or drainfield.

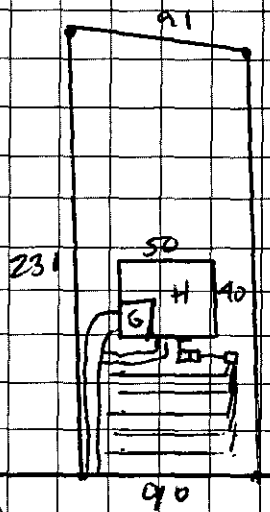Lot 5



1500 ST
Use innovative system
5 lines @ 60' each

OWNER/AGENT SIGNATURE

DATE 5-5-97

APPROVAL DATE _____

White - Health Department's Copy

Canary - E.H.S. Copy

Pink - Owner's Copy

Toney C. Jacobs & Associates, Inc.
Consulting Soil Scientists
NCRCPS ARCPACS

168 Broadbill Drive
Mooresville, NC 28115
Phone (704) 663-6905
Fax (704) 662-9845

April 15, 1997

To: Mr. Roger Martin
P. O. Box 23071
Charlotte, N. C. 28212

Mr. Kelly Randall, R. S.
Mecklenburg County Health Dept.
Charlotte, N. C.

Mr. Bill Marlin, Soil Scientist
Mecklenburg County Health Dept.
Charlotte, N. C.

Mr. Tim Bannister
Tri-County Wastewater Management
712 S. Hayne St.
Monroe, N. C. 28112

From: Toney C. Jacobs, CPSS

Ref: Recovery of abandoned Low pressure drainfield to newly platted building lots with new septic systems at Oakcroft Subdivision, Mecklenburg County, N. C.

Introduction

Oakcroft was developed with a community LPP between 1987 and 1992. North State Utilities installed and operated the system until taken over by the N.C. Utilities Commission in September 1993. The NCUC contracted with Tri-County Wastewater Management who operated the ground absorption system until 1995. In 1995 CMUD began servicing Tri-County for the existing lines and the LPP system was abandoned. After this, the area where the drainfield was placed became available for lot development and was purchased by

Roger Martin of Charlotte. Due to CMUD policy, 7 new lots cannot be added to the public sewer. This is certainly not what the developer wants, but must live with.

My scope of services was to investigate what was on site and present a plausible plan to 1) keep water from moving across lot lines to neighboring property via old lines, 2) prevent old system from interfering with new systems yet to be permitted and installed, and 3) illustrate to the Health Department what added measures or precautions should be incorporated into permitting. We believe that the "as built" can be accurately overlaid on the new plat.

The site has very good "as built" drawing of old LPP field lines. These were done by LandDesign of Charlotte and were checked in the field by Tim Bannister and myself. Tri-County Waste Water operated the system after North State failed and Tim has a good working knowledge of the surface components of the system.

Fieldwork

On April 2, 1997 two trenches approximately 100' and 50' were opened beside of new lot lines 2,3 and 4,5, respectively (Plate 1-1, 2-1, 2-2). Both of these crossed numerous pipes (1-1, 2-3) and one supply manifold line (2-3). Thirteen photographs from the trench and area were made to serve as exhibits for this report. Depths to the bottom of each pipe and trench were measured (1-1,1-2, 3-1). Special attention was given to compaction or void spaces around the supply manifold pipe (2-2).

Observations

1. Pipe depths ranged from 10" to 15". Trench depth for LPP laterals ranged from 12" to 16".
2. The manifold was 30" deep and no channels or voids existed around the pipe.
3. The quantity and size of stone was disappointing for a system (1-3, 3-1). Stone was fine material and quantity was very limited (3-3). The storage capacity per foot of pipe was minimal (1-3, 3-1).
4. The trenches measured 6" wide (1-3); however, each time the backhoe opened the ditch across a line this old line was very obvious.
5. There are observation wells for system monitoring at the site (3-2).
6. In April 1997 there were no organic or slime materials associated with the lines (1-2, 1-3, 3-1). An original copy of each picture is enclosed with the report so that the county can accurately see soil colors. These photos also illustrate the absence of the slime layer.

Recommendations

This is for each lot where LPP pipes are located. This procedure to be carried anywhere within 25' of LPP old lines.

1. A 24" trench 8'-10' off the property line will be excavated 24" deep with any roots and old pipes cut even with the sidewalls and removed from trench (see illustration).
2. The trench sidewalls will be heavily dusted with powdered Wyoming Bentonite clay. This is available from most well drillers or well driller supply houses and currently costs about $7.75/50 lb. bag.
3. Backfill the trench with clay or heavy clay loam subsoil. This does not mean topsoil or saprolite material. This must be tamped with tamping machine, backhoe bucket, or backhoe tires in combination with the bucket.
4. The new systems should be placed at normal system depths. New lines will run on contour much the same as old LPP lines. Any distribution lines should be tamped within one foot of new trench.
5. The monitoring wells should be filled following 2C rules and properly reported.
6. The developer, Roger Martin, has agreed by this report to have a management contract on all lots for the first year of operation. This contract is for any Type 2, 3, and naturally 4 systems. This contact would be with Tri-County Wastewater and Tim Bannister would know both what and where to look should problems arise. Just by house and lot size discussed in the field, many of these systems will be Type 3 and 4.
7. Soils work will be by MCHD and each system designed individually as permit is requested.



Trench
1) 24" deep
2) 24" wide
3) roots + pipe removed
4) Add 2:1 clay for seal
5) Compacted with fine textured soil
8'
10'
Old LPP
Next Lot
Old LPP
ROW
Street



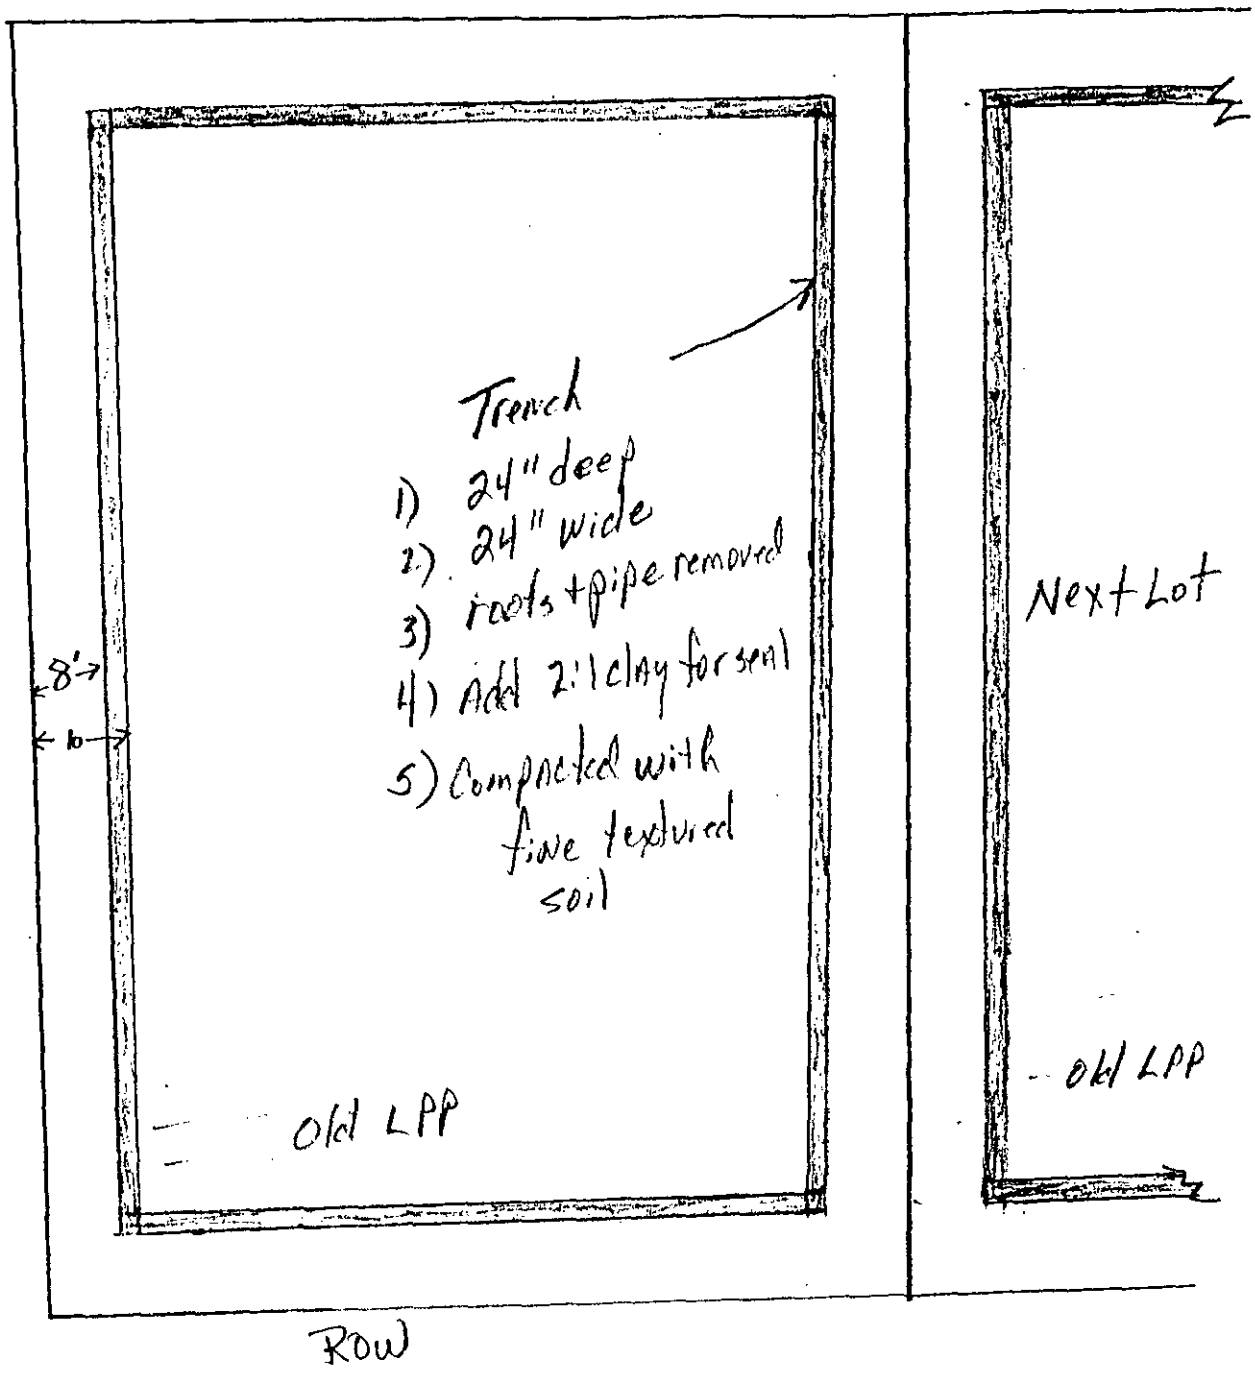Plate 1-1

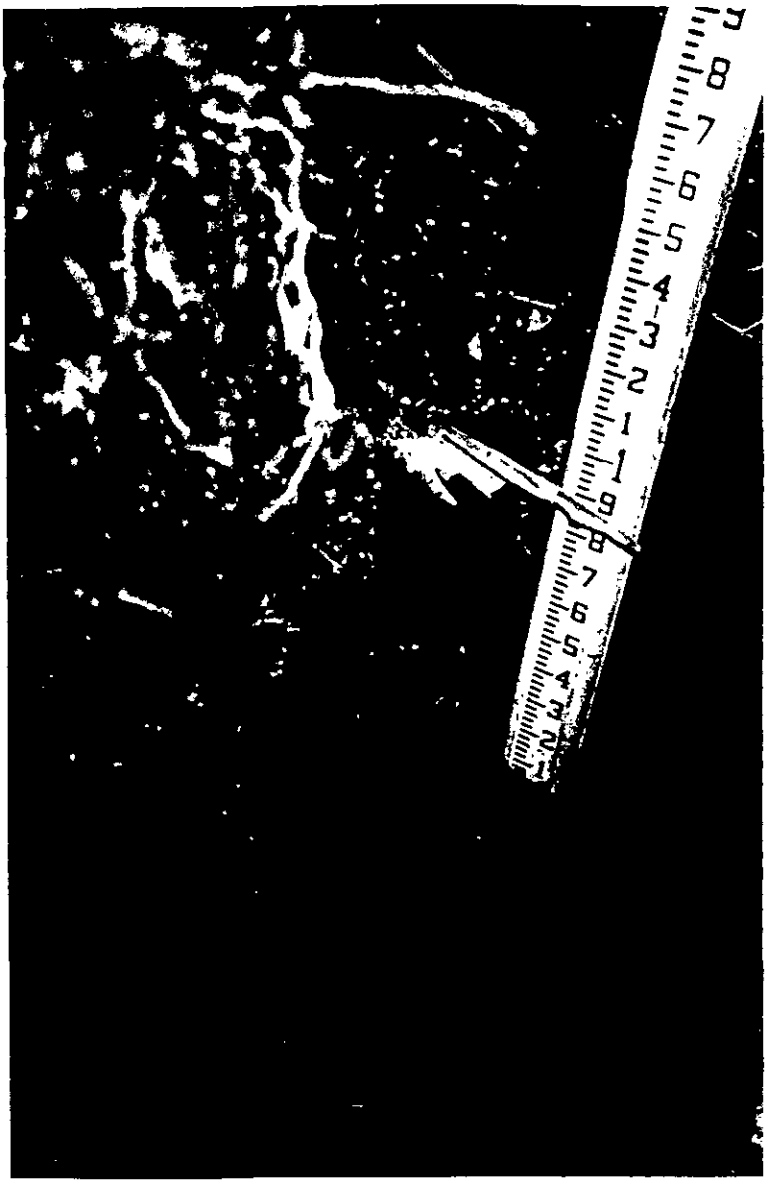


Plate 1-2



Plate 1-3



Plate 2-1



Plate 2-2

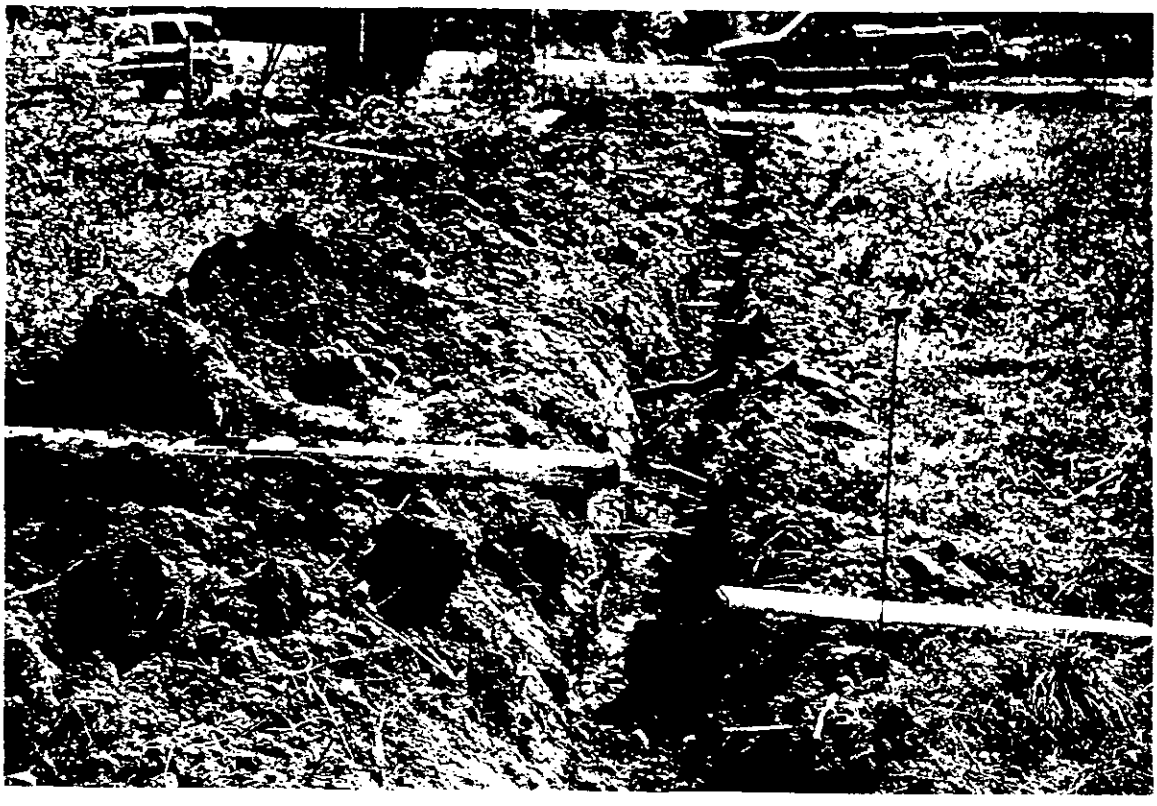


Plate 2-3



Plate 3-1



Plate 3-2

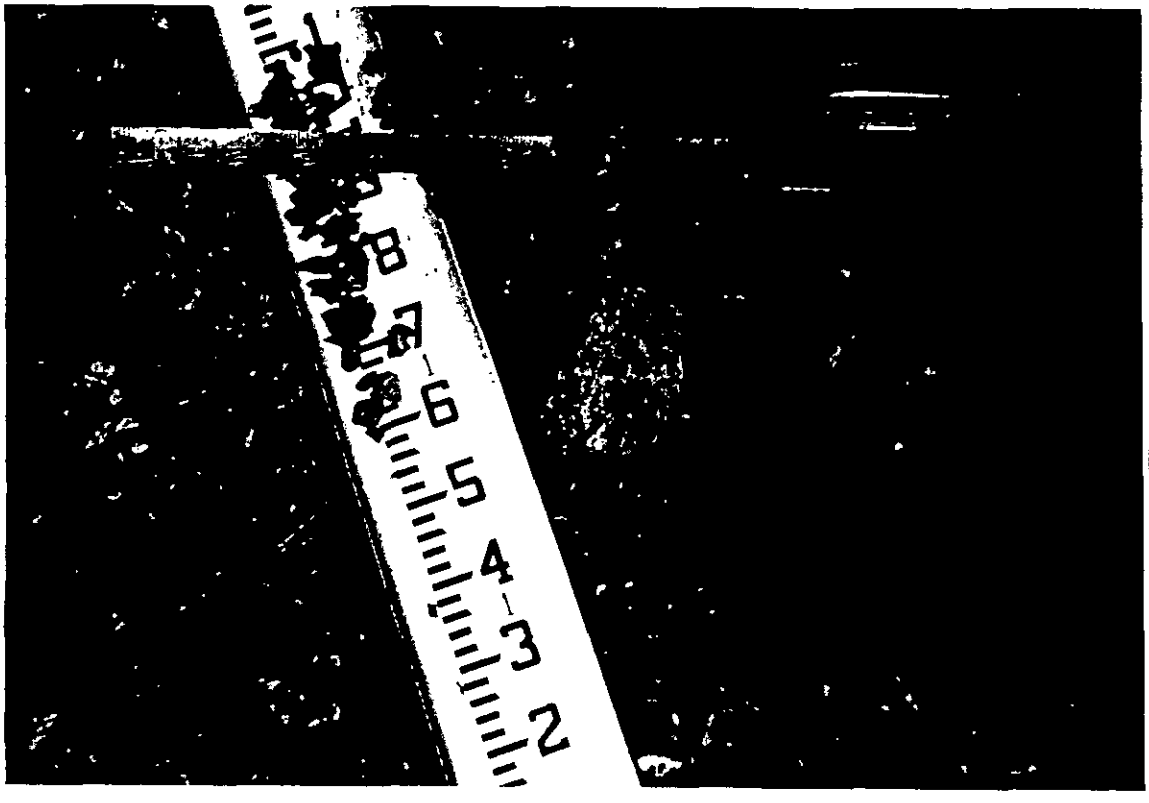


Plate 3-3

DEPARTMENT OF ENVIRONMENT, HEALTH, AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

12400

PROPERTY ID #: ____
COUNTY: ____

SOIL/SITE EVALUATION
for ON-SITE WASTEWATER SYSTEM

#2
1760B
PO 215-135-99
lot #5

OWNER: Charles Roger Marlin
ADDRESS: PO Box 23071, Charlotte
PROPOSED FACILITY: residence
LOCATION OF SITE: Phillips Acres
APPLICANT: ____
APPLICATION DATE: ____
PROPOSED DESIGN FLOW (.1949): 360gpd
DATE EVALUATED: ____
PROPERTY SIZE: .46
PROPERTY RECORDED: ____
WATER SUPPLY: ☐ Private ☑ Public ☐ Well ☐ Spring ☐ Other ____
EVALUATION METHOD: ☑ Auger Boring ☐ Pit ☐ Cut
TYPE OF WASTEWATER: ☑ Sewage ☐ Industrial Process ☐ Mixed

PROFILE #	Slopes 4-6% .1940 LANDSCAPE POSITION/ SLOPE %	HORIZON DEPTH (IN.)	SOIL MORPHOLOGY (.1941) .1941 STRUCTURE/ TEXTURE	SOIL MORPHOLOGY (.1941) .1941 CONSISTENCE/ MINERALOGY	OTHER PROFILE FACTORS .1942 SOIL WETNESS/ COLOR	.1943 SOIL DEPTH	.1956 SAPRO CLASS	.1944 RESTR HORIZ	PROFI CLAS & LT/
1	LS	0-5"	gr/cl	Fr/SEXP SS/SP	>46" TO soil wetness	46"	~~None~~ N/A	None	PS .35gpd/ft IV
		5-46"	SBK/C	Fi/SEXP SP					
2	LS	0-4"	gr/cl	Fr/SEXP SS/SP	>46" TO soil wetness	46"	N/A	None	PS .35gpd/ft IV
		4-46"	SBK/C	Fi/SEXP SP					
3	LS	0-6"	gr/cl	Fr/SEXP SS/SP	>46" TO soil wetness	46"	N/A	none	PS .35gpd/ft IV
		6-46"	SBK/C	Fi/SEXP SP					
4	LS	0-8"	gr/scl	Fr/SEXP SS/SP	>46" TO soil wetness	46"	N/A	None	PS .35gpd/ft IV
		8-46"	SBK/C	Fi/SEXP SP					
5	LS	0-6"	gr/scl	Fr/SEXP SS/SP	>46" TO soil wetness	46"	N/A	None	PS .35gpd/ft IV
		6-46"	SBK/C	Fi/SEXP SP					

DESCRIPTION	INITIAL SYSTEM	REPAIR SYSTEM
Available Space (.1945)	US	US
System Type(s)		

OTHER FACTORS (.1946): ____
SITE CLASSIFICATION (.1948): Unsuitable
EVALUATED BY: W.R. Marlin 3-17-97
OTHER(S) PRESENT: LSS

OMMENTS: 1000 Regan

LEGEND

use the following standard abbreviations

ANDSCAPE POSITION	GROUP	SOIL TEXTURE	CONVENTIONAL ,1955 LTAR	LPP ,1957 LTAR	MINERALOGY/ CONSISTENCE	STRUCTURE
C (Concave Slope) V (Convex Slope) (Drainage Way) S (Debris Slump) P (Flood Plain) S (Foot Slope) (Head Slope) (Linear Slope) (Nose Slope) (Ridge) (Shoulder Slope) (Terrace)	I	S (Sand) LS (Loamy Sand)	1.2 - 0.8	0.6 - 0.4	NEXP (Non-expansive) SEXP (Slightly Expansive) EXP (Expansive)	G (Single Grain) M (Massive) CR (Crumb) GR (Granular) SBK (Subangular Blocky) ABK (Angular Blocky) PL (Platy) PR (Prismatic)
	II	SL (Sandy Loam) L (Loam)	0.8 - 0.6	0.4 - 0.3		
	III	SI (Silt) SICL (Silty Clay Loam) CL (Clay Loam) SCL (Sandy Clay Loam) SLC (Silt Loam Clay)	0.6 - 0.3	0.3 - 0.15		
	IV	SC (Sandy Clay) SIC (Silty Clay)	0.4 - 0.1	0.2 - 0.05		
		O (Organic)	None			

	MOIST	WET
	VFR (Very Friable)	NS (Non-sticky)
	FR (Friable)	SS (Slightly Sticky)
	FI (Firm)	S (Sticky)
	VFI (Very Firm v. Very Sticky)	VS (Very Sticky)
	EFI (Extremely Firm)	NP (Non-plastic)
		SP (Slightly Plastic)
		P (Plastic)
		VP (Very Plastic)

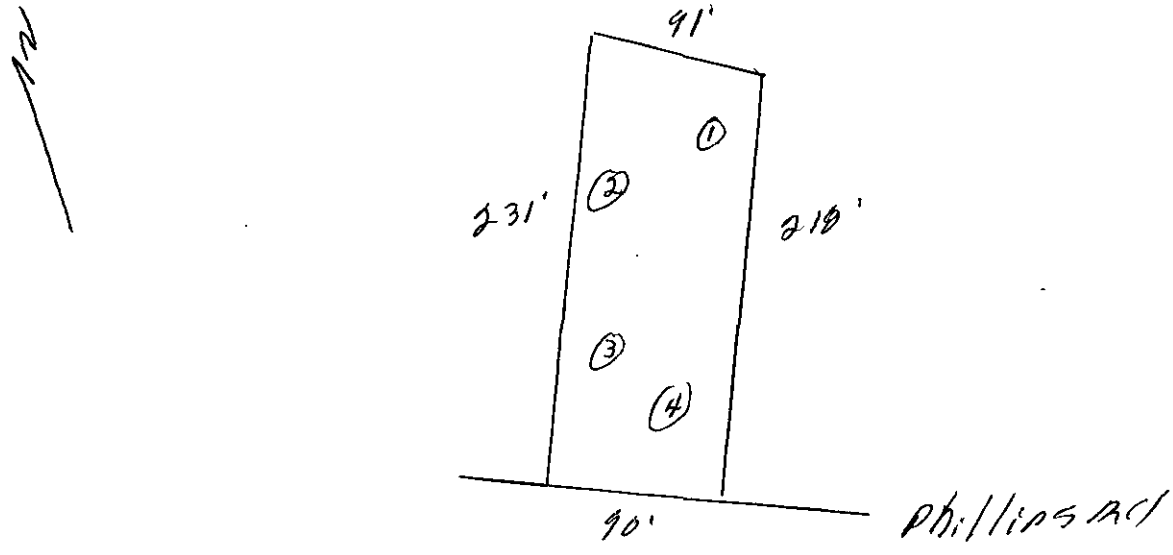
OTES

ORIZON DEPTH	In inches below natural soil surface
EPTH OF FILL	In inches from land surface
ESTRICTIVE HORIZON	Thickness and depth from land surface
APROLITE	S(suitable) or U(unsuitable)
OIL WETNESS	Inches from land surface to free water or inches from land surface to soil colors with chroma 2 or less - record Munsell color chip designation
LASSIFICATION	S (Suitable), PS (Provisionally Suitable), or U (Unsuitable)

valuation of saprolite shall be by pits.
ong-term Acceptance Rate (LTAR): gal/day/ft²

Show profile locations and other site features (dimensions, reference or benchmark, and North).

1760B



Mecklenburg County
Health Department

March 24, 1997

Mr. Roger Martin
P. O. Box 23071
Charlotte, NC 28227

Re: Phillips Road
File: 1760B
Parcel: 215-135-99PO

Dear Mr. Martin:

Receipt of your Application for Improvement Permit for the above referenced property is acknowledged. A soil evaluation and a site visit have been conducted. The results of the evaluation indicated that the site is **UNSUITABLE** under Rule .1945 **AVAILABLE SPACE.** For this reason your Application for Improvement Permit is denied. A possible way to develop the site exists under Rule .1948(d) which reads as follows:

> A site classified as **UNSUITABLE** may be used for a ground absorption sewage treatment and disposal system specifically identified in Rules .1955, .1956, or .1957 of this Section or a system approved under Rule .1969 if written documentation, including engineering, hydrogeologic, geologic or soil studies, indicates to the local health department that the proposed system can be expected to function satisfactorily. Such sites shall be reclassified as **PROVISIONALLY SUITABLE** if the local health department determines that the substantiating data indicate that:
> (1) a ground absorption system can be installed so that the effluent will be non-pathogenic, non-infectious, non-toxic, and non-hazardous;
> (2) the effluent will not contaminate ground or surface water; and
> (3) the effluent will not be exposed on the ground surface or be discharged to surface waters where it could come in contact with people, animals, or vectors.

The State shall review the substantiating data if requested by the local health department.

Please be advised that you have the right to an informal review by this department. You also have the right to appeal under G.S. 130A-24, and to have the appeal held in Mecklenburg County.

If you have any questions regarding this matter, please call me at 336-5575.

Sincerely,

Kelly Randall, R.S., Soil Scientist
Individual Water and Wastewater Systems

Mecklenburg County
Health Department

Roger Martin
Po Box 23071
Char 28227

Re: Phillip Road
File: 1760 B
Parcel: PO 215-135-99

Receipt of your Application for Improvement Permit for the above referenced property is acknowledged. A soil evaluation and a site visit have been conducted. The results of the evaluation indicated that the site is **UNSUITABLE** under Rules over For these reasons your Application for Improvement Permit is denied. A possible way to develop the site exists under Rule .1948(d) which reads as follows:

> A site classified as **UNSUITABLE** may be used for a ground absorption sewage treatment and disposal system specifically identified in Rules .1955, .1956, or .1957 of this Section or a system approved under Rule .1969 if written documentation, including engineering, hydrogeologic, geologic or soil studies, indicates to the local health department that the proposed system can be expected to function satisfactorily. Such sites shall be reclassified as **PROVISIONALLY SUITABLE** if the local health department determines that the substantiating data indicate that:
> (1) a ground absorption system can be installed so that the effluent will be non-pathogenic, non-infectious, non-toxic, and non-hazardous;
> (2) the effluent will not contaminate groundwater or surface water; and
> (3) the effluent will not be exposed on the ground surface or be discharged to surface waters where it could come in contact with people, animals, or vectors.
> The State shall review the substantiating data if requested by the local health department.

Please be advised that you have the right to an informal review by this department. You also have the right to appeal under G.S. 130A-24, and to have the appeal held in Mecklenburg County.

If you have any questions regarding this matter, please call me at 336-5575.

Sincerely,

Kelly Randall, R.S., Soil Scientist
Individual Water and Wastewater Systems

FEE: 100.00
DATE: 2-14-97 2-4-97
CK# 3235

APPLICATION FOR IMPROVEMENT PERMIT FOR RESIDENTIAL SITE INDIVIDUAL WATER AND WASTEWATER SYSTEMS PROGRAM

1 1 CRT

TYPE APPLICATION: ✓ NEW SYSTEM __ EXPANSION/ ALTERATION OF EXISTING SYSTEM __ REPAIR OF EXISTING SYSTEM

NORTH CAROLINA
DEPARTMENT OF ENVIRONMENT,
HEALTH, AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

FILE #: 17603

PROPERTY INFORMATION (FROM ENGINEERING FORM) FOR JOB LOCATION:

TAX/PARCEL NUMBER: P.O. 215-135-99

STREET ADDRESS: Phillips Road

SUBDIVISION OR MOBILE HOME PARK NAME: Phillips Trace

LOT NUMBER: 5

TYPE OF BUILDING (CHECK ONE):

__ SINGLE MOBILE HOME(S)
__ DOUBLE WIDE (D)
✓ HOUSE (H)
__ MODULAR HOME (M)
__ MULTIPLE FAMILY (U)
__ OTHER (O)

TOWNSHIP (CHECK ONE):

__ 0 MECKLENBURG
__ 1 CHARLOTTE
__ 2 DAVIDSON
__ 3 CORNELIUS
__ 4 PINEVILLE
✓ 5 MATTHEWS
__ 6 HUNTERSVILLE
__ 7 MINT HILL

HEATED SQUARE FOOTAGE: 1,500 ±

NUMBER OF BEDROOMS: 3 NUMBER OF OCCUPANTS: 4

CLOSING DATE Pre-Construction

FOUNDATION FOR RESIDENCE:

__ WITHOUT BASEMENT
__ ON SLAB
✓ CRAWL SPACE
__ WITH BASEMENT /PLUMBING
__ WITH BASEMENT /NO PLUMBING

IF EXPANSION/ALTERATION OF EXISTING SYSTEM, DESCRIBE THE PROPOSED BUILDING ADDITION:

WILL THERE BE A HOME BUSINESS IN THE RESIDENCE: __ YES ✓ NO TYPE: _____

WATER SUPPLY (CHECK ONE):
__ COMMUNITY (C)
✓ MUNICIPAL (M)
__ PRIVATE WELL (P)
__ SHARED WELL (S)
__ OTHER 'SPRINGS' (O)

IF ANY OF THE FOLLOWING ARE LOCATED ON THE PROPERTY, PLEASE SHOW LOCATION ON PLAT:

BURIED CABLES, LANDFILLS, STUMPHOLES	__ YES ✓ NO	WELL, SPRINGS OR WATERLINES	__ YES ✓ NO
EXISTING WASTEWATER SYSTEMS	__ YES __ NO	DESIGNATED WETLANDS	__ YES ✓ NO
EASTMENTS OR RIGHT-OF-WAYS	__ YES ✓ NO		

PROPERTY OWNER:

NAME: Martin Charles Roger
(LAST) (FIRST) (MI)

ADDRESS: P.O. Box 23071

CITY: Char STATE: N.C. ZIP: 28227

DAYTIME PHONE: 704 -545-9461

LEGAL AGENT FOR PROPERTY OWNER, IF APPLICABLE:

NAME:
(LAST) (FIRST) (MI)

DAYTIME PHONE: ( ) -

WHAT DATE WAS THE PROPERTY ORIGINALLY DEEDED AND RECORDED? 1-13-97

An Improvement Permit is subject to suspension or revocation if site plans or the intended use change or if information submitted in this application is falsified or changed. The undersigned, owner, or legal agent for the owner, of the property described above as the "Job Location" has read the foregoing application, acknowledges that the contents of same are true, and authorizes agents of the Mecklenburg County Health Department to enter onto the property for the purpose of processing this request.

SIGNED _____ DATE: 2-15-97

MECKLENBURG COUNTY HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
c/o HAL MARSHALL CTR., SUITE 211, 700 N. TRYON ST., CHARLOTTE, N.C. 28202., (704) 336-5102

PROPOSED PLOT PLAN

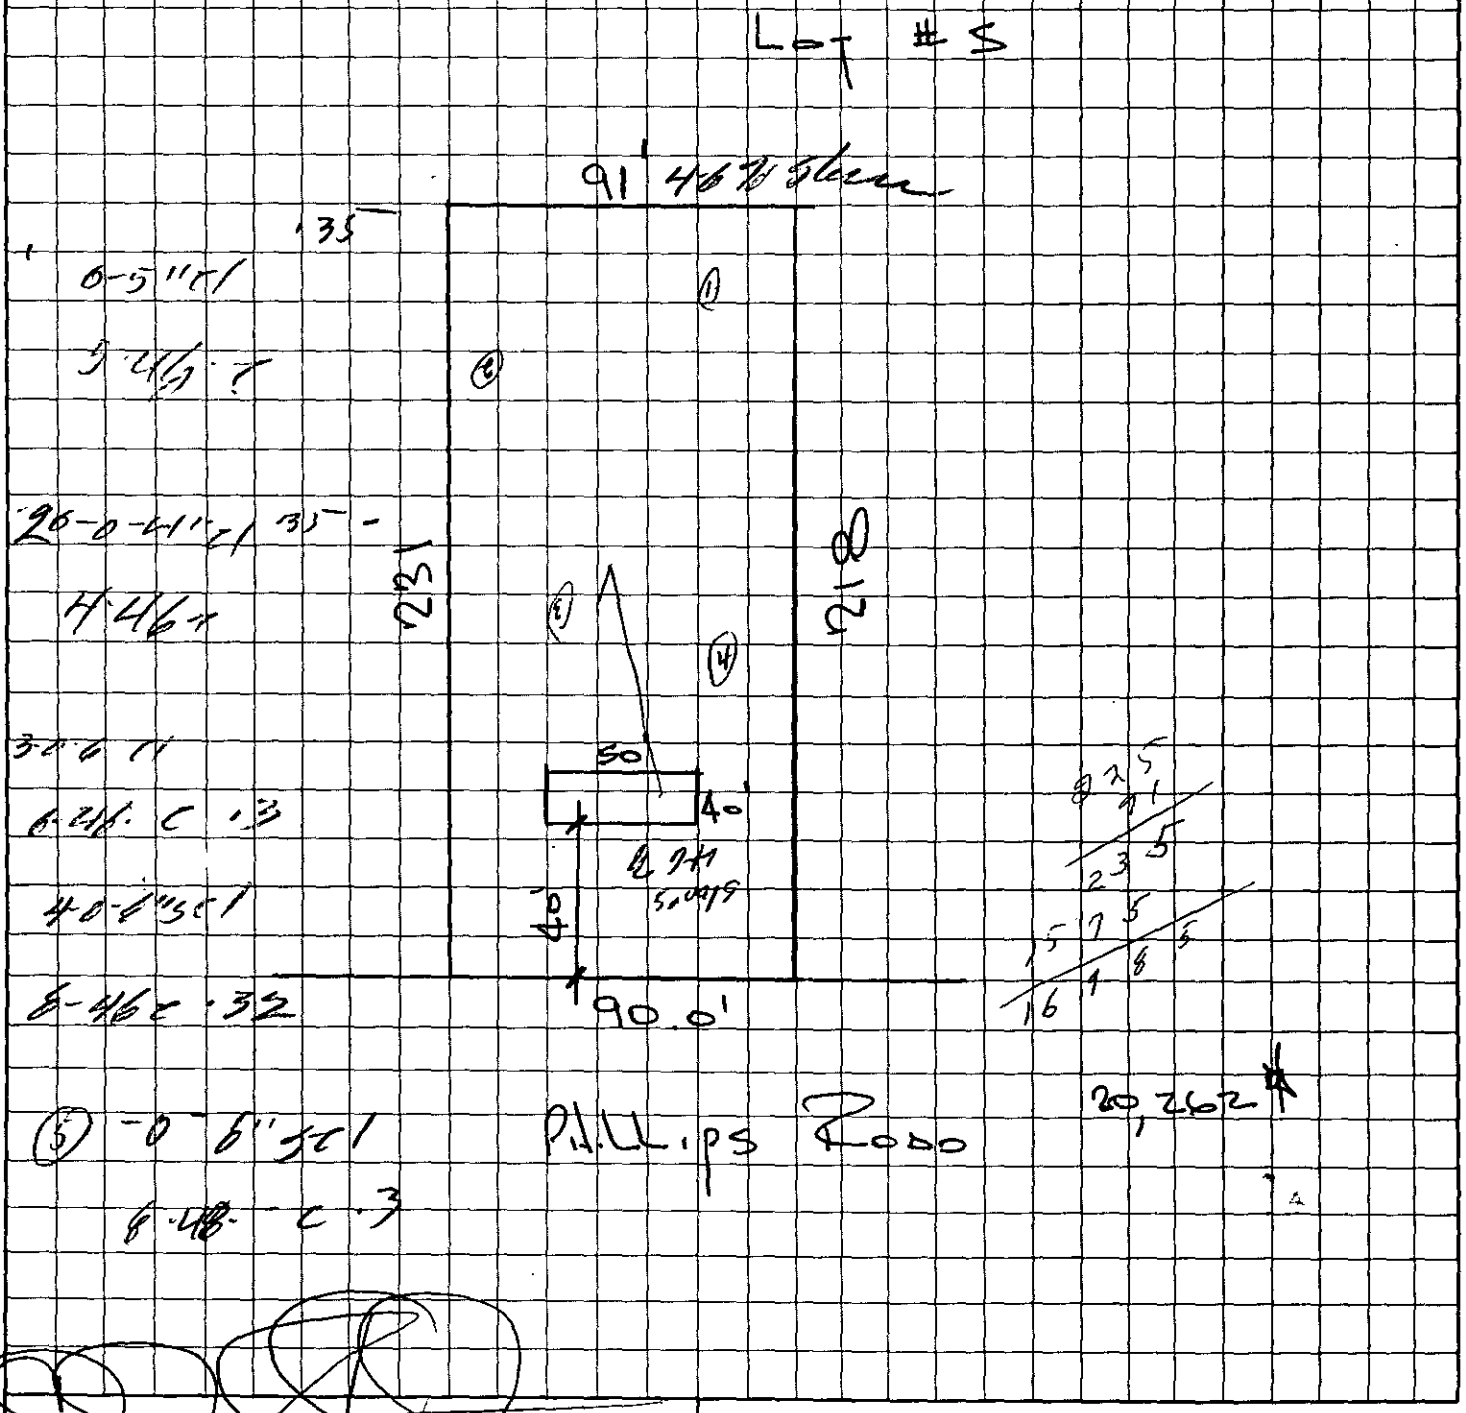
Lot #5

HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON STREET
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 1760B

TC: 215-135-9980

Draw in and name all roads adjoining the property. Draw in and accurately dimension the lot concerned. Accurately indicate property boundaries proposed and/or existing structures and driveways, underground utilities, and wells and springs within 100 feet of the proposed building or drainfield.



OWNER/AGENT SIGNATURE

DATE 2-15-97

APPROVAL DATE _____

White - Health Department's Copy Canary - E.H.S. Copy Pink - Owner's Copy

DEPARTMENT OF ENVIRONMENT, HEALTH, AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

PROPERTY ID #: 4
COUNTY: 2

SOIL/SITE EVALUATION
for ON-SITE WASTEWATER SYSTEM

#2
1760B
PO 215-135-97
Lot #5

OWNER: Charles Roger Marlin
APPLICANT:
DATE EVALUATED:
ADDRESS: PO Box 23071, Charleston
APPLICATION DATE:
PROPERTY SIZE: 46
PROPOSED FACILITY: residence
PROPOSED DESIGN FLOW (.1949): 360gpd
PROPERTY RECORDED:
LOCATION OF SITE: Phillips Acres
WATER SUPPLY: ☐ Private ☑ Public ☐ Well ☐ Spring ☐ Other
EVALUATION METHOD: ☑ Auger Boring ☐ Pit ☐ Cut
TYPE OF WASTEWATER: ☑ Sewage ☐ Industrial Process ☐ Mixed

PROFILE #	1940 LANDSCAPE POSITION/ SLOPE %	HORIZON DEPTH (IN.)	SOIL MORPHOLOGY (.1941) 1941 STRUCTURE/ TEXTURE	1941 CONSISTENCE/ MINERALOGY	OTHER PROFILE FACTORS 1942 SOIL WETNESS/ COLOR	1943 SOIL DEPTH	1956 SAPRO CLASS	1944 RESTR HORIZ	PROF CLA & LT
1	LS	0-5"	gr/cl	Fr/SEXP SS/SP	>46" TO soil wetness	46"	N/A	None	PS .38 IV
		5-48"	SBM/C	F:/SEXP/ S/P					
2	LS	0-4"	gr/cl	Fr/SEXP SS/SP	>46" TO soil wetness	48"	N/A	None	PS .35 IV
		4-46"	SBM/C	F:/SEXP S/P					
3	LS	0-6"	gr/cl	Fr/SEXP SS/SP	>46" TO soil wetness	46"	N/A	None	PS .39 IV
		6-46"	SBM/C	F:/SEXP S/P					
4	LS	0-8"	gr/scl	Fr/SEXP SS/SP	>46" TO soil wetness	46"	N/A	None	PS .35 IV
		8-46"	SBM/C	F:/SEXP S/P					
5	LS	0-8"	gr/scl	Fr/SEXP SS/SP	>46" TO soil wetness	46"	N/A	None	PS .3 IV
		8-48"	SBM/C	F:/SEXP S/P					

DESCRIPTION	INITIAL SYSTEM	REPAIR SYSTEM
Available Space (.1945)	US	US
System Type(s)		

OTHER FACTORS (.1946):
SITE CLASSIFICATION (.1948): Unsuitable
EVALUATED BY: W. R. Marlin 3-17-97
OTHER(S) PRESENT: LSS

OMMENTS: Toobkeyer

LEGEND

use the following standard abbreviations

ANDSCAPE POSITION	GROUT	SOIL TEXTURE	CONVENTIONAL 1955 LTAR	LPP 1957 LTAR	MINERALOGY/ CONSISTENCE	STRUCTURE
C (Concave Slope)	I	S (Sand)	1.2 - 0.8	0.6 - 0.4	NEXP (Non-expansive)	G (Single Grain)
V (Convex Slope)		LS (Loamy Sand)			SEXP (Slightly Expansive)	M (Massive)
(Drainage Way)					EXP (Expansive)	CR (Crumb)
S (Debris Slump)	II	SL (Sandy Loam)	0.8 - 0.6	0.4 - 0.3		GR (Granular)
P (Flood Plain)		L (Loam)				SBK (Subangular Blocky)
S (Foot Slope)						ABK (Angular Blocky)
(Head Slope)	III	SI (Silt)	0.6 - 0.3	0.3 - 0.15		PL (Platy)
(Linear Slope)		SICL (Silty Clay Loam)				PR (Prismatic)
(Nose Slope)		CL (Clay Loam)			MOIST	WET
(Ridge)		SCL (Sandy Clay Loam)				
(Shoulder Slope)		SLC (Silt Loam Clay)			VFR (Very Friable)	NS (Non-sticky)
(Terrace)					FR (Friable)	SS (Slightly Sticky)
	IV	SC (Sandy Clay)	0.4 - 0.1	0.2 - 0.05	FI (Firm)	S (Sticky)
		SIC (Silty Clay)			VFI (Very Firm v. Very Sticky)	VS (Very Sticky)
					EFI (Extremely Firm)	NP (Non-plastic)
		O (Organic)	None			SP (Slightly Plastic)
						P (Plastic)
						VP (Very Plastic)

OTES

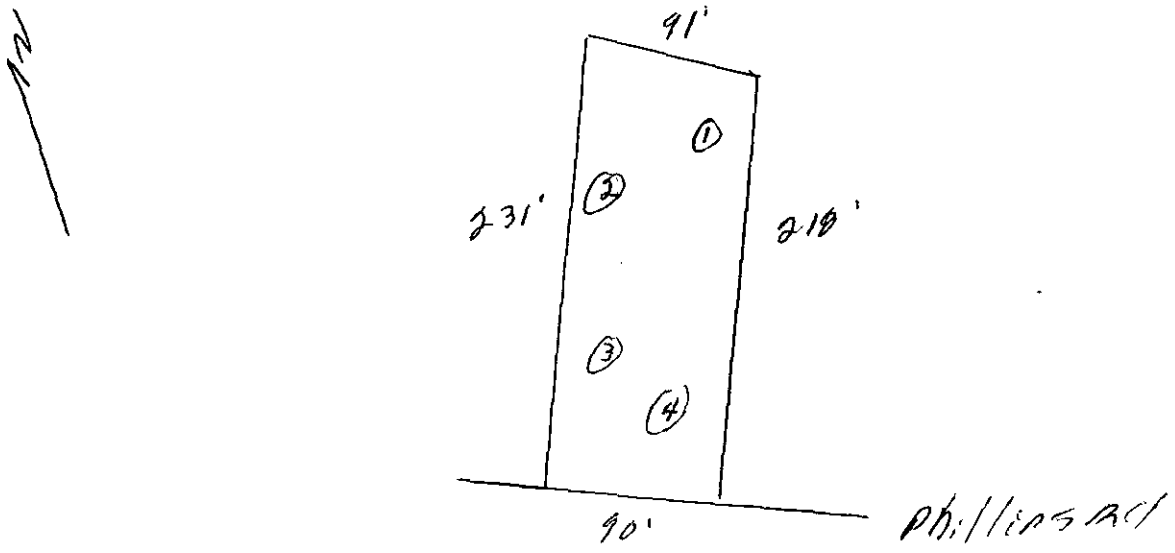
ORIZON DEPTH	In inches below natural soil surface
EPTH OF FILL	In inches from land surface
ESTRICTIVE HORIZON	Thickness and depth from land surface
APROLITE	S(suitable) or U(unsuitable)
OIL WETNESS	Inches from land surface to free water or inches from land surface to soil colors with chroma 2 or less - record Munsell color chip designation
LASSIFICATION	S (Suitable), PS (Provisionally Suitable), or U (Unsuitable)

valuation of saprolite shall be by pits.

ong-term Acceptance Rate (LTAR): gal/day/ft²

Show profile locations and other site features (dimensions, reference or benchmark, and North).

1760B



FEE: 100.00

DATE: 2-14-97 2-14-97

CK# 3235

APPLICATION FOR IMPROVEMENT PERMIT FOR RESIDENTIAL SITE INDIVIDUAL WATER AND WASTEWATER SYSTEMS PROGRAM

[ ] CRT

TYPE APPLICATION: ✓ NEW SYSTEM __ EXPANSION/ ALTERATION OF EXISTING SYSTEM __ REPAIR OF EXISTING SYSTEM

NORTH CAROLINA
DEPARTMENT OF ENVIRONMENT,
HEALTH, AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

FILE #: 1760B

PROPERTY INFORMATION (FROM ENGINEERING FORM) FOR JOB LOCATION:

TAX/PARCEL NUMBER: P.O. 215-135-99

STREET ADDRESS: PHILLIPS ROAD

SUBDIVISION OR MOBILE HOME PARK NAME: PHILLIPS TRACE

LOT NUMBER: 5

TYPE OF BUILDING (CHECK ONE):

__ SINGLE MOBILE HOME(S)
__ DOUBLE WIDE (D)
✓ HOUSE (H)
__ MODULAR HOME (M)
__ MULTIPLE FAMILY (U)
__ OTHER (O)

TOWNSHIP (CHECK ONE):

__ 0 MECKLENBURG
__ 1 CHARLOTTE
__ 2 DAVIDSON
__ 3 CORNELIUS
__ 4 PINEVILLE
✓ 5 MATTHEWS
__ 6 HUNTERSVILLE
__ 7 MINT HILL

HEATED SQUARE FOOTAGE: 1,500 ±

NUMBER OF BEDROOMS: 3 NUMBER OF OCCUPANTS: 4

CLOSING DATE: PRE-CONSTRUCTION

FOUNDATION FOR RESIDENCE:

__ WITHOUT BASEMENT
__ ON SLAB
✓ CRAWL SPACE
__ WITH BASEMENT /PLUMBING
__ WITH BASEMENT /NO PLUMBING

IF EXPANSION/ALTERATION OF EXISTING SYSTEM, DESCRIBE THE PROPOSED BUILDING ADDITION:

WILL THERE BE A HOME BUSINESS IN THE RESIDENCE: __ YES ✓ NO TYPE: _____

WATER SUPPLY (CHECK ONE):
__ COMMUNITY (C)
✓ MUNICIPAL (M)
__ PRIVATE WELL (P)
__ SHARED WELL (S)
__ OTHER 'SPRINGS' (O)

IF ANY OF THE FOLLOWING ARE LOCATED ON THE PROPERTY, PLEASE SHOW LOCATION ON PLAT:

BURIED CABLES, LANDFILLS, STUMPHOLES __ YES ✓ NO
EXISTING WASTEWATER SYSTEMS __ YES __ NO
EASTMENTS OR RIGHT-OF-WAYS __ YES ✓ NO
WELL, SPRINGS OR WATERLINES __ YES ✓ NO
DESIGNATED WETLANDS __ YES ✓ NO

PROPERTY OWNER:

NAME: Martin Charles Roger
(LAST) (FIRST) (MI)

ADDRESS: P.O. Box 23071

CITY: Char STATE: N.C. ZIP: 28227

DAYTIME PHONE: 704 -545-9461

LEGAL AGENT FOR PROPERTY OWNER, IF APPLICABLE:

NAME:
(LAST) (FIRST) (MI)

DAYTIME PHONE: ( ) -

WHAT DATE WAS THE PROPERTY ORIGINALLY DEEDED AND RECORDED? 1-13-97

An Improvement Permit is subject to suspension or revocation if site plans or the intended use change or if information submitted in this application is falsified or changed. The undersigned, owner, or legal agent for the owner, of the property described above as the "Job Location" has read the foregoing application, acknowledges that the contents of same are true, and authorizes agents of the Mecklenburg County Health Department to enter onto the property for the purpose of processing this request.

SIGNED: [signature] DATE: 2-15-97

MECKLENBURG COUNTY HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
c/o HAL MARSHALL CTR., SUITE 211, 700 N. TRYON ST., CHARLOTTE, N.C. 28202., (704) 336-5102

PROPOSED PLOT PLAN

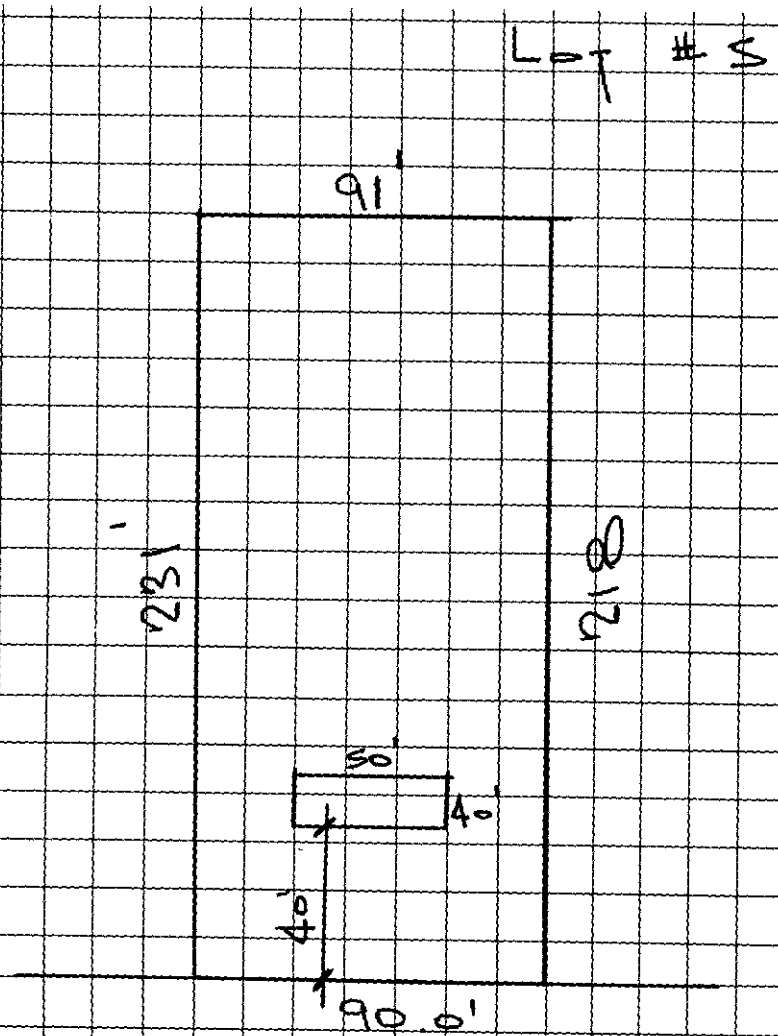
Lot #5

HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON STREET
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 1760B

TC: 215-135-99P0

Draw in and name all roads adjoining the property. Draw in and accurately dimension the lot concerned. Accurately indicate property boundaries proposed and/or existing structures and driveways, underground utilities, and wells and springs within 100 feet of the proposed building or drainfield.



OWNER/AGENT SIGNATURE

DATE 2-15-97

APPROVAL DATE _____

White - Health Department's Copy

Canary - E.H.S. Copy

Pink - Owner's Copy
