5

Date Received 3-27-73

APT No 5838

T C No

Map Date

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

APPLICATION FOR PERCOLATION TEST

1) NAME OF OWNER Robinson (LAST) Larry (FIRST) James (MIDDLE)

2) ADDRESS OF OWNER 2336 Julia Ave. Ft S ZIP 28206

3) PHONE NO Home 377-1834 Office 333-8691


4) LOCATION OF PROPERTY Off Mallard Ck. Church Rd Breezewood Dr (STREET OR COUNTY ROAD)

5) SUBDIVISION Homewood Acers (Breezewood Dr.) LOT NO 1 BLOCK NO. B

MAP BOOK NO PAGE NO.

6) DEED REFERENCE DEED BOOK PAGE NO.

Application is hereby made to the Mecklenburg County Health Department for the conduct of a percolation test and an on site inspection of the lot hereinabove described for the purpose of determining if the lot is suitable for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge.

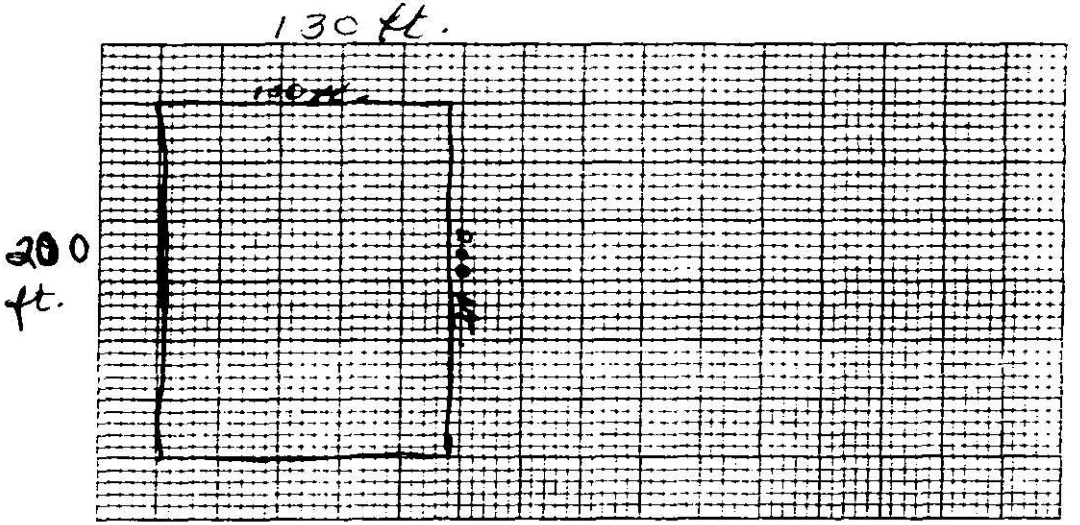

7) ACCURATELY DIAGRAM & DIMENSION LOT

Mrs. Larry J. Robinson
OWNER

FORM NO. E-1-9-1-72

HEALTH DEPARTMENT'S COPY

MECKLENBURG COUNTY HEALTH DEPARTMENT
INTER-OFFICE COMMUNICATION

DATE: November 23, 1973

TO: Randy Reynolds
Environmentalist

FROM: W. Everette Lynn, Jr.
Soil Scientist

SUBJECT: APT #5838 (L. Robinson)
Lot No. 1, Block B, Breezewood Drive
11-23-73

Soils were found to be of the Iredell series. These soils have very plastic and sticky clay subsoils which contain swelling clay minerals. They may also have a perched high water table during periods of high rainfall. These factors result in inadequately slow percolation rate and permeability.

Based on this investigation, it is recommended that the lot be disapproved for installation of a septic tank system.

WEL:jdg

MECKLENBURG COUNTY
Department of Public Health
1200 Blythe Boulevard
Charlotte, North Carolina 28203

Telephone 374-2113
P.O. 029-142-[illegible]
9-5-73

Nov. 23, 1973
Date Issued

1. April 10, 1973
2. _____
3. _____

SITE DISAPPROVAL REPORT
INDIVIDUAL SEPTIC TANK SYSTEM WITH SUBSURFACE, SOIL ABSORPTION, EFFLUENT DISCHARGE

SDR No. 5838
T.C. No. _____

NAME OF OWNER Robinson, Larry James

ADDRESS OF OWNER 2336 Julia Ave., #5 ZIP 28206

LOCATION OF LOT Breezewood Drive, Lot 1-B

The lot described above has been disapproved for the installation of an individual septic tank system with subsurface, soil absorption, effluent discharge due to the following:

FAILURE TO PASS PERCOLATION TEST (60 minutes per inch or less)

	Test No.	Date of Test	Percolation Rate
X	1.	4-9-73	350 min/in
X	2.	4-25-73	300 min/in
X	3.	5-15-73	180 min/in

X

11-23-73 - Soils were found to be of the Iredell series. These soils have very plastic and sticky clay subsoils

ON SITE INSPECTION REVEALED OTHER REASONS WHICH MAY BE CORRECTABLE THAT CONTRIBUTE TO THE DISAPPROVAL

_____ have a perched high water table during periods of high rainfall. These factors result in inadequately slow percolation rate and permeability.

Soil Scientist

Environmentalist

(Stencil No.)
MMD 396
8/70

FORM NO.
R-19-8-14-70

MECKLENBURG COUNTY
Department of Public Health

1200 Blythe Boulevard
Charlotte, North Carolina 28203
Telephone 374-2113

Date Issued
1. 4-10-73
2. 11-23-73
3. 6-3-74*

SITE DISAPPROVAL REPORT
INDIVIDUAL SEPTIC TANK SYSTEM WITH SUBSURFACE, SOIL ABSORPTION, EFFLUENT DISCHARGE

SDR No. 5838
T.C. No. Portion Of 029-142-05
9-5-73

NAME OF OWNER Robinson, Larry James

ADDRESS OF OWNER 2336 Julia Ave., #5 ZIP 28206

LOCATION OF LOT Breezewood Drive, Lot 1-B

The lot described above has been disapproved for the installation of an individual septic tank system with subsurface, soil absorption, effluent discharge due to the following:

FAILURE TO PASS PERCOLATION TEST (60 minutes per inch or less)

	Test No.	Date of Test	Percolation Rate
X	1.	4-9-73	350 min/in
X	2.	4-25-73	300 min/in
X	3.	5-15-73	180 min/in

X ON SITE INSPECTION REVEALED LOT TO BE UNSUITABLE FOR THE FOLLOWING REASON(S) 11-23-73 - Soils were found to be of the Iredell series. These soils have very plastic and sticky clay subsoils which contain swelling clay minerals. They may also have a perched high water table during periods of high rainfall. These factors result in inadequately slow percolation rate and permeability.

*Soil analysis confirmed on 5-31-74.

Soil Scientist

Environmentalist

(Stencil No.)
HHD 398
8/70

FORM NO.
E-19-8-14-70
