R

Date Received 9-11-73

APT No. 6974

T. C. No.

Map Date

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

APPLICATION FOR PERCOLATION TEST

1) NAME OF OWNER MARTIN (LAST) FRED (FIRST) ALVIN (MIDDLE)

2) ADDRESS OF OWNER P.O. BOX 12061 - CHARLOTTE, N.C. ZIP 28205

3) PHONE NO Home 372-3145 Office 334-7317


4) LOCATION OF PROPERTY BRIGHT ROAD EXTENSION (STREET OR COUNTY ROAD)

5) SUBDIVISION STAR HARBOR LOT NO 13 BLOCK NO "C"

MAP BOOK NO 113 PAGE NO 71

6) DEED REFERENCE DEED BOOK 1862 PAGE NO 259

Application is hereby made to the Mecklenburg County Health Department for the conduct of a percolation test and on on site inspection of the lot hereinabove described for the purpose of determining if the lot is suitable for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge

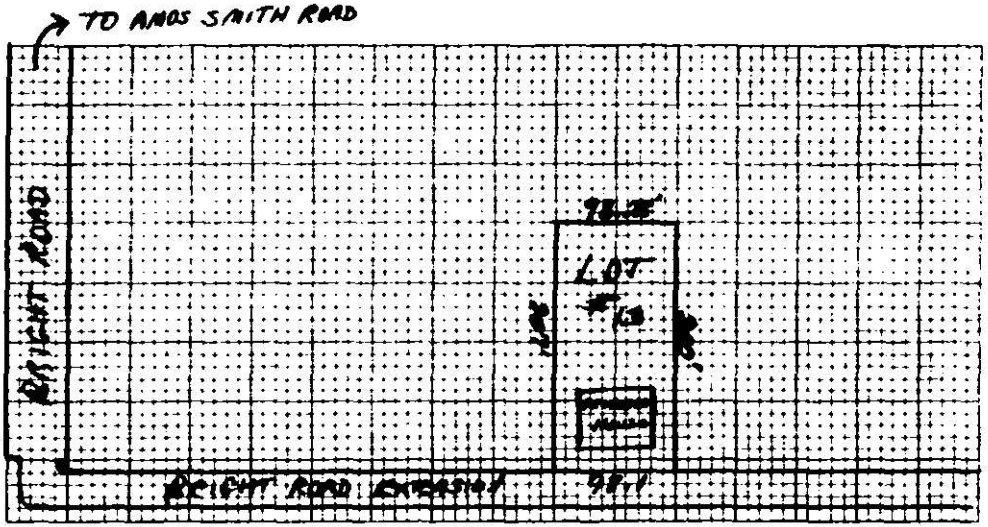

7) ACCURATELY DIAGRAM & DIMENSION LOT

NOTE: * WANT TO BUILD SMALL 2-BEDROOM BUNGALOW

Fred A. Martin
OWNER

FORM NO. E-1-11-1-70

HEALTH DEPARTMENT'S COPY

MECKLENBURG COUNTY
Department of Public Health

1200 Blythe Boulevard
Charlotte, North Carolina 28203
Telephone 374-2113

Date Issued
1. October 4, 1973
2. _____
3. _____

SITE DISAPPROVAL REPORT
INDIVIDUAL SEPTIC TANK SYSTEM WITH SUBSURFACE, SOIL ABSORPTION, EFFLUENT DISCHARGE

SDR No. 6974
T.C. No. _____

NAME OF OWNER Martin, Fred Alvin

ADDRESS OF OWNER P.O. Box 12061 ZIP 28205

LOCATION OF LOT Bright Road Extension, Lot 13-0

The lot described above has been disapproved for the installation of an individual septic tank system with subsurface, soil absorption, effluent discharge due to the following:

FAILURE TO PASS PERCOLATION TEST (60 minutes per inch or less)

	Test No.	Date of Test	Percolation Rate
X	1.	10-4-73	72+ min/in
____	2.	_____	_____ min/in
____	3.	_____	_____ min/in

X ON SITE INSPECTION REVEALED LOT TO BE UNSUITABLE FOR THE FOLLOWING REASON(S) 10-4-73 - unsuitable due to topography.

_____

_____

_____

_____
Environmentalist

(Stencil No.)
EHD 398
8/70

FORM NO.
E-19-8-14-70

MECKLENBURG COUNTY HEALTH DEPARTMENT

INTER-OFFICE COMMUNICATION

DATE: October 12, 1973

TO: Luther Bridgeman
Environmentalist

FROM: W. Everette Lynn, Jr. W.E.L.
Soil Scientist

SUBJECT: APT #6974 (F. A. Martin)
Lot No. 13, Block C, Bright Road Extension
Star Harbor Subdivision
10-11-73

Soils were found to be of the Cecil series. These soils have good drainage, good aeration and moderate permeability.

Topography of the lot was found to be slightly limiting; however, the soils seem to be adequately deep to prevent lateral seepage of effluent.

It is recommended that the lot be granted approval for a septic tank system. The system should be located down-slope from the perc. test site in order to install a gravity flow system. Design should be based on a 60 min./in. perc. rate.

WEL:jdg

Serial No. 3674

PTR No. 6974

Date Issued October 12, 1973

T C No 113-071-13

Map Date _____

Do Not Issue A Building Permit Based On This Form

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION


PERCOLATION TEST REPORT

NAME OF OWNER Martin (LAST) Fred (FIRST) Alvin (MIDDLE)

ADDRESS OF OWNER P.O. Box 12061 ZIP 28205

LOCATION OF PROPERTY Bright Road Extension (STREET OR COUNTY ROAD)

SUBDIVISION Star Harbor LOT NO 13 BLOCK NO C

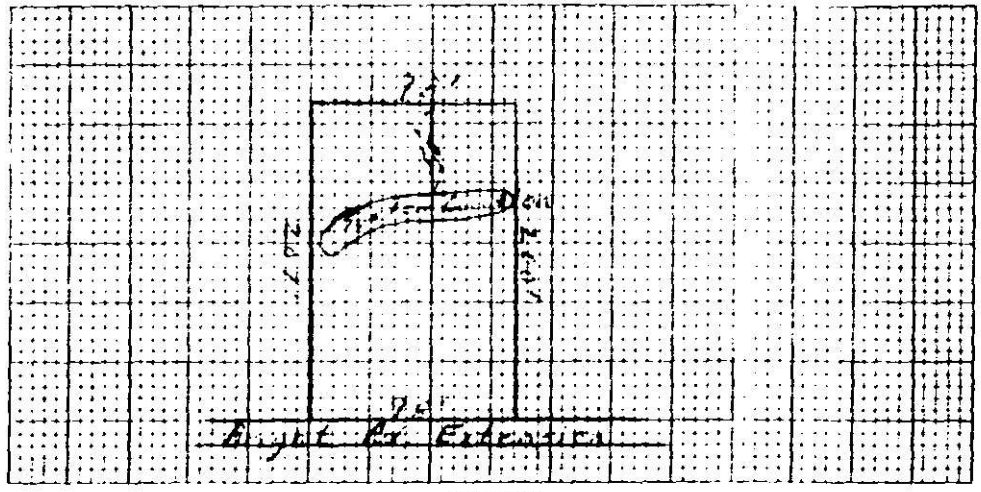

PLOT PLAN

This is to certify that a percolation test has been run and an on site inspection made by the Mecklenburg County Health Department on the lot described above. The said test was conducted on that portion of the lot as indicated on above plot.

The percolation rate determined by the test was 60 min/in* The said lot is approved for the installation of an individual septic tank wastewater treatment system with subsurface soil absorption effluent discharge subject to the following terms and conditions:

1. A permit to install, construct, alter or repair the specific system shall be obtained from the Mecklenburg County Health Department prior to the beginning of any construction of buildings or of the wastewater treatment system on the said lot.
2. The size of the septic tank wastewater treatment system which must be installed will be determined by the Health Department prior to installation based on the percolation rate obtained above, and on the size and type of building constructed thereon.
3. This approval is valid only if the system is installed in the immediate area where the percolation test was run.
4. This approval is void if any grading, filling, or construction (including the drilling of a well) is performed on the lot which, in the opinion of the Health Department, renders the area where the percolation test was run unsuitable for the installation, construction, alteration, and/or repair of such a system.

This approval is granted based on the laws of the State of North Carolina and the rules and regulations of the North Carolina State Board of Health and the Mecklenburg County Board of Health which were in effect on the date of issuance and is void if at any time in the future, prior to the completion of the system, these laws, rules, and regulations are changed such that this approval would not have been granted had the new or revised laws, rules, and regulations been in effect on the issue date.

* Results determined by soil analysis.

Director, Environmental Health Division or Authorized Section Head

FORM NO. E 2-4-1-71 by Everette Lynn, Jr. Soil Scientist

HEALTH DEPARTMENT'S COPY
