N.C. Department of Environment and Natural Resources
Division of Environmental Health

Inspection of Engineered Subsurface Wastewater System

Mecklenburg County	UNITER HOUSE OF PRAYER	5352B
Health Department	**Name of Establishment**	**Permit/Project No.**
5449 CHRISTENBURY RD	CHURCH	360
Location	**Type of Establishment**	**Design Flow**
UNITED HOUSE OF PRAYER	5449 CHRISTENBURY RD	
Owner/Agent	**Address**	**Phone**
NA	CHARLOTTE NC	
Operator	**Address**	**Phone**
IIIb	1/19/2010	1/19/2015
System Type	**Date of Inspection**	**Next Inspection Due**

	Yes	No	N/A	Comments:
1. ESTABLISHMENT:				
a. Type, size, and sewage flow in accordance with permit?	☒	☐	☐	
2. COLLECTION SYSTEM:				
a. No evidence of leaks into or out from sewer lines/manholes?	☒	☐	☐	
b. Free of blockages/solids buildup in lines or manholes?	☒	☐	☐	
3. TANKAGE: (Grease Traps/Lift Stations/Septic/Dosing Tanks)				
a. Tank risers accessible and surface water diverted?	☒	☐	☐	
b. Tanks and access manholes structurally sound, watertight?	☒	☐	☐	
c. Sanitary tee(s) in good working condition?.....	☐	☐	☒	3.c. Sanitary tee not inspected.
d. Tanks pumped, cleaned out as needed?.....	☒	☐	☐	
4. RAW SEWAGE LIFT STATION (if present):				
a. Required pumps present, operating, and cycling properly	☒	☐	☐	
b. High-water alarm present and operating properly?	☒	☐	☐	
c. Floats/pipe/valves/disconnects in good condition?	☒	☐	☐	
5. EFFLUENT DOSING SYSTEM:				
a. Effluent appears clear, free of excess solids?	☐	☐	☒	
A. PUMP SYSTEMS:				
a. Required pumps present, operating, and cycling properly?	☒	☐	☐	
b. High-water alarm present and operating properly?	☒	☐	☐	
c. Floats/pipe/valves/disconnects in good working condition?	☒	☐	☐	
d. Control panel enclosure/components in good condition?	☒	☐	☐	
e. Elapsed time readings: _____ _____ _____ _____				
B. SIPHON SYSTEMS:				
a. No evidence of overflow or siphon leakage?	☐	☐	☒	
b. Siphon(s) appear to be working/alternating properly?	☐	☐	☒	
c. Bells and vents free of debris and in good condition?	☐	☐	☒	

	Yes	No	N/A	Comments:
6. GROUND ABSORPTION FIELDS:				
a. No evidence of effluent surfacing/reaching surface waters?	☒	☐	☐	
b. Minimal ponding in subsurface trenches?	☒	☐	☐	
c. Surface water being effectively diverted away?	☒	☐	☐	
d. Diversions/ditches/swales/tiles drains properly maintained?	☒	☐	☐	
e. Line cover/vegetation adequate/maintained as needed?	☒	☐	☐	
f. Protected from traffic, destructive uses?	☒	☐	☐	
g. Distribution devices in good condition, working properly?	☒	☐	☐	
h. Repair area properly reserved, maintained?	☒	☐	☐	
A. LOW PRESSURE PIPE DRAIN FIELDS:				
a. Turnups/cleanouts/valves intact and accessible?	☐	☐	☒	
b. No effluent standing in lower laterals?	☐	☐	☒	
c. Laterals free of excess solids, cleaned out as needed?	☐	☐	☒	
d. Pressure head is properly adjusted?	☐	☐	☒	

OVERALL CONDITION AND OPERATION OF SYSTEM:

GOOD

SUMMARY OF REPAIRS REQUIRED AT THIS TIME:

***REPAIR WITHIN DAYS.**

SYSTEM MAINTENANCE/IMPROVEMENTS REQUIRED:

*The MCHD recommends having the tanks (septic & dosing) pumped out every 3 to 5 years to remove excess solids.

*Please visit http://groundwater.charmeck.org for additional information.

DATE: 1/19/2010

SIGNED: Philo Walker RS AGENT

Division of Environmental Health

Printed Name: PHILO WALKER RS

Phone #: 704-336-5570

N.C. Department of Environment and Natural Resources
Division of Environmental Health

Inspection of Engineered Subsurface Wastewater System

Mecklenburg County	UNITER HOUSE OF PRAYER	5352B
Health Department	**Name of Establishment**	**Permit/Project No.**
5449 CHRISTENBURY RD	CHURCH	360
Location	**Type of Establishment**	**Design Flow**
UNITED HOUSE OF PRAYER	5449 CHRISTENBURY RD	
Owner/Agent	**Address**	**Phone**
NA	CHARLOTTE NC	
Operator	**Address**	**Phone**
IIIb	1/19/2010	1/19/2015
System Type	**Date of Inspection**	**Next Inspection Due**

	Yes	No	N/A	Comments:
1. ESTABLISHMENT:				
a. Type, size, and sewage flow in accordance with permit?	☒	☐	☐	
2. COLLECTION SYSTEM:				
a. No evidence of leaks into or out from sewer lines/manholes?	☒	☐	☐	
b. Free of blockages/solids buildup in lines or manholes?	☒	☐	☐	
3. TANKAGE: (Grease Traps/Lift Stations/Septic/Dosing Tanks)				
a. Tank risers accessible and surface water diverted?	☒	☐	☐	
b. Tanks and access manholes structurally sound, watertight?	☒	☐	☐	
c. Sanitary tee(s) in good working condition?.....	☐	☐	☒	3.c. Sanitary tee not inspected.
d. Tanks pumped, cleaned out as needed?.....	☒	☐	☐	
4. RAW SEWAGE LIFT STATION (if present):				
a. Required pumps present, operating, and cycling properly	☒	☐	☐	
b. High-water alarm present and operating properly?	☒	☐	☐	
c. Floats/pipe/valves/disconnects in good condition?	☒	☐	☐	
5. EFFLUENT DOSING SYSTEM:				
a. Effluent appears clear, free of excess solids?	☐	☐	☒	
A. PUMP SYSTEMS:				
a. Required pumps present, operating, and cycling properly?	☒	☐	☐	
b. High-water alarm present and operating properly?	☒	☐	☐	
c. Floats/pipe/valves/disconnects in good working condition?	☒	☐	☐	
d. Control panel enclosure/components in good condition?	☒	☐	☐	
e. Elapsed time readings: _____ _____ _____ _____				
B. SIPHON SYSTEMS:				
a. No evidence of overflow or siphon leakage?	☐	☐	☒	
b. Siphon(s) appear to be working/alternating properly?	☐	☐	☒	
c. Bells and vents free of debris and in good condition?	☐	☐	☒	

	Yes	No	N/A	Comments:
6. GROUND ABSORPTION FIELDS:				
a. No evidence of effluent surfacing/reaching surface waters?	☒	☐	☐	
b. Minimal ponding in subsurface trenches?	☒	☐	☐	
c. Surface water being effectively diverted away?	☒	☐	☐	
d. Diversions/ditches/swales/tiles drains properly maintained?	☒	☐	☐	
e. Line cover/vegetation adequate/maintained as needed?	☒	☐	☐	
f. Protected from traffic, destructive uses?	☒	☐	☐	
g. Distribution devices in good condition, working properly?	☒	☐	☐	
h. Repair area properly reserved, maintained?	☒	☐	☐	
A. LOW PRESSURE PIPE DRAIN FIELDS:				
a. Turnups/cleanouts/valves intact and accessible?	☐	☐	☒	
b. No effluent standing in lower laterals?	☐	☐	☒	
c. Laterals free of excess solids, cleaned out as needed?	☐	☐	☒	
d. Pressure head is properly adjusted?	☐	☐	☒	

OVERALL CONDITION AND OPERATION OF SYSTEM:

GOOD

SUMMARY OF REPAIRS REQUIRED AT THIS TIME:

***REPAIR WITHIN DAYS.**

SYSTEM MAINTENANCE/IMPROVEMENTS REQUIRED:

*The MCHD recommends having the tanks (septic & dosing) pumped out every 3 to 5 years to remove excess solids.

*Please visit http://groundwater.charmeck.org for additional information.

DATE: 1/19/2010

SIGNED: Philo Walker RS AGENT

Division of Environmental Health

Printed Name: PHILO WALKER RS

Phone #: 704-336-5570

FEE: 200.00 CK# 5110
DATE: 8/11/03

APPLICATION FOR IMPROVEMENT PERMIT FOR RESIDENTIAL SITE INDIVIDUAL WATER AND WASTEWATER SYSTEMS PROGRAM

I [ ] CRT

TYPE APPLICATION: __ NEW SYSTEM __ EXPANSION/ ALTERATION OF EXISTING SYSTEM __ REPAIR OF EXISTING SYSTEM

NORTH CAROLINA
DEPARTMENT OF ENVIRONMENT,
HEALTH, AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

FILE #: 53528

PROPERTY INFORMATION (FROM ENGINEERING FORM) FOR JOB LOCATION:

TAX/PARCEL NUMBER: PO 043-261-01

STREET ADDRESS: 5449 Christenbury Rd.

SUBDIVISION OR MOBILE HOME PARK NAME:

LOT NUMBER:

TOWNSHIP (CHECK ONE):

__ 0 MECKLENBURG
__ 1 CHARLOTTE
__ 2 DAVIDSON
__ 3 CORNELIUS
__ 4 PINEVILLE
__ 5 MATTHEWS
__ 6 HUNTERSVILLE
__ 7 MINT HILL

CLOSING DATE_____

TYPE OF BUILDING (CHECK ONE):

__ SINGLE MOBILE HOME(S)
__ DOUBLE WIDE (D)
__ HOUSE (H)
X MODULAR HOME (M)
__ MULTIPLE FAMILY (U)
__ OTHER (O)

HEATED SQUARE FOOTAGE: 1,100 sq.Ft.

NUMBER OF BEDROOMS: 3 | NUMBER OF OCCUPANTS:

FOUNDATION FOR RESIDENCE:

X WITHOUT BASEMENT ON SLAB
X CRAWL SPACE
__ WITH BASEMENT /PLUMBING
__ WITH BASEMENT /NO PLUMBING

IF EXPANSION/ALTERATION OF EXISTING SYSTEM, DESCRIBE THE PROPOSED BUILDING ADDITION:

WILL THERE BE A HOME BUSINESS IN THE RESIDENCE: __ YES X NO TYPE: _____

WATER SUPPLY (CHECK ONE):
__ COMMUNITY (C)
__ SHARED WELL (S)
X MUNICIPAL (M)
__ OTHER 'SPRINGS' (O)
__ PRIVATE WELL (P)

IF ANY OF THE FOLLOWING ARE LOCATED ON THE PROPERTY, PLEASE SHOW LOCATION ON PLAT:

BURIED CABLES, LANDFILLS, STUMPHOLES	__ YES __ NO	*WELL, SPRINGS OR WATERLINES*	__ YES __ NO
EXISTING WASTEWATER SYSTEMS	__ YES __ NO	DESIGNATED WETLANDS	__ YES __ NO
EASTMENTS OR RIGHT-OF-WAYS	__ YES __ NO		

PROPERTY OWNER:	LEGAL AGENT FOR PROPERTY OWNER, IF APPLICABLE:
NAME: (LAST) United House of Prayer (FIRST) (MI)	NAME: (LAST) Barringer (FIRST) Kelvin B. (MI)
ADDRESS: 1665 N. Portal Dr N.W	DAYTIME PHONE: 704 726-1036
CITY: Washington STATE: D.C. ZIP: 20012-1053	
DAYTIME PHONE: ( ) —	

WHAT DATE WAS THE PROPERTY ORIGINALLY DEEDED AND RECORDED? _____

An Improvement Permit is subject to suspension or revocation if site plans or the intended use change or if information submitted in this application is falsified or changed. The undersigned, owner, or legal agent for the owner, of the property described above as the "Job Location" has read the foregoing application, acknowledges that the contents of same are true, and authorizes agents of the Mecklenburg County Health Department to enter onto the property for the purpose of processing this request.

SIGNED: X Kelvin Barringer X DATE: 8-11-03

MECKLENBURG COUNTY HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
c/o HAL MARSHALL CTR., SUITE 211, 700 N. TRYON ST., CHARLOTTE, N.C. 28202., (704) 336-5102


PROPOSED PLOT PLAN

HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON STREET
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 5352B

TC: PO 043-261-01

Draw in and name all roads adjoining the property. Draw in and accurately dimension the lot concerned. Accurately indicate property boundaries proposed and/or existing structures and driveways, underground utilities, and wells and springs within 100 feet of the proposed building or drainfield.

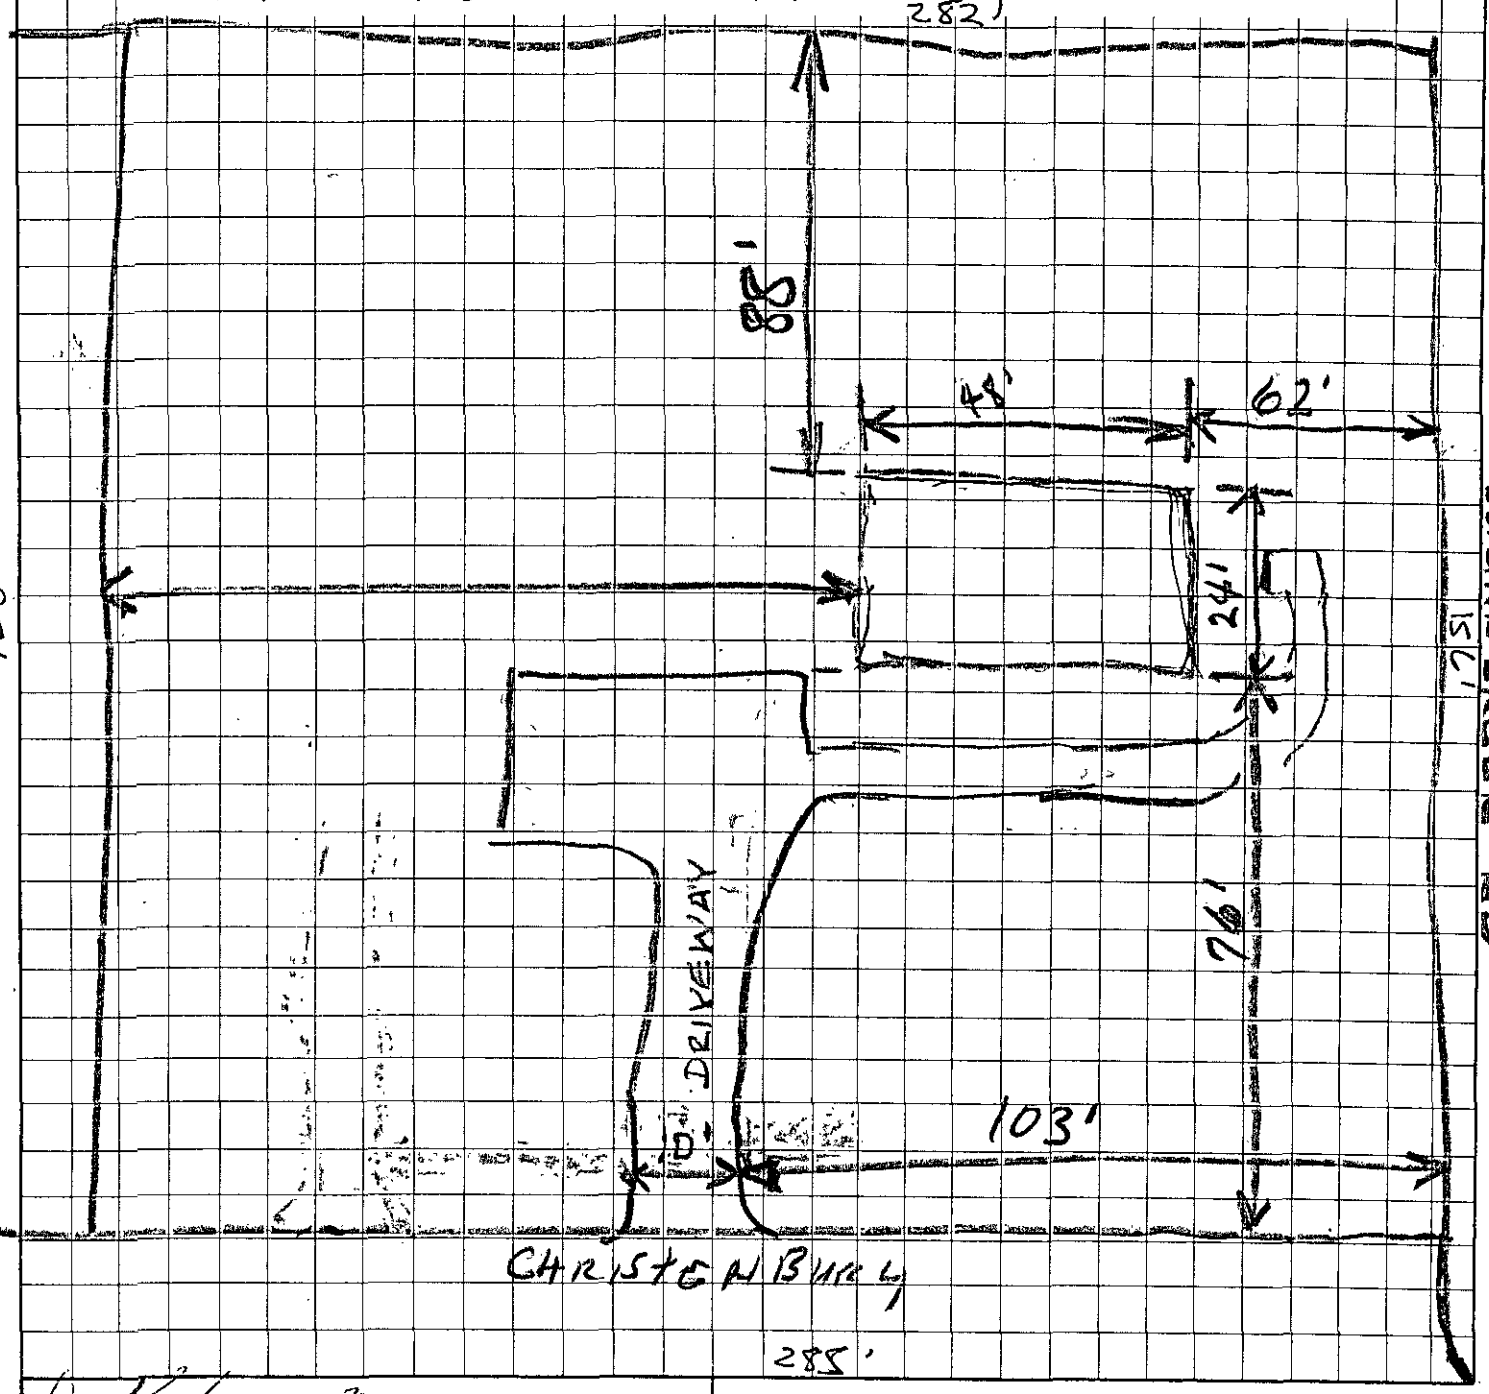

OWNER/AGENT SIGNATURE [signature]

DATE 8-11-03

APPROVAL DATE _____

White - Health Department's Copy Canary - E.H.S. Copy Pink - Owner's Copy

Department of Environment, Health, and Natural Resources
Division of Environmental Health
On-site Wastewater Section

Sheet: 1
Property ID: 043-261-01
Lot #:
File #: 5352B
Code: 1

SOIL/SITE EVALUATION
for ON-SITE WASTEWATER SYSTEM

Owner: United House of Prayer
Applicant: Kelvin B. Barringer
Address: 1665 N. Portal Drive, N. W., Washington, D. C. 2001-1053
Date Evaluated: 08/15/2003
Proposed Facility: Residence
Design Flow (.1949): 360gpd
Property Size: 1.0a. Inv.
Location of Site: 5449 Christenbury Road
Property Recorded:
Water Supply: [x] Public [ ] Individual [ ] Well [ ] Spring [ ] Other
Evaluation Method: [x] Auger Boring [ ] Pit [ ] Cut
Type of Wastewater: [x] Sewage [ ] Industrial Process [ ] Mixed

PROFILE #	1940 Landscape Position/ Slope%	Horizon Depth (IN.)	SOIL MORPHOLOGY .1941 .1941 Structure/ Texture	.1941 Consistence Mineralogy	OTHER PROFILE FACTORS .1942 Soil Wetness/ Color	.1943 Soil Depth (IN.)	.1956 Sapro Class	.1944 Restr Horiz	Profile Class & LTAR
1	LS, 6	0-6	GR/CL	FR/SEXP/SS/SP	>48" TO SOIL WETNESS	48	N/A	NONE	PS, IV
		6-48	SBK/C	FI/SEXP/S/P					.3GPD/FT^2
2	"	0-5	GR/CL	FR/SEXP/SS/SP	"	"	"	"	"
		5-40	SBK/C	FI/SEXP/S/P					
		40-48	SBK/CL	FR/SEXP/SS/SP					
3	"	0-4	GR/CL	"	"	"	"	"	"
		4-46	SBK/C	FI/SEXP/S/P					
4	"	0-5	GR/CL	FR/SEXP/SS/SP	"	"	"	"	"
		5-48	SBK/C	FI/SEXP/S/P					
5	"	0-4	GR/CL	FR/SEXP/SS/SP	"	"	"	"	"
		4-48	SBK/C	FI/SEXP/S/P					

Description	Initial System	Repair System
Available Space (.1945)	PS	PS
System Type(s)		
Site LTAR	.3GPD/FT^2	.3GPD/FT^2


Other Factors (.1946): _____
Site Classification (.1948): PROVISIONALLY SUITABLE
Evaluated By: W. R. Marlin, LSS, 8/18/2003, W. R. Marlin
Others Present: D. Walker, K. Barringer

FILE # 5352B

COMMENTS: 100% repair

LANDSCAPE POSITIONS	GROUP	TEXTURES	.1955 LTAR	CONSISTENCE MOIST	WET
R-RIDGE	I	S-SAND	1.2 - 0.8		
S-SHOULDER SLOPE		LS-LOAMY SAND		VFR-VERY FRIABLE	NS-NON-STICKY
L-LINEAR SLOPE				FR-FRIABLE	SS-SLIGHTLY STICKY
FS-FOOT SLOPE	II	SL-SANDY LOAM	0.8 – 0.6	FI-FIRM	S-STICKY
N-NOSE SLOPE		L-LOAM		VFI-VERY FIRM	VS-VERY STICKY
H-HEAD SLOPE				EFI-EXTREMELY FIRM	NP-NON-PLASTIC
CC-CONCLAVE SLOPE	III	SI-SILT-	0.6 – 0.3		SP-SLIGHTLY STICKY
CV-CONVEX SLOPE		SIL-SILT LOAM			P-PLASTIC
T-TERRACE		CL-CLAY LOAM			VP-VERY PLASTIC
FP-FLOOD PLAN		SCL-SANDY CLAY LOAM			
		SICL-SILTY CLAY LOAM			
	IV	SIC-SILTY CLAY	0.4 – 0.1		
		C-CLAY			
		SC-SANDY CLAY			

STRUCTURE	MINERALOGY
SG-SINGLE GRAIN	SLIGHTLY EXPANSIVE
M-MASSIVE	
CR-CRUMB	EXPANSIVE
GR-GRANULAR	
SBK-SUBANGULAR BLOCKY	
ABK-ANGULAR BLOCKY	
PL-PLATY	
PR-PRISMATIC	

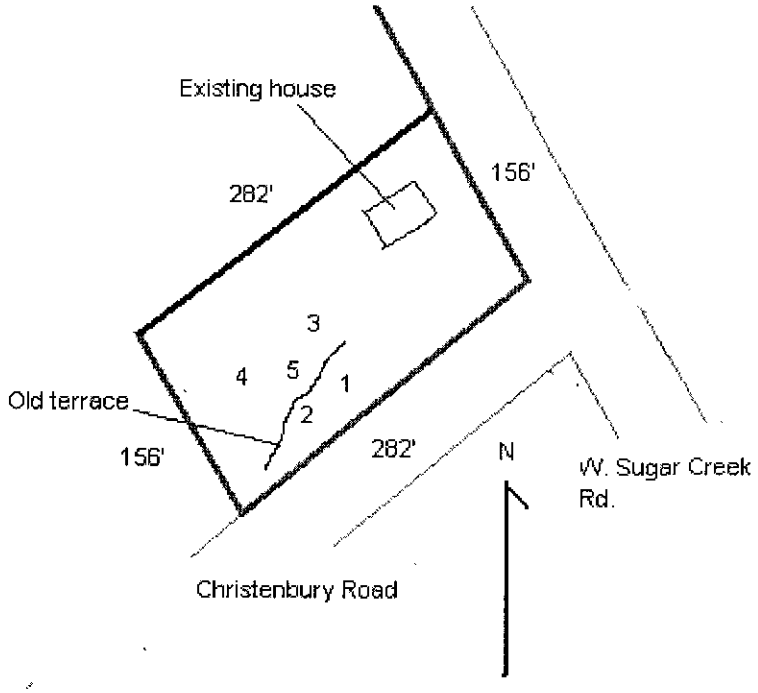

PROPOSED PLOT PLAN

HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON STREET
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 5352B

TC: 043-261-01

Draw in and name all roads adjoining the property. Draw in and accurately dimension the lot concerned. Accurately indicate property boundaries proposed and/or existing structures and driveways, underground utilities, and wells and springs within 100 feet of the proposed building or drainfield.


PERMIT FOR
5446 CHRISTENBURY ROAD

SCALE 1" = 40

(1) THIS IS A TYPE III-B, E ~~TRADITIONAL~~ SEPTIC SYSTEM THAT IS REQUIRED BY STATE LAW TO BE INSPECTED AT LEAST ONCE EVERY 5 YEARS, BY THE LOCAL HEALTH DEPT.

(2) INSTALL DRAINLINES SHALLOW (36") AND ON CONTOUR.

(3) INSTALL PRESSURE MANIFOLD AS A DISTRIBUTION DEVICE.

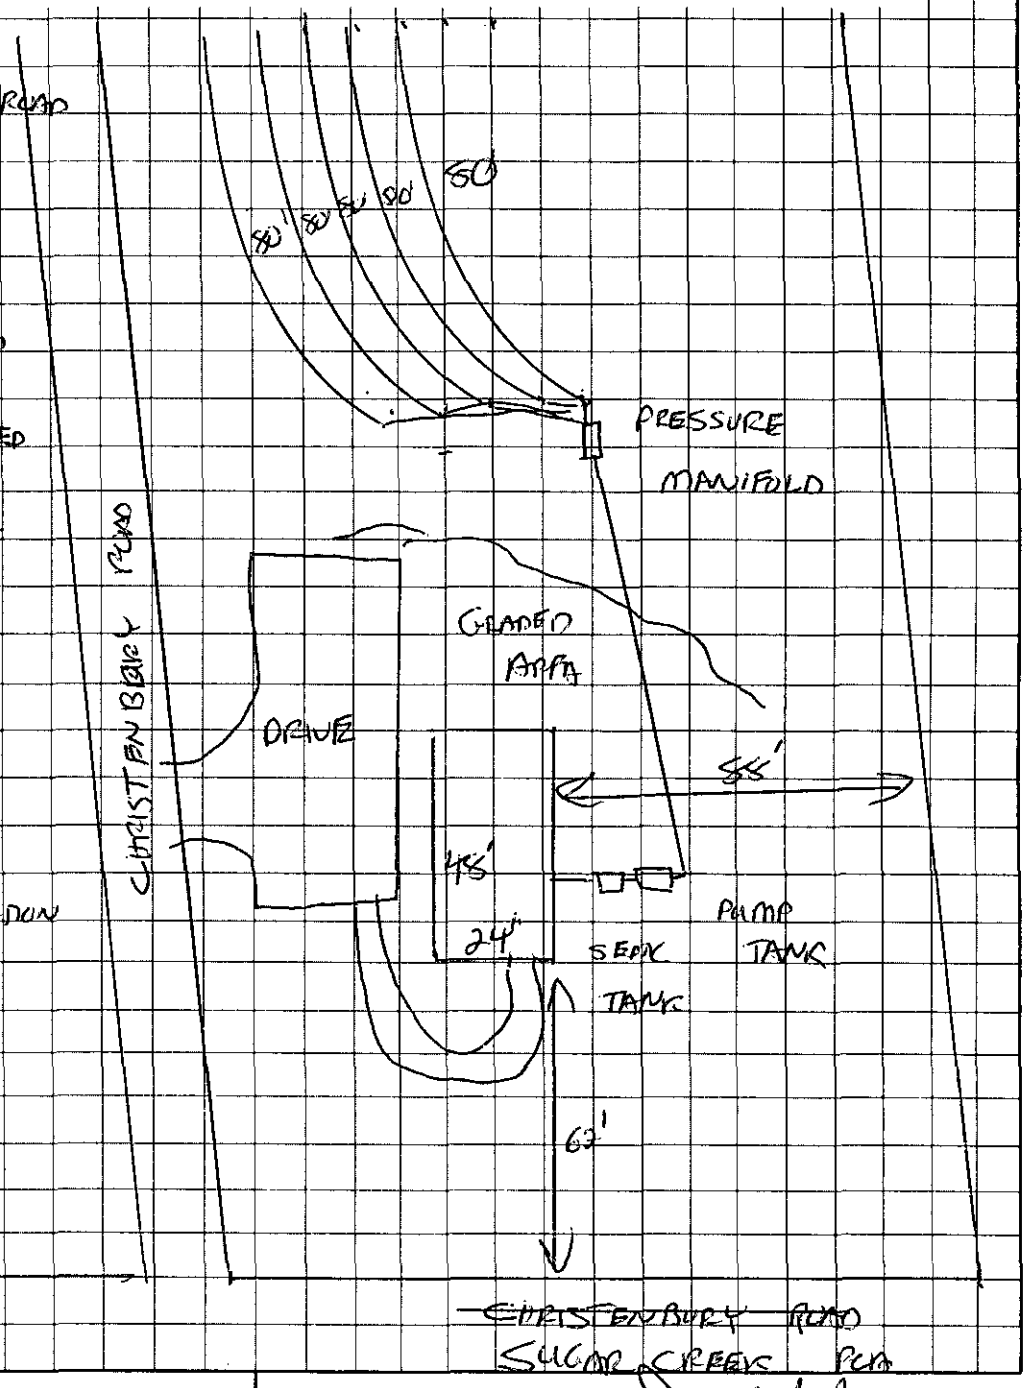

OWNER/AGENT SIGNATURE

DATE 1-20-04

APPROVAL DATE 8/19/03

White - Health Department's Copy Canary - E.H.S. Copy Pink - Owner's Copy

Permit Number: 5352B

Tax Number: 043-261-04

- The IMPROVEMENT PERMIT is subject to revocation if site plans or the intended use change. There is to be NO grading, filling or disturbance of the soil in the area of the septic tank system or repair area.
- CONSTRUCTION AUTHORIZATION must be obtained prior to receiving a Building Permit. The Construction Authorization is NOT transferable. Do not clear, grade, fill or disturb soil prior to obtaining a Construction Authorization.
- *Domestic-type wastewater only. No industrial process wastewater may be discharged into the system.*

Basement	___ Yes	X No	___ Partial Basement
Type Primary Wastewater System Type (circle one): I II (III) IV V VI	X Conventional ___ Prefabricated, permeable block panel system ___ Shallow Placed Conventional	___ Low Pressure Pipe ___ Large Diameter Pipe ___ Fill ___ Other	___ Innovative or Experimental: ___ IWWS-93-1 ___ IWWS-93-2 ___ IWWS-94-1

.3 Long-term acceptance rate	360 Max gallons/day wastewater flow	1200 Absorption Area (sq ft)	9' Trench spacing (min. on centers)
NO Serviced by private well	1500 Gallon septic tank	400 Total trench length (ft)	36" Maximum trench depth (At least 12" of provisionally suitable soil must remain between trench bottom and unsuitable soil conditions)
3 Bedrooms in residence	1000 Gallon pump tank	12" Depth of stone	

Any surface waters present: Type: Minimum separation distance:

Site modifications required:

Additional Conditions: USE PRESSURE MANIFOLD

Repair Area System Type NOT REQUIRED. Type (circle one): I II III IV V VI	___ Conventional ___ Prefabricated, permeable block panel system ___ Shallow Placed Conventional	___ Low Pressure Pipe ___ Large Diameter Pipe ___ Fill ___ Other	___ Innovative or Experimental: ___ IWWS-93-1 ___ IWWS-93-2 ___ IWWS-94-1

___ Absorption Area (Sq ft) ___ Total Trench Length (Ft)	___ Depth of Stone Trench	___ Trench spacing (min. on centers)	___ Maximum Trench Depth

For existing system, enter the year originally installed:

The undersigned, an authorized agent of the MECKLENBURG COUNTY HEALTH DEPARTMENT, certifies that the Department has approved the Request for th Job Location contained in this document. This approval is granted in accordance with the provisions of Laws and Rules For Sewage Treatment and Disposal in effe at the time of issuance of the permit and is subject to the following provisions:

- No work shall be conducted on the septic tank system until an Installation, Construction, Alteration and/or Repair Approval is granted by this Departmen
- This Improvement permit is transferable.

DEHNR Authorized Agent — Date 8/19/03

Owner/Agent Signature — Date 1-20-04

MECKLENBURG COUNTY
HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
c/o HAL MARSHALL CTR.
SUITE 211
700 N. TRYON ST.
CHARLOTTE, N.C. 28202.
(704) 336-5102

NORTH CAROLINA DEPARTMENT OF
ENVIRONMENTAL, HEALTH,
AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

Check 2620 JKA

ACS

FEE: 30.00 **AUTHORIZATION FOR WASTEWATER SYSTEM CONSTRUCTION**
DATE: 1-20-04 **VOID SIXTY (60) MONTHS FROM DATE OF ISSUANCE**

DATE: 8/19/03 PERMIT NO: 5352-B
PARCEL NO: 043-261-01

JOB LOCATION ADDRESS: 5449 CHRISTENBURY ROAD
PROPERTY OWNER: UNITED HOUSE OF PRAYER
BUILDING CONTRACTOR:
SUBDIVISION NAME:
AUTHORIZATION ISSUED BY: _____ DATE: 8/19/03
DEHNR AUTHORIZED AGENT

AUTHORIZATION CONDITIONS

1. WASTEWATER SYSTEM CONSTRUCTION AND INSTALLATION MUST MEET ALL CONDITIONS AND SPECIFICATIONS AS SET FORTH IN IMPROVEMENT PERMIT NO. 5352B, AND THE ATTACHED SITE PLAN WITH SYSTEM DETAILS. CONSTRUCTION AND INSTALLATION MUST ALSO MEET ALL REQUIREMENTS SET FORTH IN THE RULES GOVERNING SANITARY SEWAGE COLLECTION, TREATMENT, AND DISPOSAL AND ANY OTHER APPLICABLE RULES AND LAWS.

2. AN INSTALLATION, CONSTRUCTION, ALTERATION AND/OR REPAIR APPROVAL MUST BE SECURED **PRIOR** TO INSTALLATION OF THE SEPTIC TANK SYSTEM. THE INSTALLER OF THE SYSTEM SHALL BE A REGISTERED SEPTIC TANK CONTRACTOR WITH MECKLENBURG COUNTY HEALTH DEPARTMENT.

3. ANY ALTERATION IN SITE OR SOIL CONDITIONS (INCLUDING LOCATION OF STRUCTURES AND APPURTENANCES) OR MODIFICATION IN USE, DESIGN WASTEWATER FLOW, OR WASTEWATER CHARACTERISTICS AS SPECIFIED IN THE ASSOCIATED IMPROVEMENT PERMIT AND APPLICATION, MAY SUBJECT THIS AUTHORIZATION AND ASSOCIATED PERMIT(S) TO REVOCATION.

4. OTHER CONDITIONS: _____

OWNER CERTIFICATION

I CERTIFY THAT THERE HAVE BEEN NO ALTERATIONS IN SITE OR SOIL CONDITIONS OR MODIFICATIONS TO FACILITY, WASTEWATER FLOW, OR WASTEWATER CHARACTERISTICS FROM THOSE SPECIFIED IN THE ORIGINAL APPLICATION OR ASSOCIATED IMPROVEMENT PERMIT UNLESS AUTHORIZED IN WRITING BY THE MECKLENBURG COUNTY HEALTH DEPARTMENT. I ALSO UNDERSTAND THAT ANY SUCH ALTERATIONS, MODIFICATIONS, OR FALSE INFORMATION ARE GROUNDS FOR REVOCATION OF PERMITS AND AUTHORIZATION TO CONSTRUCT.

Kelvin Banning 1-20-04
SIGNATURE OF OWNER/OWNER'S REPRESENTATIVE DATE

INSTALLATION, CONSTRUCTION, ALTERATION, AND/OR REPAIR APPROVAL


HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON ST., SUITE 211
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 5352 B DATE: 8-12-03

TC: 043-261-01 ☑ L

SERIAL 19656

Permission is hereby given to ___ Install or Construct, ___ Alter or Repair the individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge as specified herein at the described location. This permit is granted based upon the information supplied in the application dated 8-11-03. All work shall be completed on or before ___, after which date this permit shall be null and void. The system shall meet all of the construction requirements of 15A NCAC 18A. 1900 which are in effect on the date of the granting of this permit. A Certificate of Completion or an Operation Permit must be obtained from the Mecklenburg County Health Department before any system can be covered up or placed into service. The issuance of this permit does not in any way guarantee that the system anticipated to be constructed will operate properly, or relieve any person now or hereafter owning, controlling or using such system from any liability resulting from the failure of the system to operate properly.

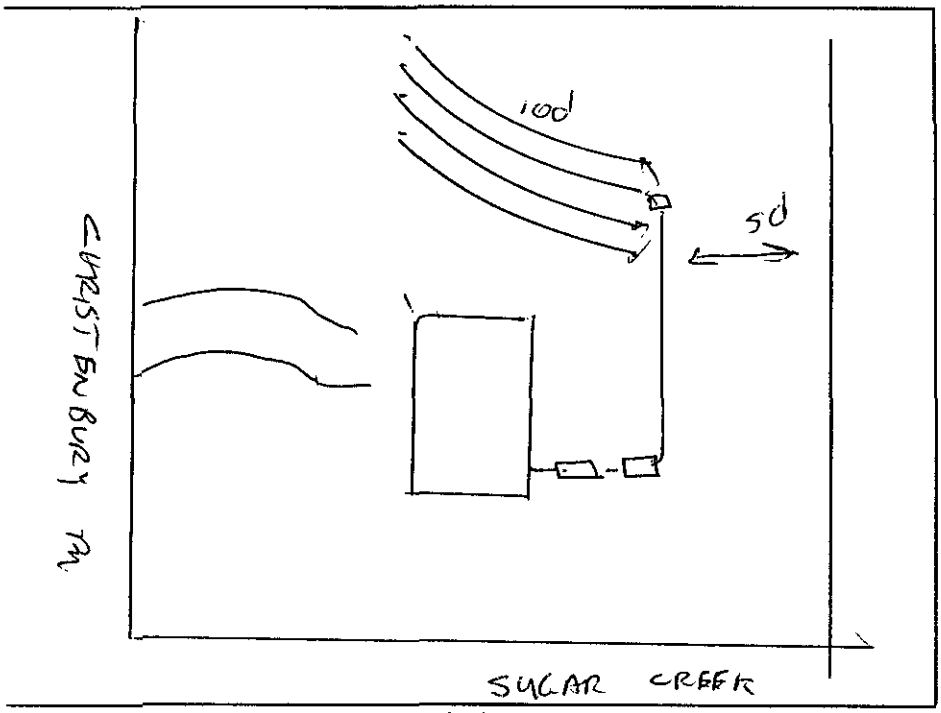

PLOT OF SYSTEM

Liquid Capacity of Septic Tank 1500 gallons

Liquid Capacity of Dosing Tank 1000 gallons

Tank Construction PCC

Trench Depth 30"

Absorption and/or Nitrification Lines:

Trench Width 3 feet

Trench Walls Scored and Porous yes

Total Line Length 400 feet

Number of Lines 4

Depth of Stone 12" inches

Distance from House 5' feet

Distance from Property Line 10' feet

Distance from Well 750' feet

NOTICE: This system shall not be installed while soils are in a wet condition.

NAME OF OWNER UNITED HOUSE OF PRAYER

LOCATION OF PROPERTY 5449 CHRISTENBURY ROAD,

Comments: (1) THIS IS A MDE #-B PUMP TO CONVENTIONAL

(2) INSTALL PRESSURE MANIFOLD,

Environmental Health Specialist

WHITE - HEALTH DEPARTMENT's COPY • CANARY - E.H.S. COPY • PINK - OWNER OR AGENT's COPY

CERTIFICATE OF COMPLETION/OPERATION PERMIT

HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON ST., SUITE 211
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 5352B DATE: 12/23/03

TC: 043-261-01 ☑ L ☑ CRT

SERIAL 19373

Name of Owner UNITED HOUSE OF PRAYER Juris.:

Address of Property 5449 CHRISTEN BUER ROAD

Inspection Data:

Tank Material 1500 gal

Total Length of Drainfield 400

Number of Lines 4 @ 100'

Cover Depth 12"

Water Supply Source MUNICIPAL


Distance to Water Source >10

Excavation Inspected 12/23/03

Tank(s) Inspected 12/23/03

Wash Line Inspected —

High Water Alarm Inspected 12/23/03

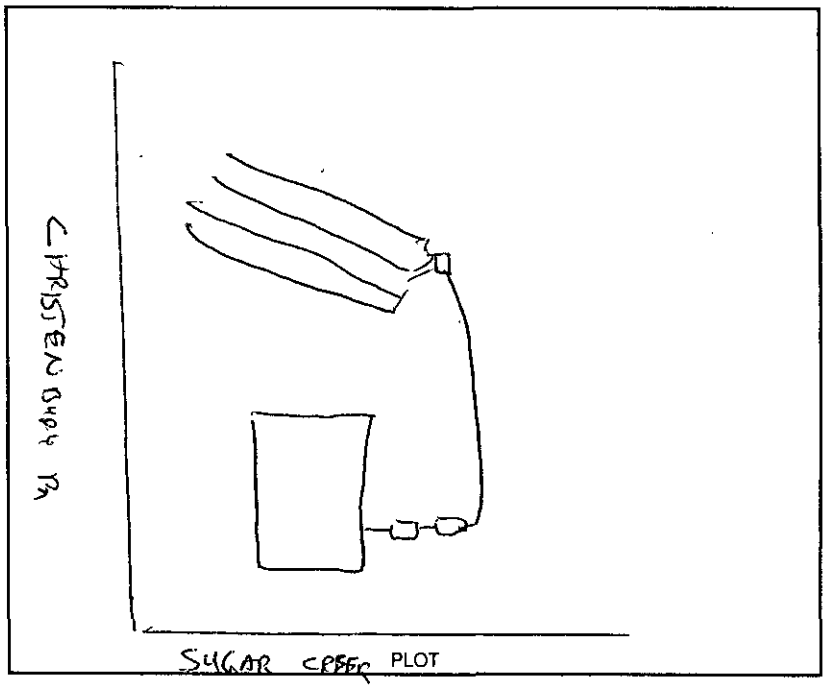

Design 1500ST 1000DT 1200SFT EQUAL LG PRESSURE MANIFOLD CTR# MORRISON

The undersigned has inspected the Septic Tank System described above, and certifies it has been

☑ installed or constructed ☐ altered or repaired

☐ in accordance with the permit issued ☑ as detailed in the plot above

and meets the provisions of 15A NCAC 18A. 1900, "Laws And Rules For Sewage Treatment and Disposal Systems" in effect on the date of issuance of the permit. This issuance of this

☐ Certificate of Completion ☑ Operation Permit

does not in any way guarantee that the system will operate properly or relieve any person now or hereafter owning, controlling, or using such system from any liability resulting from the failure of the system to operate properly. This document is issued subject to those restrictions and conditions shown on the permit(s) and the provisions of 15A NCAC 18A. 1990 in addition to those listed below under "COMMENTS." This document shall be null and void if any information contained in the application is untrue or if any additions are made to the property which would increase the requirements for said system.

Notice: Disturbance of the designated repair area may result in the suspension/revocation of this permit.

COMMENTS: TYPE II-B

Environmental Health Specialist

Mecklenburg County services are available without regard to ethnic origin, sex, or disability.



5449 CHRISTENBURY RD

04326101

1/8/2008

duponbj

Groundwater and Wastewater Services File Imaging Project
May 2007
Barcode Font = IDAutomationHC39M
