

13607 HAMILTON RD

21909113

1/4/2008

duponbj

Groundwater and Wastewater Services File Imaging Project
May 2007
Barcode Font = IDAutomationHC39M

CERTIFICATE OF COMPLETION/OPERATION PERMIT

HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON ST., SUITE 211
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 4015B DATE: 6/24/99

TC: 219-091-13 ☒ L ☐ CRT

SERIAL Nº 17766

Name of Owner Danny O Keaton Juris.:

Address of Property 13607 Hamilton Rd

Inspection Data:

Tank Material PCC

Total Length of Drainfield 200'

Number of Lines 3 @ 67'

Cover Depth 12"

Water Supply Source existing WELL

Distance to Water Source >50'

Excavation Inspected 6/24/99

Tank(s) Inspected 6/24/99

Wash Line Inspected plumb to tank

High Water Alarm Inspected NA

PLOT

Design 1999 Repair 1500ST, CON, 600SFB, 18"stone CTR# Curt Bradley

The undersigned has inspected the Septic Tank System described above, and certifies it has been

☐ installed or constructed ☒ altered or repaired

☒ in accordance with the permit issued ☐ as detailed in the plot above

and meets the provisions of I5A NCAC 18A. 1900, "Laws And Rules For Sewage Treatment and Disposal Systems" in effect on the date of issuance of the permit. This issuance of this

☐ *Certificate of Completion* ☒ Operation Permit

does not in any way guarantee that the system will operate properly or relieve any person now or hereafter owning, controlling, or using such system from any liability resulting from the failure of the system to operate properly. This document is issued subject to those restrictions and conditions shown on the permit(s) and the provisions of I5A NCAC 18A. 1990 in addition to those listed below under "COMMENTS." This document shall be null and void if any information contained in the application is untrue or if any additions are made to the property which would increase the requirements for said system.

Notice: Disturbance of the designated repair area may result in the suspension/revocation of this permit.

COMMENTS: Repair to the existing system

Smith 1980 OD 1989

Philip A. Walker RS
Environmental Health Specialist

Mecklenburg County services are available without regard to ethnic origin, sex, or disability.

INSTALLATION, CONSTRUCTION, ALTERATION, AND/OR REPAIR APPROVAL


HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON ST., SUITE 211
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 4015B DATE: 6/24/99

TC: 219-091-13 ☐ L

SERIAL Nº 17940

Permission is hereby given to _____ Install or Construct, ✓ Alter or Repair the individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge as specified herein at the described location. This permit is granted based upon the information supplied in the application dated 6/14/99. All work shall be completed on or before 7/14/99, after which date this permit shall be null and void. The system shall meet all of the construction requirements of 15A NCAC 18A. 1900 which are in effect on the date of the granting of this permit. A Certificate of Completion or an Operation Permit must be obtained from the Mecklenburg County Health Department before any system can be covered up or placed into service. The issuance of this permit does not in any way guarantee that the system anticipated to be constructed will operate properly, or relieve any person now or hereafter owning, controlling or using such system from any liability resulting from the failure of the system to operate properly.

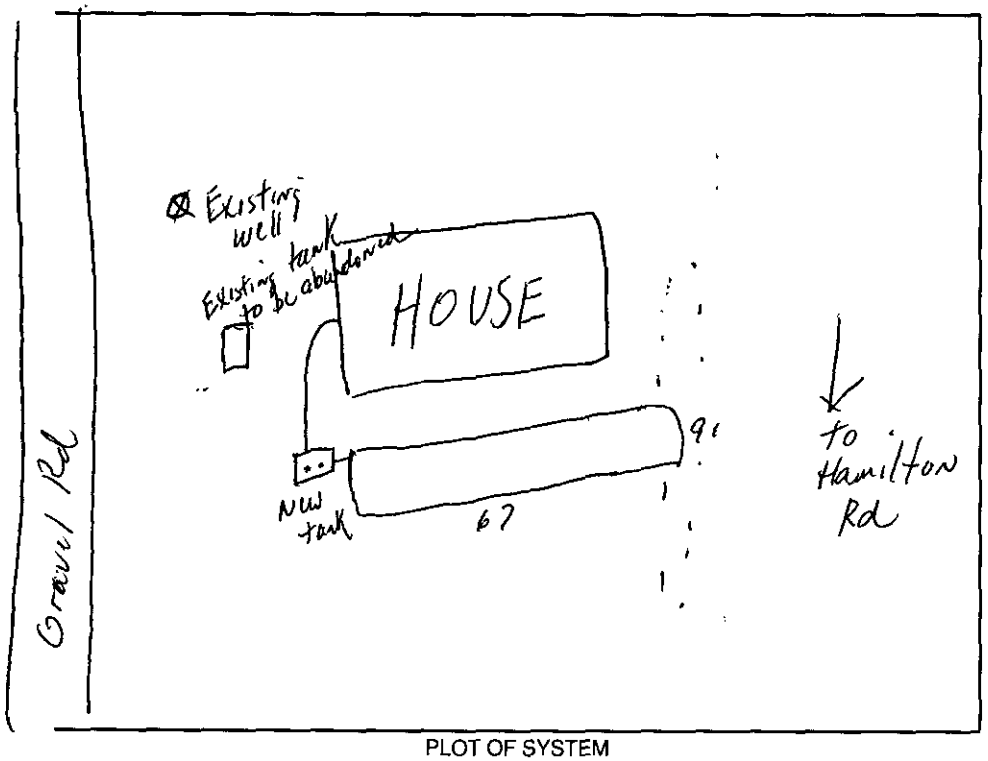

PLOT OF SYSTEM

Liquid Capacity of Septic Tank 1500 gallons

Liquid Capacity of Dosing Tank NA gallons

Tank Construction PCC

Trench Depth 36"

Absorption and/or Nitrification Lines:

Bed Trench Width 9' feet

Trench Walls Scored and Porous yes

Bed Total Line Length 200' feet

Bed Number of Lines 3 (67')

Depth of Stone 18" inches

Distance from House 5' feet

Distance from Property Line 10' feet

Distance from Well > 50' feet

NOTICE: This system shall not be installed while soils are in a wet condition.

NAME OF OWNER Danny O. Keaton

LOCATION OF PROPERTY 13607 Hamilton Rd

Comments: The existing septic system is being altered due to a 30' setback from the existing well. Install a 1500 ST, Bed System 9' wd x 67' long x 18" stone Keep the new septic system > 50' from the existing well

Phila A. Walker RS.

Environmental Health Specialist

WHITE - HEALTH DEPARTMENT's COPY • CANARY - E.H.S. COPY • PINK - OWNER OR AGENT's COPY

FEE: _____

DATE: _____

C

APPLICATION FOR IMPROVEMENT PERMIT FOR RESIDENTIAL SITE INDIVIDUAL WATER AND WASTEWATER SYSTEMS PROGRAM

REPAIR

1] CRT

TYPE APPLICATION: __ NEW SYSTEM __ EXPANSION/ ALTERATION OF EXISTING SYSTEM X REPAIR OF EXISTING SYSTEM

NORTH CAROLINA
DEPARTMENT OF ENVIRONMENT,
HEALTH, AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

FILE #: 4015B

PROPERTY INFORMATION (FROM ENGINEERING FORM) FOR JOB LOCATION:

TAX/PARCEL NUMBER: 219-091-13

STREET ADDRESS: 13607 Hamilton Rd

SUBDIVISION OR MOBILE HOME PARK NAME: 1980

LOT NUMBER: A

TYPE OF BUILDING (CHECK ONE):

__ SINGLE MOBILE HOME(S)
__ DOUBLE WIDE (D)
__ HOUSE (H)
__ MODULAR HOME (M)
__ MULTIPLE FAMILY (U)
__ OTHER (O)

TOWNSHIP (CHECK ONE):

__ 0 MECKLENBURG
__ 1 CHARLOTTE
__ 2 DAVIDSON
__ 3 CORNELIUS
__ 4 PINEVILLE
__ 5 MATTHEWS
__ 6 HUNTERSVILLE
__ 7 MINT HILL

HEATED SQUARE FOOTAGE:

NUMBER OF BEDROOMS: 2

NUMBER OF OCCUPANTS: 2

CLOSING DATE _____

FOUNDATION FOR RESIDENCE:

__ WITHOUT BASEMENT
__ ON SLAB
__ CRAWL SPACE
__ WITH BASEMENT /PLUMBING
__ WITH BASEMENT /NO PLUMBING

IF EXPANSION/ALTERATION OF EXISTING SYSTEM, DESCRIBE THE PROPOSED BUILDING ADDITION:

WILL THERE BE A HOME BUSINESS IN THE RESIDENCE: __ YES __ NO TYPE: _____

WATER SUPPLY (CHECK ONE):

__ COMMUNITY (C)
__ MUNICIPAL (M)
✓ PRIVATE WELL (P)
__ SHARED WELL (S)
__ OTHER 'SPRINGS' (O)

IF ANY OF THE FOLLOWING ARE LOCATED ON THE PROPERTY, PLEASE SHOW LOCATION ON PLAT:

BURIED CABLES, LANDFILLS, STUMPHOLES	__ YES __ NO	WELL, SPRINGS OR WATERLINES	__ YES __ NO
EXISTING WASTEWATER SYSTEMS	__ YES __ NO	DESIGNATED WETLANDS	__ YES __ NO
EASTMENTS OR RIGHT-OF-WAYS	__ YES __ NO		

PROPERTY OWNER:	LEGAL AGENT FOR PROPERTY OWNER, IF APPLICABLE:
NAME: KEATON DANNY O'SHEA (LAST) (FIRST) (MI)	NAME: (LAST) (FIRST) (MI)
ADDRESS: 10117 JOHN PRICE Rd	DAYTIME PHONE: ( ) -
CITY CHARLOTTE STATE: NC. ZIP: 28273	
DAYTIME PHONE: (704) 578 - 6462	

WHAT DATE WAS THE PROPERTY ORIGINALLY DEEDED AND RECORDED? _____

An Improvement Permit is subject to suspension or revocation if site plans or the intended use change or if information submitted in this application is falsified or changed. The undersigned, owner, or legal agent for the owner, of the property described above as the "Job Location" has read the foregoing application, acknowledges that the contents of same are true, and authorizes agents of the Mecklenburg County Health Department to enter onto the property for the purpose of processing this request.

SIGNED: Danny Keaton DATE: 6-24-99

MECKLENBURG COUNTY HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
c/o HAL MARSHALL CTR., SUITE 211, 700 N. TRYON ST., CHARLOTTE, N.C. 28202., (704) 336-5102

CONDITIONS OF IMPROVEMENT PERMIT

Permit Number: _____ Tax Number: 13607

- The IMPROVEMENT PERMIT is subject to revocation if site plans or the intended use change. There is to be NO grading, filling or disturbance of the soil in the area of the septic tank system or repair area.
- CONSTRUCTION AUTHORIZATION must be obtained prior to receiving a Building Permit. The Construction Authorization is NOT transferable. Do not clear, grade, fill or disturb soil prior to obtaining a Construction Authorization.
- Domestic-type wastewater only. No industrial process wastewater may be discharged into the system.

Basement	___ Yes	✓ No	___ Partial Basement	
Type Primary Wastewater System Type (circle one): I II III IV V VI	___ Conventional ___ Prefabricated, permeable block panel system ___ Shallow Placed Conventional	___ Low Pressure Pipe ___ Large Diameter Pipe ___ Fill ___ Other	___ Innovative or Experimental: ___ IWWS-93-1 ___ IWWS-93-2 ___ IWWS-94-1	
___ Long-term acceptance rate	___ Max gallons/day wastewater flow	___ Absorption Area (sq ft)	___ Trench spacing (min. on centers)	
___ Serviced by private well	___ Gallon septic tank	___ Total trench length (ft)	___ Maximum trench depth (At least 12" of provisionally suitable soil must remain between trench bottom and unsuitable soil conditions)	
___ Bedrooms in residence	___ Gallon pump tank	___ Depth of stone		
Any surface waters present:	Type:	Minimum separation distance:		
Site modifications required:				
Additional Conditions: Repair to the existing system. The septic system is being altered due to a 30' seperation from the existing well. Install 1500ST, Bed System repair 9'wd x 67'lon x 18"Stone Keep the septic system > 50' from the existing well				
Repair Area System Type Type (circle one): I (II) III IV V VI	✓ Conventional ___ Prefabricated, permeable block panel system ___ Shallow Placed Conventional	___ Low Pressure Pipe ___ Large Diameter Pipe ___ Fill ___ Other	___ Innovative or Experimental: ___ IWWS-93-1 ___ IWWS-93-2 ___ IWWS-94-1	
600' Absorption Area (Sq ft) 200' Total Trench Length (Ft)	18" Depth of Stone Trench	N/A Trench spacing (min. on centers)	36" Maximum Trench Depth	
For existing system, enter the year originally installed:				

The undersigned, an authorized agent of the MECKLENBURG COUNTY HEALTH DEPARTMENT, certifies that the Department has approved the Request for th Job Location contained in this document. This approval is granted in accordance with the provisions of Laws and Rules For Sewage, Treatment and Disposal in effe at the time of issuance of the permit and is subject to the following provisions:

- No work shall be conducted on the septic tank system until an Installation, Construction, Alteration and/or Repair Approval is granted by this Departmen
- This Improvement permit is transferable.

Phila A. Walker RS 6/24/99
DEHNR Authorized Agent Date

_____ Owner/Agent Signature Date

MECKLENBURG COUNTY
HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
c/o HAL MARSHALL CTR.
SUITE 211
700 N. TRYON ST.
CHARLOTTE, N.C. 28202.
(704) 336-5102

NORTH CAROLINA DEPARTMENT OF
ENVIRONMENTAL, HEALTH,
AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

FEE: _____ **AUTHORIZATION FOR WASTEWATER SYSTEM CONSTRUCTION**
DATE: _____ **VOID SIXTY (60) MONTHS FROM DATE OF ISSUANCE**

DATE: 6/24/99 PERMIT NO: 4015B

PARCEL NO: 219 091 13

JOB LOCATION ADDRESS: 13607 Hamilton Rd

PROPERTY OWNER: Danny O Keaton

BUILDING CONTRACTOR: —

SUBDIVISION NAME: —

AUTHORIZATION ISSUED BY: Philo L Walker RS DATE: 6/24/99

DEHNR AUTHORIZED AGENT

AUTHORIZATION CONDITIONS

1. WASTEWATER SYSTEM CONSTRUCTION AND INSTALLATION MUST MEET ALL CONDITIONS AND SPECIFICATIONS AS SET FORTH IN IMPROVEMENT PERMIT NO. 4015B, AND THE ATTACHED SITE PLAN WITH SYSTEM DETAILS. CONSTRUCTION AND INSTALLATION MUST ALSO MEET ALL REQUIREMENTS SET FORTH IN THE RULES GOVERNING SANITARY SEWAGE COLLECTION, TREATMENT, AND DISPOSAL AND ANY OTHER APPLICABLE RULES AND LAWS.

2. AN INSTALLATION, CONSTRUCTION, ALTERATION AND/OR REPAIR APPROVAL MUST BE SECURED PRIOR TO INSTALLATION OF THE SEPTIC TANK SYSTEM. THE INSTALLER OF THE SYSTEM SHALL BE A REGISTERED SEPTIC TANK CONTRACTOR WITH MECKLENBURG COUNTY HEALTH DEPARTMENT.

3. ANY ALTERATION IN SITE OR SOIL CONDITIONS (INCLUDING LOCATION OF STRUCTURES AND APPURTENANCES) OR MODIFICATION IN USE, DESIGN WASTEWATER FLOW, OR WASTEWATER CHARACTERISTICS AS SPECIFIED IN THE ASSOCIATED IMPROVEMENT PERMIT AND APPLICATION, MAY SUBJECT THIS AUTHORIZATION AND ASSOCIATED PERMIT(S) TO REVOCATION.

4. OTHER CONDITIONS: Repair to the existing system

OWNER CERTIFICATION

I CERTIFY THAT THERE HAVE BEEN NO ALTERATIONS IN SITE OR SOIL CONDITIONS OR MODIFICATIONS TO FACILITY, WASTEWATER FLOW, OR WASTEWATER CHARACTERISTICS FROM THOSE SPECIFIED IN THE ORIGINAL APPLICATION OR ASSOCIATED IMPROVEMENT PERMIT UNLESS AUTHORIZED IN WRITING BY THE MECKLENBURG COUNTY HEALTH DEPARTMENT. I ALSO UNDERSTAND THAT ANY SUCH ALTERATIONS, MODIFICATIONS, OR FALSE INFORMATION ARE GROUNDS FOR REVOCATION OF PERMITS AND AUTHORIZATION TO CONSTRUCT.

SIGNATURE OF OWNER/OWNER'S REPRESENTATIVE DATE
