Date Received 4-19-93 APT No. 6057

T. C. No.

MECKLENBURG COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

APPLICATION FOR PERCOLATION TEST

NAME OF OWNER LYERLY (LAST) NED (FIRST) T. (MIDDLE)

ADDRESS OF OWNER 166 Laburn Avenue, Charlotte, N. C. ZIP 28214

PHONE NO. Home 392-1585 Office


LOCATION OF PROPERTY Pine Forest Road (STREET OR COUNTY ROAD)

SUBDIVISION Pine Island Country Club LOT NO. 33 BLOCK NO. 4

MAP BOOK NO. 14 PAGE NO. 265

DEED REFERENCE: DEED BOOK 3213 PAGE NO. 275

Application is hereby made to the Mecklenburg County Health Department for the conduct of a percolation test and an on site inspection of the lot hereinabove described for the purpose of determining if the lot is suitable for the installation of an individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge

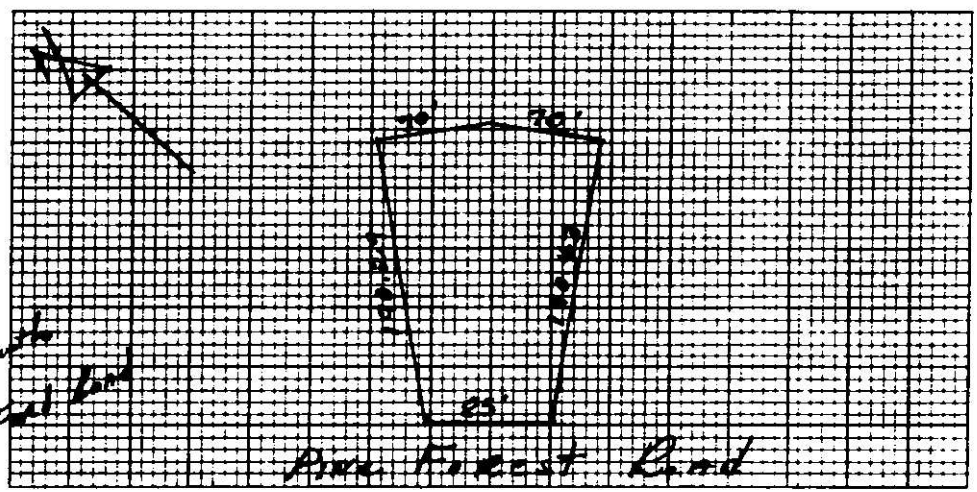

860' South of South Post Road

ACCURATELY DIAGRAM & DIMENSION LOT

OWNER NED T. LYERLY

FORM NO. E-1-7-1-78

HEALTH DEPARTMENT'S COPY

MECKLENBURG COUNTY
Department of Public Health

1200 Blythe Boulevard
Charlotte, North Carolina 28203
Telephone 374-2113

Date Issued
1. November 8, 1973
2. Nov. 23, 1973
3. _____

SITE DISAPPROVAL REPORT
INDIVIDUAL SEPTIC TANK SYSTEM WITH SUBSURFACE, SOIL ABSORPTION, EFFLUENT DISCHARGE

SDR No. 6057
T.C. No. 031-103-53

NAME OF OWNER Lyerly, Ned T.

ADDRESS OF OWNER 166 Laburn Avenue ZIP 28214

LOCATION OF LOT Pine Forest Road, Lot 33-A

The lot described above has been disapproved for the installation of an individual septic tank system with subsurface, soil absorption, effluent discharge due to the following:

FAILURE TO PASS PERCOLATION TEST (60 minutes per inch or less)

	Test No.	Date of Test	Percolation Rate
X	1.	11-7-73	200 min/in
____	2.	_____	_____ min/in
____	3.	_____	_____ min/in

X ON SITE INSPECTION REVEALED LOT TO BE UNSUITABLE FOR THE FOLLOWING REASON(S) 11-21-73 - Soils were found to be of the Enon series. These soils have plastic and stiff clay subsoils which contain swelling clay minerals. These factors result in inadequately slow percolation rate and permeability.

W. Everette Lyons, Jr.
Soil Scientist

Environmentalist

(Stencil No.)
MED 398
8/70

FORM NO.
E-19-8-14-70

MECKLENBURG COUNTY HEALTH DEPARTMENT
INTER-OFFICE COMMUNICATION

DATE: November 21, 1973

TO: Luther Bridgeman
Environmentalist

FROM: W. Everette Lynn, Jr. WEL
Soil Scientist

SUBJECT: APT #6057 (N. Lyerly)
Lot No. 33, Block 4, Pine Forest Road
11-21-73

Soils were found to be of the Enon series. These soils have plastic and sticky clay subsoils which contain swelling clay minerals. These factors result in inadequately slow percolation rate and permeability.

Based on this investigation, it is recommended that the lot be disapproved for installation of a septic tank system.

WEL:jdg
