

4801 PROSPERITY CHURCH RD

02755198

5/19/08

marliwr

Groundwater and Wastewater Services File Imaging Project
May 2007
Barcode Font = IDAutomationHC39M

Mecklenburg County
Health Department

April 2, 1997

Martin P. Haugh
4801 Prosperity Church Road
Charlotte, NC 28269

Re: 4801 Prosperity Church Road
File: 712
Parcel: 027-551-98

Dear Mr. Haugh:

At your request an inspection was made at the above referenced property to facilitate the issuance of an Operation Permit for the Sewage Treatment and Disposal system. During the inspection it was found that the following items did not meet the regulations set forth in the "Laws and Rules for Sewage Treatment and Disposal Systems, 15A NCAC 18A .1900;.1952 Septic Tank, Dosing, Dosing Tank and Lift Station Design." Our comments follow:

1) (6) Pump and control circuits shall be provided with manual circuit disconnects within a watertight, corrosion-resistant, outside enclosure (NEMA 4X or equivalent) adjacent to the pump tank, securely mounted at least 12 inches above the finished grade. The pump(s) shall be manually operable without requiring the use of special tools or entrance into the tank for testing purposes. Conductors shall be conveyed to the disconnect enclosure through water proof, gasproof, and corrosion-resistant conduits, with no splices or junction boxes provided inside the tank. Wire grips, duct seal, or other suitable material shall be used to seal around wire and wire conduit openings inside the pump tank and disconnect enclosure.

2) (9) The pump tank shall have a properly functioning high-water alarm. The alarm circuit shall be supplied ahead of any pump overload and short circuit protective devices. The alarm shall be audible and visible by system users and weatherproof if installed outdoors in an enclosure (NEMA 4X or equivalent).

The above mentioned items must be installed and inspected prior to the Operation Permit being issued. The Operation Permit is required for the Certificate of Occupancy and the permanent electric hook-ups. Please schedule the inspections at least five (5) working days in advance to ensure no delays in the Operation Permit issuance.

Please call me at 336-5570 to discuss any question you may have concerning this matter.

Sincerely,

Philo S. Walker, R.S.
Individual Water and Wastewater Systems

PW:gc

FEE: 100.00 CHK #3502
DATE: 3/10/97

APPLICATION FOR IMPROVEMENT PERMIT FOR RESIDENTIAL SITE INDIVIDUAL WATER AND WASTEWATER SYSTEMS PROGRAM

[ ] CRT

TYPE APPLICATION: ___ NEW SYSTEM X EXPANSION/ ALTERATION OF EXISTING SYSTEM ___ REPAIR OF EXISTING SYSTEM

NORTH CAROLINA
DEPARTMENT OF ENVIRONMENT,
HEALTH, AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

FILE #: 712

PROPERTY INFORMATION (FROM ENGINEERING FORM) FOR JOB LOCATION:

TAX/PARCEL NUMBER: 027-551-98

STREET ADDRESS: 4801 PROSPERITY CHURCH RD

SUBDIVISION OR MOBILE HOME PARK NAME: —

LOT NUMBER: —

TYPE OF BUILDING (CHECK ONE):

___ SINGLE MOBILE HOME(S) ___ MODULAR HOME (M)
___ DOUBLE WIDE (D) ___ MULTIPLE FAMILY (U)
X HOUSE (H) ___ OTHER (O)

TOWNSHIP (CHECK ONE):

X 0 MECKLENBURG ___ 4 PINEVILLE
___ 1 CHARLOTTE ___ 5 MATTHEWS
___ 2 DAVIDSON ___ 6 HUNTERSVILLE
___ 3 CORNELIUS ___ 7 MINT HILL

CLOSING DATE_____

HEATED SQUARE FOOTAGE: ~2800 SF

NUMBER OF BEDROOMS: 4 NUMBER OF OCCUPANTS: 4

FOUNDATION FOR RESIDENCE:

___ WITHOUT BASEMENT ON SLAB
X CRAWL SPACE
___ WITH BASEMENT /PLUMBING
___ WITH BASEMENT /NO PLUMBING

IF EXPANSION/ALTERATION OF EXISTING SYSTEM, DESCRIBE THE PROPOSED BUILDING ADDITION: NEED TO MOVE THE EXISTING SEPTIC FIELD BECAUSE IT WOULD BE EXPOSED WHEN OUR FRONT YARD SPACE IS CHANGED INTO A PRESCHOOL AREA.

WILL THERE BE A HOME BUSINESS IN THE RESIDENCE: ___ YES X NO TYPE: _____

WATER SUPPLY (CHECK ONE): ___ COMMUNITY (C) X MUNICIPAL (M) ___ PRIVATE WELL (P)
___ SHARED WELL (S) ___ OTHER 'SPRINGS' (O)

IF ANY OF THE FOLLOWING ARE LOCATED ON THE PROPERTY, PLEASE SHOW LOCATION ON PLAT:

BURIED CABLES, LANDFILLS, STUMPHOLES ___ YES ___ NO
EXISTING WASTEWATER SYSTEMS ___ YES ___ NO
EASTMENTS OR RIGHT-OF-WAYS ___ YES ___ NO
WELL, SPRINGS OR WATERLINES ___ YES ___ NO
DESIGNATED WETLANDS ___ YES ___ NO

PROPERTY OWNER:

NAME: (LAST) HAUGH (FIRST) MARTIN (MI) P
ADDRESS: 4801 PROSPERITY CHURCH RD.
CITY: CHARLOTTE STATE: NC ZIP: 28269
DAYTIME PHONE: (704) 549 - 4253

LEGAL AGENT FOR PROPERTY OWNER, IF APPLICABLE:

NAME: (LAST) (FIRST) (MI)
DAYTIME PHONE: ( ) —

WHAT DATE WAS THE PROPERTY ORIGINALLY DEEDED AND RECORDED? _____

An Improvement Permit is subject to suspension or revocation if site plans or the intended use change or if information submitted in this application is falsified or changed. The undersigned, owner, or legal agent for the owner, of the property described above as the "Job Location" has read the foregoing application, acknowledges that the contents of same are true, and authorizes agents of the Mecklenburg County Health Department to enter onto the property for the purpose of processing this request.

SIGNED: Martin P. Haugh DATE: 3/10/97

MECKLENBURG COUNTY HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
c/o HAL MARSHALL CTR., SUITE 211, 700 N. TRYON ST., CHARLOTTE, N.C. 28202., (704) 336-5102

INSTALLATION, CONSTRUCTION, ALTERATION, AND/OR REPAIR APPROVAL


HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON ST., SUITE 211
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 7/2 DATE: 3/27/97

TC: 027 551 98 ☐ L

SERIAL Nº 16849

Permission is hereby given to _____ Install or Construct, _____ (Alter) or Repair the individual septic tank wastewater treatment system with subsurface, soil absorption, effluent discharge as specified herein at the described location. This permit is granted based upon the information supplied in the application dated 3/10/97. All work shall be completed on or before 4/27/97, after which date this permit shall be null and void. The system shall meet all of the construction requirements of 15A NCAC 18A. 1900 which are in effect on the date of the granting of this permit. A Certificate of Completion or an Operation Permit must be obtained from the Mecklenburg County Health Department before any system can be covered up or placed into service. The issuance of this permit does not in any way guarantee that the system anticipated to be constructed will operate properly, or relieve any person now or hereafter owning, controlling or using such system from any liability resulting from the failure of the system to operate properly.

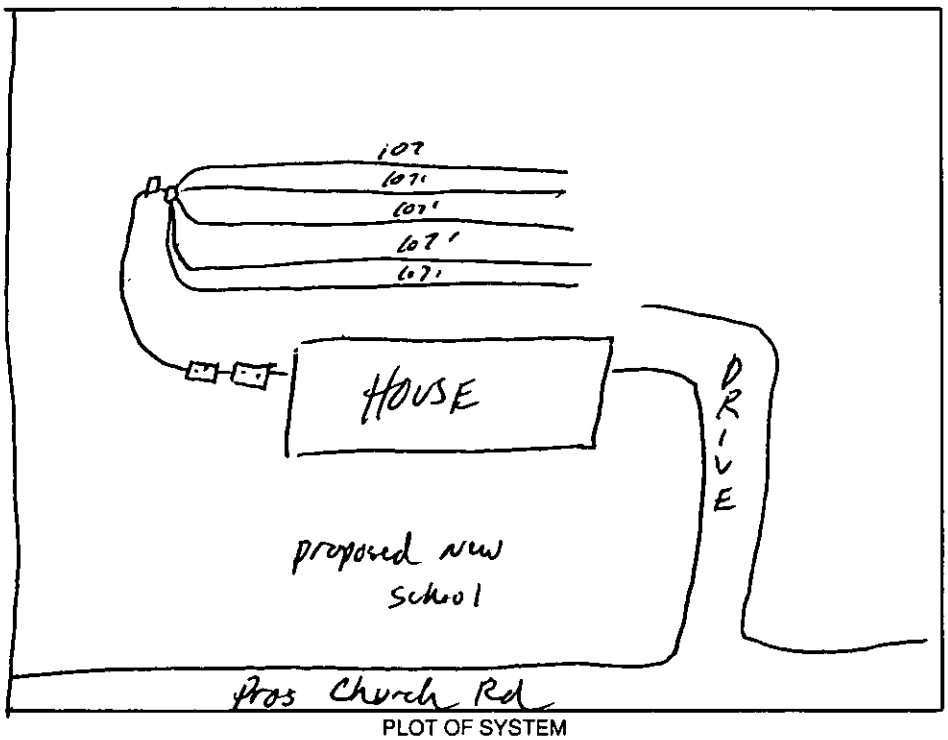

PLOT OF SYSTEM

Liquid Capacity of Septic Tank NA gallons

Liquid Capacity of Dosing Tank 1000 gallons

Tank Construction PCC

Trench Depth 24"

Absorption and/or Nitrification Lines:

Trench Width 36" feet

Trench Walls Scored and Porous Yes

Total Line Length 535' feet

Number of Lines 5 (107')

Depth of Stone 12" inches

Distance from House 5' feet

Distance from Property Line 10' feet

Distance from Well 100' feet
50' min

NOTICE: This system shall not be installed while soils are in a wet condition.

NAME OF OWNER Martin P. Haugh

LOCATION OF PROPERTY 4801 Prosperity Church Rd

Comments: Alteration, ~~1000 GT~~, PI, 5 lines x 107' long x 3' wd x 12" stone
Keep septic septic system >50' from existing well

Philo S. Walker R.S.
Environmental Health Specialist

WHITE - HEALTH DEPARTMENT's COPY • CANARY - E.H.S. COPY • PINK - OWNER OR AGENT's COPY

Mecklenburg County
Health Department

MEMORANDUM

TO: Susan Uzzell
Accountant II

FROM: Sylvia D. Daniel, R.S.
Program Chief

Date: March 26, 1997

Ref: 4801 Prosperity Church Rd/File #712

SUBJECT: Refund

(Mr./Mrs./Co.) Mr. Martin P. Haugh originally paid $200.00 for additional fee for alteration of septic system on March 24, 1997.

A refund should be issued for $100.00 because the additional fee due was $100.00.

Please make check payable to: Martin P. Haugh
4801 Prosperity Church Road
Charlotte, NC 28269

MARTIN P. HAUGH
DEBORAH W. HAUGH
NCDL 5669944 PHONE 704-593-1905
4801 PROSPERITY CHURCH RD.
CHARLOTTE, NC 28269

66-73
531
012064688

3510

DATE 3/20/97

PAY TO THE ORDER OF Mecklenburg County Health Dept $ 200.00

Two hundred + 00/100 DOLLARS

FIRST CHARTER NATIONAL BANK
HARRISBURG, NORTH CAROLINA 28075

Charter Banking

MEMO #712; 4801 Prosperity Church

Martin P. Haugh MP

⑆053100737⑆ 012064688⑈ 3510

SAFETY PAPER

Prepaid
4/02

4/02 Prepaid
Dec

3/1/97

3/20/97

Dear Sirs:

As noted on my check, this is for the next 2 steps in our process to have a septic installed at 4801 Prosperity Church Road, Charlotte, N.C., The person who called told me to refer to # 712.

Sincerely,
Martin P. Haugh
549-4253 – Work
593-1905 – Home

chk # 3510 - Downpaid by #100 - Paid in full

FEE: 200.00 **AUTHORIZATION FOR WASTEWATER SYSTEM CONSTRUCTION**
DATE: 3/4/97 **& VOID SIXTY (60) MONTHS FROM DATE OF ISSUANCE**

DATE: 3/18/97 PERMIT NO: 712

PARCEL NO: 027 55198

JOB LOCATION ADDRESS: 4801 Prosperity Church Rd

PROPERTY OWNER: Martin P. Haugh

BUILDING CONTRACTOR: Robert Levy

SUBDIVISION NAME: NA

AUTHORIZATION ISSUED BY: Philo S. Walker R.S. DATE: 3/18/97

DEHNR AUTHORIZED AGENT

AUTHORIZATION CONDITIONS

1. WASTEWATER SYSTEM CONSTRUCTION AND INSTALLATION MUST MEET ALL CONDITIONS AND SPECIFICATIONS AS SET FORTH IN IMPROVEMENT PERMIT NO. 712, AND THE ATTACHED SITE PLAN WITH SYSTEM DETAILS. CONSTRUCTION AND INSTALLATION MUST ALSO MEET ALL REQUIREMENTS SET FORTH IN THE RULES GOVERNING SANITARY SEWAGE COLLECTION, TREATMENT, AND DISPOSAL AND ANY OTHER APPLICABLE RULES AND LAWS.

2. AN INSTALLATION, CONSTRUCTION, ALTERATION AND/OR REPAIR APPROVAL MUST BE SECURED **PRIOR** TO INSTALLATION OF THE SEPTIC TANK SYSTEM. THE INSTALLER OF THE SYSTEM SHALL BE A REGISTERED SEPTIC TANK CONTRACTOR WITH MECKLENBURG COUNTY HEALTH DEPARTMENT.

3. ANY ALTERATION IN SITE OR SOIL CONDITIONS (INCLUDING LOCATION OF STRUCTURES AND APPURTENANCES) OR MODIFICATION IN USE, DESIGN WASTEWATER FLOW, OR WASTEWATER CHARACTERISTICS AS SPECIFIED IN THE ASSOCIATED IMPROVEMENT PERMIT AND APPLICATION, MAY SUBJECT THIS AUTHORIZATION AND ASSOCIATED PERMIT(S) TO REVOCATION.

4. OTHER CONDITIONS: Septic system alteration

OWNER CERTIFICATION

I CERTIFY THAT THERE HAVE BEEN NO ALTERATIONS IN SITE OR SOIL CONDITIONS OR MODIFICATIONS TO FACILITY, WASTEWATER FLOW, OR WASTEWATER CHARACTERISTICS FROM THOSE SPECIFIED IN THE ORIGINAL APPLICATION OR ASSOCIATED IMPROVEMENT PERMIT UNLESS AUTHORIZED IN WRITING BY THE MECKLENBURG COUNTY HEALTH DEPARTMENT. I ALSO UNDERSTAND THAT ANY SUCH ALTERATIONS, MODIFICATIONS, OR FALSE INFORMATION ARE GROUNDS FOR REVOCATION OF PERMITS AND AUTHORIZATION TO CONSTRUCT.

x Robert Levy for John S. Clark Company 3/18/97

SIGNATURE OF OWNER/OWNER'S REPRESENTATIVE DATE

Permit Number: 712

Tax Number: 027 551 98

- The IMPROVEMENT PERMIT is subject to revocation if site plans or the intended use change. There is to be NO grading, filling or disturbance of the soil in the area of the septic tank system or repair area.
- CONSTRUCTION AUTHORIZATION must be obtained prior to receiving a Building Permit. The Construction Authorization is NOT transferable. Do not clear, grade, fill or disturb soil prior to obtaining a Construction Authorization.
- Domestic-type wastewater only. No industrial process wastewater may be discharged into the system.

Basement	___ Yes	✓ No	___ Partial Basement	
Type Primary Wastewater System Type (circle one): I II (III) IV V VI	✓ Conventional ___ Prefabricated, permeable block panel system ___ Shallow Placed Conventional	___ Low Pressure Pipe ___ Large Diameter Pipe ___ Fill ___ Other	___ Innovative or Experimental: ___ IWWS-93-1 ___ IWWS-93-2 ___ IWWS-94-1	
.3 Long-term acceptance rate	480 Max gallons/day wastewater flow	1610 Absorption Area (sq ft)	9' Trench spacing (min. on centers)	
Yes Serviced by private well	Existing Gallon septic tank	535' Total trench length (ft)	24" Maximum trench depth (At least 12" of provisionally suitable soil must remain between trench bottom and unsuitable soil conditions)	
4 Bedrooms in residence	1000 Gallon pump tank	12" Depth of stone		
Any surface waters present: NO Type:		Minimum separation distance:		
Site modifications required: Abandon existing drainfield				
Additional Conditions: Septic system alteration				
Repair Area System Type Type (circle one): I II (III) IV V VI	✓ Conventional ___ Prefabricated, permeable block panel system ___ Shallow Placed Conventional	___ Low Pressure Pipe ___ Large Diameter Pipe ___ Fill ___ Other	___ Innovative or Experimental: ___ IWWS-93-1 ___ IWWS-93-2 ___ IWWS-94-1	
1610 Absorption Area (Sq ft) 535' Total Trench Length (Ft)	12" Depth of Stone Trench	9' Trench spacing (min. on centers)	24" Maximum Trench Depth	
For existing system, enter the year originally installed:				

The undersigned, an authorized agent of the MECKLENBURG COUNTY HEALTH DEPARTMENT, certifies that the Department has approved the Request for t
Job Location contained in this document. This approval is granted in accordance with the provisions of Laws and Rules For Sewage, Treatment and Disposal in effe
at the time of issuance of the permit and is subject to the following provisions:

- ... No work shall be conducted on the septic tank system until an Installation, Construction, Alteration and/or Repair Approval is granted by this Departme
- ... This Improvement permit is transferable.

Phil S. Walker 3/18/97
DEHNR Authorized Agent Date

Robert Levy for John S. Clark Company 3/18/97
Owner/Agent Signature Date

MECKLENBURG COUNTY
HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
c/o HAL MARSHALL CTR.
SUITE 211
700 N. TRYON ST.
CHARLOTTE, N.C. 28202.
(704) 336-5102

NORTH CAROLINA DEPARTMENT OF
ENVIRONMENTAL, HEALTH,
AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

PROPOSED PLOT PLAN


HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON STREET
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 712

TC: 027-551-98

⊗ Existing well

Draw in and name all roads adjoining the property. Draw in and accurately dimension the lot concerned. Accurately indicate property boundaries proposed and/or existing structures and driveways, underground utilities, and wells and springs within 100 feet of the proposed building or drainfield.

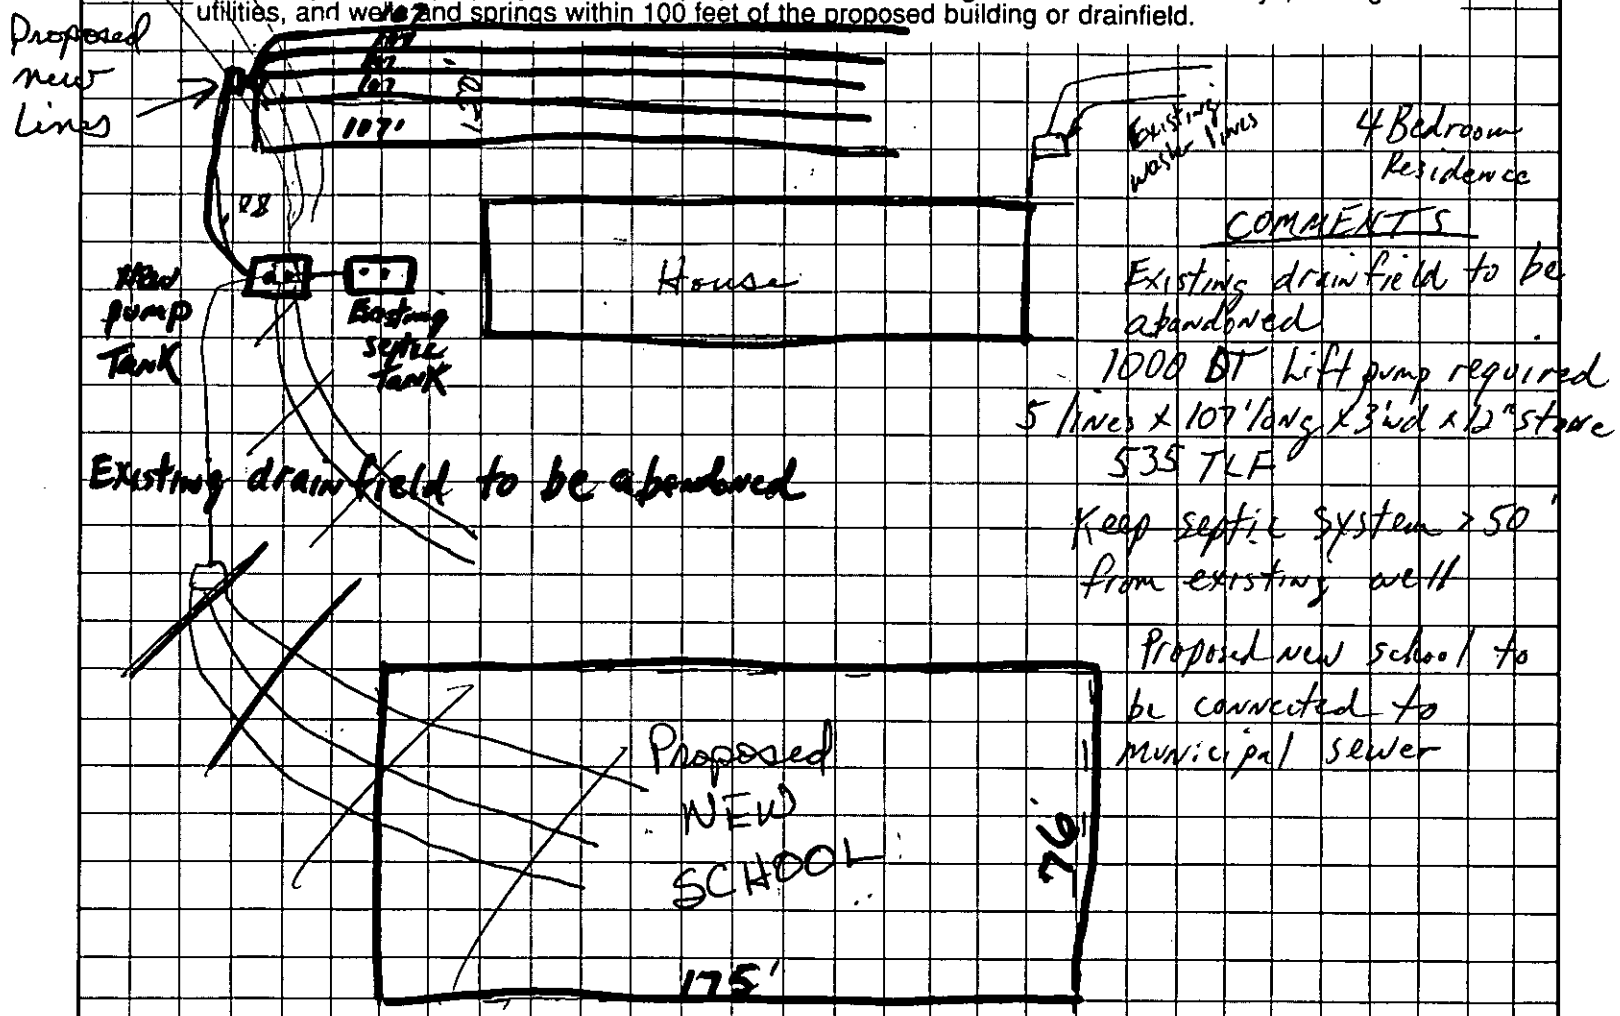

COMMENTS

Existing drainfield to be abandoned

1000 GT Lift pump required

5 lines x 107'long x 3'wd x 12"stone

535 TLF

Keep septic system > 50' from existing well

Proposed new school to be connected to municipal sewer

Robert Lever for John S. Clark, Inc.
OWNER/AGENT SIGNATURE

DATE 3-10-97

APPROVAL DATE 3/18/97

Robert Lever for John S. Clark Company

White - Health Department's Copy Canary - E.H.S. Copy Pink - Owner's Copy

DEPARTMENT OF ENVIRONMENT, HEALTH, AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

PROPERTY ID #: Sheet ___ of ___
COUNTY:

SOIL/SITE EVALUATION
for ON-SITE WASTEWATER SYSTEM

= #1 7/2

PO 022551-96

OWNER: Maurice P. Vaughn Sr. APPLICANT: _____
ADDRESS: 4801 Prospect Church Rd Monroe APPLICATION DATE: _____ DATE EVALUATED: _____
PROPOSED FACILITY: residence PROPOSED DESIGN FLOW (.1949): 480gpd PROPERTY SIZE: .2
LOCATION OF SITE: 4801 Prospect Church Rd PROPERTY RECORDED: _____
WATER SUPPLY: ☐ Private ☑ Public ☐ Well ☐ Spring ☐ Other _____
EVALUATION METHOD: ☐ Auger Boring ☐ Pit ☐ Cut
TYPE OF WASTEWATER: ☐ Sewage ☐ Industrial Process ☐ Mixed

PROFILE #	Slopes 2-6% 1940 LANDSCAPE POSITION/ SLOPE %	HORIZON DEPTH (IN.)	SOIL MORPHOLOGY (.1941) STRUCTURE/ TEXTURE	SOIL MORPHOLOGY (.1941) CONSISTENCE/ MINERALOGY	OTHER PROFILE FACTORS 1942 SOIL WETNESS/ COLOR	1943 SOIL DEPTH	1956 SAPRO CLASS	1944 RESTR HORIZ	PROFILE CLASS & LT.
1	LS	0-6"	gr/cl	Fr/SEXP/SS/SP	740" TO soil wetness	40"	N/A	None	.39/P2 IV P3
		6-40"	SBK/C	F:/SEXP/S/P					
		40-48"	SBK/cl	FR/SEXP/SS/SP					
2	LS	0-8"	gr/cl	Fr/SEXP/SS/SP	748" TO soil wetness	48"	N/A	None	.39/P2 IV P3
		8-48"	SBK/C	F:/SEXP/S/P					
3	LS	0-6"	gr/cl	Fr/SEXP/SS/SP	746" TO soil wetness	46"	N/A	None	.39/P2 IV P3
		6-46"	SBK/C	F:/SEXP/S/P					
4									

DESCRIPTION	INITIAL SYSTEM	REPAIR SYSTEM
Available Space (.1945)	P2	P3
System Type(s)		

OTHER FACTORS (.1946): _____
SITE CLASSIFICATION (.1948): profusely suitable
EVALUATED BY: W.B. Wade 3-14-97
OTHER(S) PRESENT: LSS

OMMENTS: Would require pump

LEGEND

use the following standard abbreviations

ANDSCAPE POSITION	GROUP	SOIL TEXTURE	CONVENTIONAL 1955 LTAR	LPP 1957 LTAR	MINERALOGY/ CONSISTENCE	STRUCTURE
C (Concave Slope)	I	S (Sand)	1.2 - 0.8	0.6 - 0.4	NEXP (Non-expansive)	G (Single Grain)
V (Convex Slope)		LS (Loamy Sand)			SEXP (Slightly Expansive)	M (Massive)
(Drainage Way)					EXP (Expansive)	CR (Crumb)
S (Debris Slump)	II	SL (Sandy Loam)	0.8 - 0.6	0.4 - 0.3		GR (Granular)
P (Flood Plain)		L (Loam)				SBK (Subangular Blocky)
S (Foot Slope)						ABK (Angular Blocky)
(Head Slope)	III	SI (Silt)	0.6 - 0.3	0.3 - 0.15		PL (Platy)
(Linear Slope)		SICL (Silty Clay Loam)				PR (Prismatic)
(Nose Slope)		CL (Clay Loam)			MOIST	WET
(Ridge)		SCL (Sandy Clay Loam)				
(Shoulder Slope)		SLC (Silt Loam Clay)			VFR (Very Friable)	NS (Non-sticky)
(Terrace)					FR (Friable)	SS (Slightly Sticky)
	IV	SC (Sandy Clay)	0.4 - 0.1	0.2 - 0.05	FI (Firm)	S (Sticky)
		SIC (Silty Clay)			VFI (Very Firm v. Very Sticky)	VS (Very Sticky)
					EFI (Extremely Firm)	NP (Non-plastic)
		O (Organic)	None			SP (Slightly Plastic)
						P (Plastic)
						VP (Very Plastic)

OTES


ORIZON DEPTH	In inches below natural soil surface
EPTH OF FILL	In inches from land surface
ESTRICTIVE HORIZON	Thickness and depth from land surface
APROLITE	S(suitable) or U(unsuitable)
OIL WETNESS	Inches from land surface to free water or inches from land surface to soil colors with chroma 2 or less - record Munsell color chip designation
LASSIFICATION	S (Suitable), PS (Provisionally Suitable), or U (Unsuitable)

valuation of saprolite shall be by pits.

ong-term Acceptance Rate (LTAR): gal/day/ft²

Show profile locations and other site features (dimensions, reference or benchmark, and North).

7/2

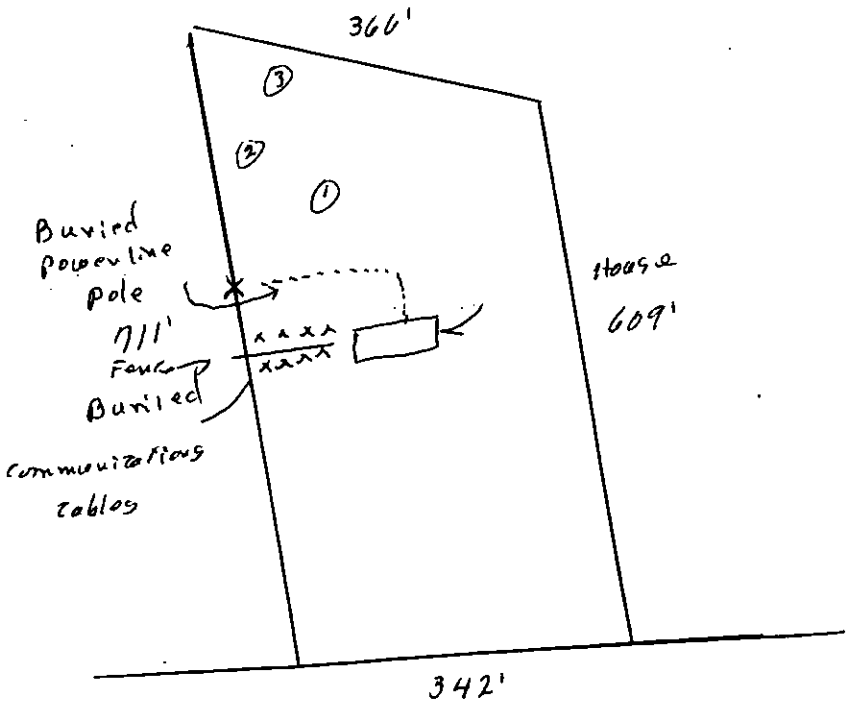

Prosperity Ch. Rd.

DEPARTMENT OF ENVIRONMENT, HEALTH, AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

PROPERTY ID: ___ of ___
COUNTY: ___

SOIL/SITE EVALUATION
for ON-SITE WASTEWATER SYSTEM

= #1 712

PO 022551-9

OWNER: Martin P. Vaughn Jr. APPLICANT: ___
ADDRESS: 4601 Prosperity Church Road APPLICATION DATE: ___ DATE EVALUATED: ___
PROPOSED FACILITY: residence PROPOSED DESIGN FLOW (.1949): 480gpd PROPERTY SIZE: .2
LOCATION OF SITE: 4601 Prosperity Church Rd PROPERTY RECORDED: ___
WATER SUPPLY: ☐ Private ☑ Public ☐ Well ☐ Spring ☐ Other ___
EVALUATION METHOD: ☑ Auger Boring ☐ Pit ☐ Cut
TYPE OF WASTEWATER: ☐ Sewage ☐ Industrial Process ☐ Mixed

PROFILE #	1940 LAND-SCAPE POSITION/ SLOPE %	HORIZON DEPTH (IN.)	SOIL MORPHOLOGY (.1941) 1941 STRUCTURE/ TEXTURE	1941 CONSISTENCE/ MINERALOGY	OTHER PROFILE FACTORS 1942 SOIL WETNESS/ COLOR	1943 SOIL DEPTH	1956 SAPRO CLASS	1944 RESTR HORIZ	PROP CLASS & LTR
1	LS	0-6"	gr/cl	Fr/SEXP/SS/SP	7 40" TO soil wetness	40"	N/A	None	1941 IV P3
		6-40"	SBK/C	F/SEXP/SS/SP					
		40-48"	SBK/cl	FR/SEXP/SS/SP					
2	LS	0-8"	gr/cl	Fr/SEXP/SS/SP	7 46" TO soil wetness	48"	N/A	None	1941 IV P3
		8-46"	SBK/C	F/SEXP/SS/SP					
3	LS	0-6"	gr/cl	Fr/SEXP/SS/SP	7 46" TO soil wetness	46"	N/A	None	1941 IV P3
		6-46"	SBK/C	F/SEXP/SS/SP					
4									

DESCRIPTION	INITIAL SYSTEM	REPAIR SYSTEM
Available Space (.1945)	P3	P3
System Type(s)		

OTHER FACTORS (.1946): ___
SITE CLASSIFICATION (.1948): prelim. evaluation suitable
EVALUATED BY: WR Mauldin 3-14-97
OTHER(S) PRESENT: LSS

COMMENTS: Would require sewer

LEGEND

use the following standard abbreviations

LANDSCAPE POSITION	GROUP	SOIL TEXTURE	CONVENTIONAL 1955 LTAR	LPP 1957 LTAR	MINERALOGY/ CONSISTENCE	STRUCTURE
C (Concave Slope)	I	S (Sand)	1.2 - 0.8	0.6 - 0.4	NEXP (Non-expansive)	G (Single Grain)
V (Convex Slope)		LS (Loamy Sand)			SEXP (Slightly Expansive)	M (Massive)
(Drainage Way)					EXP (Expansive)	CR (Crumb)
S (Debris Slump)	II	SL (Sandy Loam)	0.8 - 0.6	0.4 - 0.3		GR (Granular)
P (Flood Plain)		L (Loam)				SBK (Subangular Blocky)
S (Foot Slope)						ABK (Angular Blocky)
(Head Slope)	III	SI (Silt)	0.6 - 0.3	0.3 - 0.15		PL (Platy)
(Linear Slope)		SICL (Silty Clay Loam)				PR (Prismatic)
(Nose Slope)		CL (Clay Loam)			MOIST	WET
(Ridge)		SCL (Sandy Clay Loam)				
(Shoulder Slope)		SLC (Silt Loam Clay)			VFR (Very Friable)	NS (Non-sticky)
(Terrace)					FR (Friable)	SS (Slightly Sticky)
	IV	SC (Sandy Clay)	0.4 - 0.1	0.2 - 0.05	FI (Firm)	S (Sticky)
		SIC (Silty Clay)			VFI (Very Firm v. Very Sticky)	VS (Very Sticky)
					EFI (Extremely Firm)	NP (Non-plastic)
		O (Organic)	None			SP (Slightly Plastic)
						P (Plastic)
						VP (Very Plastic)

NOTES


HORIZON DEPTH	In inches below natural soil surface
DEPTH OF FILL	In inches from land surface
RESTRICTIVE HORIZON	Thickness and depth from land surface
SAPROLITE	S(suitable) or U(unsuitable)
SOIL WETNESS	Inches from land surface to free water or inches from land surface to soil colors with chroma 2 or less - record Munsell color chip designation
CLASSIFICATION	S (Suitable), PS (Provisionally Suitable), or U (Unsuitable)

Evaluation of saprolite shall be by pits.

Long-term Acceptance Rate (LTAR): gal/day/ft²

Show profile locations and other site features (dimensions, reference or benchmark, and North).

712

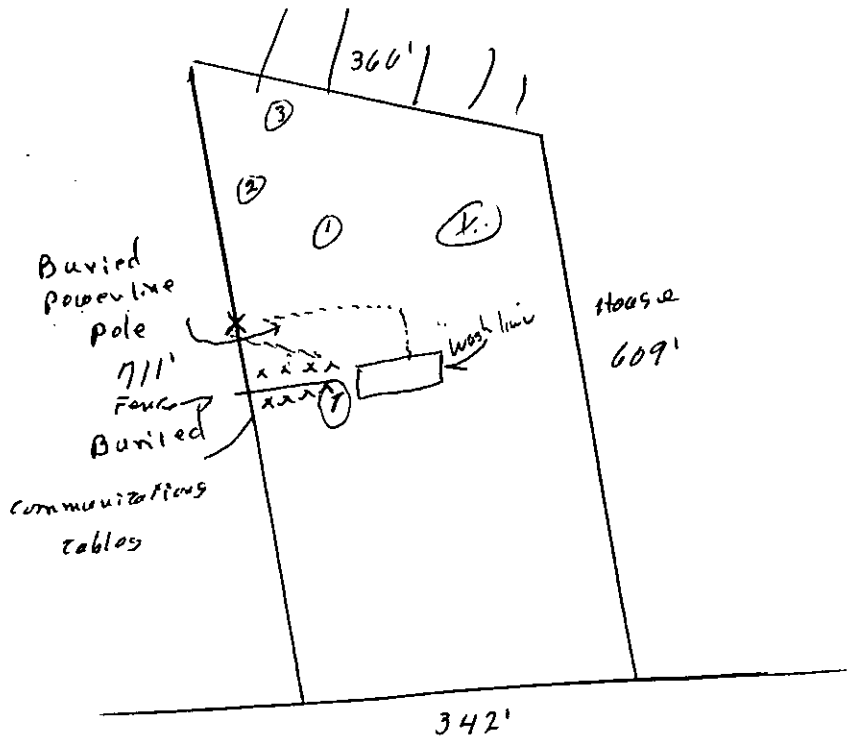

Prosperity ch. Rd.

2


PROPOSED PLOT PLAN

HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON STREET
CHARLOTTE, NC 28202
PHONE (704) 336-5102

FILE: 712

TC: 027-551-98

Draw in and name all roads adjoining the property. Draw in and accurately dimension the lot concerned. Accurately indicate property boundaries proposed and/or existing structures and driveways, underground utilities, and wells and springs within 100 feet of the proposed building or drainfield.

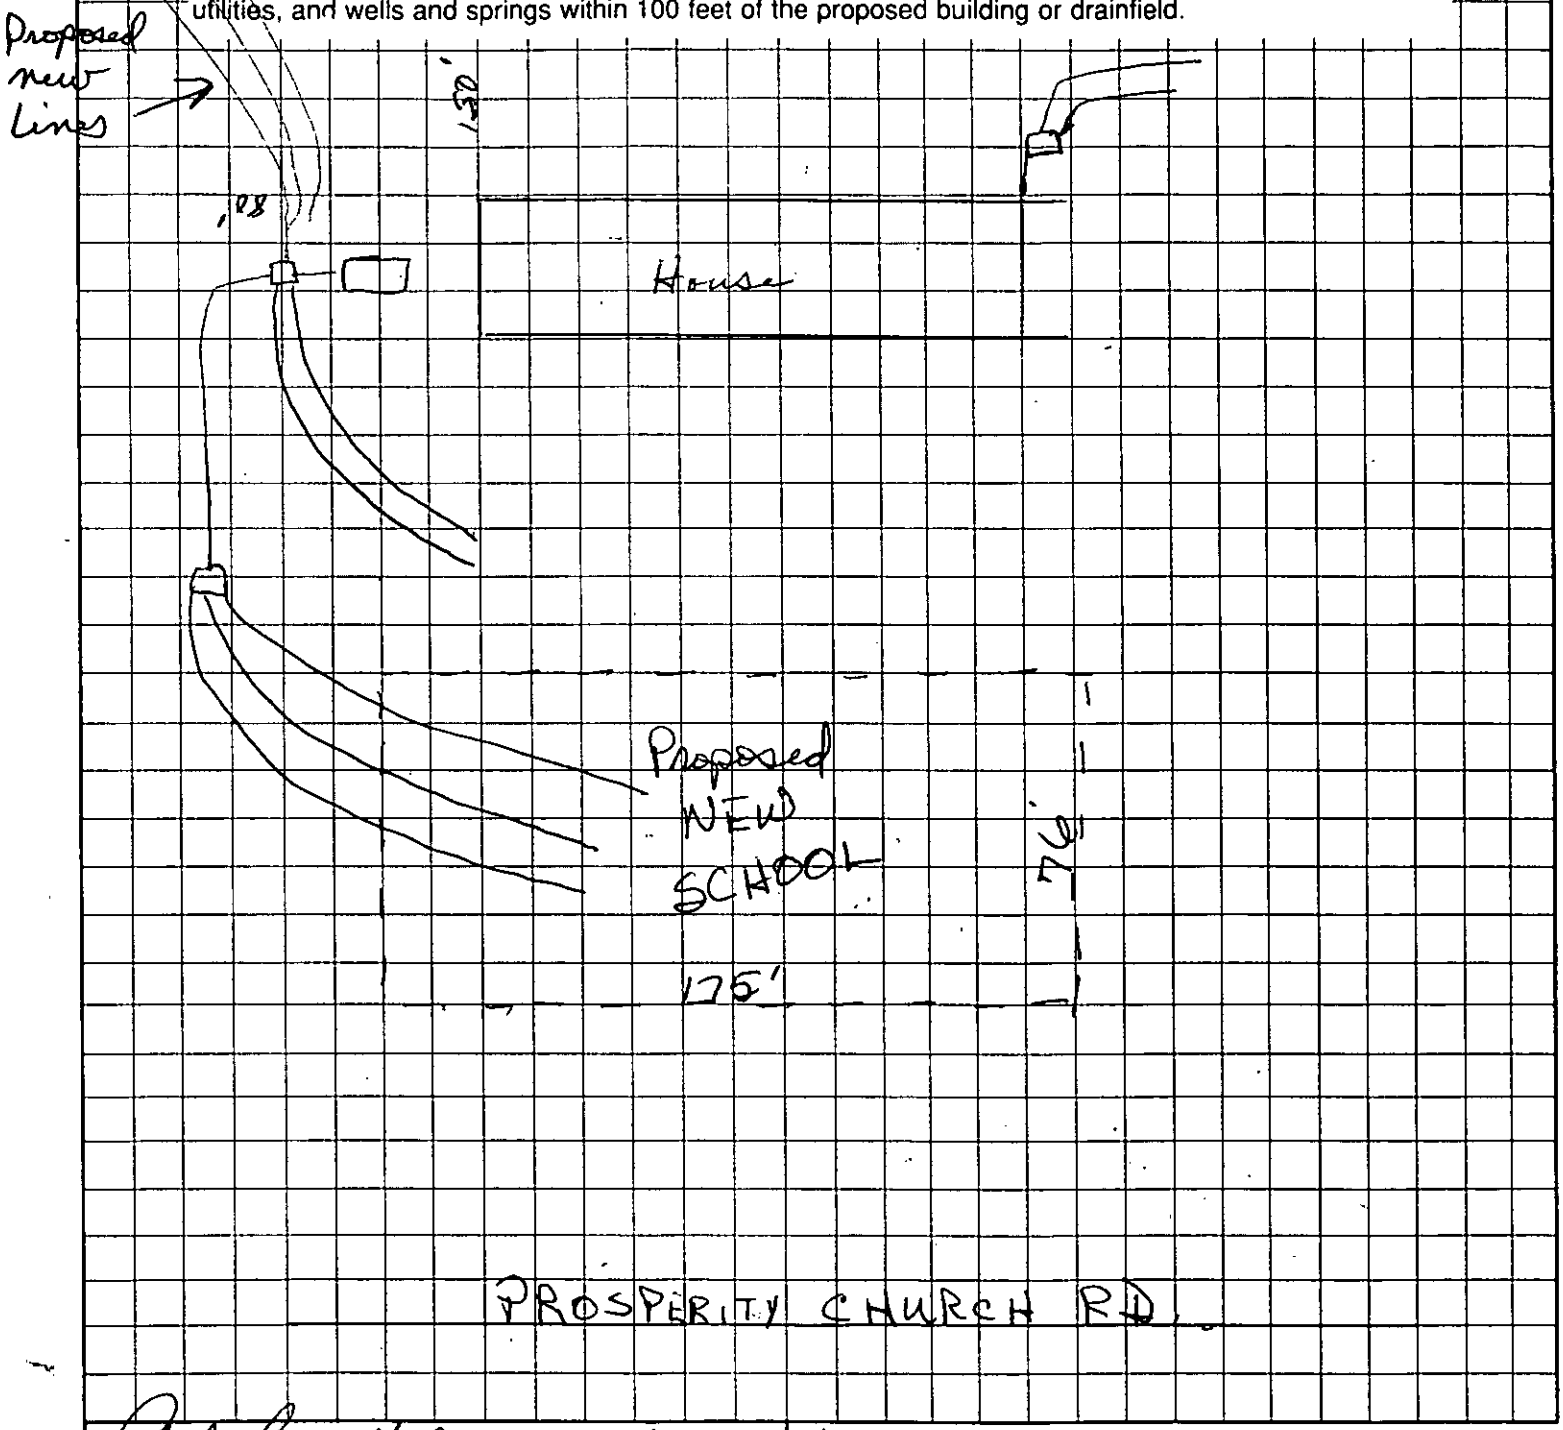

Robert Leverette John S. Clark, Jr.

OWNER/AGENT SIGNATURE

APPROVAL DATE

DATE 3-10-97

White - Health Department's Copy Canary - E.H.S. Copy Pink - Owner's Copy
