Groundwater & Wastewater Services
Septic Project File & Data Review Worksheet

GWS File #: 1307 B WASPS App #: 2040

Primary ES assigned to project: DC

Secondary ES assigned to project:

Project Type: New System ☑ Alteration ☐ Repair ☐ Modified Plot Plan ☐

I. File Review:

Rule or Law				
	Permit Application			
.1937(d)	Is the Application complete	Yes ☑	No ☐	N/A ☐
.1937(d)	Is there a Site plan/Plat with application	Yes ☑	No ☐	N/A ☐
.1937(d)	Is the Facility shown?	Yes ☑	No ☐	N/A ☐
.1937(d)	Are appurtenances shown	Yes ☑	No ☐	N/A ☐
	Site Evaluation Information			
.1939 (a)(1)	Topography and Landscape Position Recorded?	Yes ☑	No ☐	N/A ☐
.1940 (a-g)	Slope % Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(2)	Texture Class Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(2)	Structure type Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(2)	Consistence Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(2)	Mineralogy Recorded?	Yes ☐	No ☐	N/A ☐
.1939 (a)(3)	Soil Wetness Condition Recorded?	Yes ☐	No ☐	N/A ☑
.1939 (a)(4)	Soil Depth to Rock or Parent Material Recorded When Encountered	Yes ☐	No ☐	N/A ☑
.1939 (a)(5)	Depth to Restrictive Horizons Recorded When Encountered?	Yes ☐	No ☐	N/A ☑
.1939 (a)(6)	Sufficient Available Space Recorded?	Yes ☑	No ☐	N/A ☐
.1937(m)	Are the Profile Locations Shown?	Yes ☑	No ☐	N/A ☐
.1939(a)	Are the S/PS Profiles in system & in repair area?	Yes ☑	No ☐	N/A ☐
& .1945(b)	Number of auger borings made: 5			
	Were sufficient auger borings made?	Yes ☑	No ☐	N/A ☐
.1939(d), .1955, .1956, .1957	LTAR .3	Yes ☑	No ☐	N/A ☐
	Improvement Permit/Construction Authorization			
.1937(g) 130A-336(a)	Proposed System Type stated-Initial	Yes ☑	No ☐	N/A ☐
.1945(b) 130A-336 (a)(3)	Proposed System Type stated-Repair	Yes ☑	No ☐	N/A ☐
	System location identifiable by setbacks - Initial	Yes ☑	No ☐	N/A ☐
.1937(g) .1945(b)	System components shown – Initial	Yes ☑	No ☐	N/A ☐
.1945(b)	Repair area shown	Yes ☑	No ☐	N/A ☐
.1937 (f)(g)	Does System design match facility, flow & WWcharacteristics?	Yes ☑	No ☐	N/A ☐
.1937 (f)(g)	Is System design consistent with soil/site conditions?	Yes ☑	No ☐	N/A ☐
.1937 (f)(g)	Is the System located in the approved area?	Yes ☑	No ☐	N/A ☐
130A-336(a)	Is the Design flow (gpd) indicated?	Yes ☑	No ☐	N/A ☐

130A-336(a)	Number of Bedrooms, employees, seats, etc. indicated?	Yes ☐	No ☐	N/A ☐
.1937(g)	Trench depth indicated?	Yes ☐	No ☐	N/A ☐
.1937(g)	Trench width indicated?	Yes ☐	No ☐	N/A ☐
.1937(g)	Trench length indicated?	Yes ☐	No ☐	N/A ☐
130A-336(a)(1)	Proposed/existing well shown?	Yes ☐	No ☐	N/A ☐
130A-336(a)(1)	Property line lengths shown?	Yes ☐	No ☐	N/A ☐
130A-336(a)	Facility/appurtenance setbacks shown from fixed points?	Yes ☐	No ☐	N/A ☐
	Operation Permit			
.1937(i)	System type as described in table V(a) of rule .1961	Yes ☐	No ☐	N/A ☐
.1937(i)	Conditions for system performance, operation, maintenance, monitoring and reporting.	Yes ☐	No ☐	N/A ☐

II. WASPS Review:

Construction authorization issued	Yes ☐	No ☐	N/A ☐
Installation approval issued	Yes ☐	No ☐	N/A ☐
Operation permit issued	Yes ☐	No ☐	N/A ☐
Other related documentation	Yes ☐	No ☐	N/A ☐

Items requiring correction/modification: _____

Comments:

_____

_____

_____

_____

_____

IA issued date: _____

OP issued date: _____

Review performed by: _____

Date performed: 12-2007

FILE NUMBER: 7387B CK# 6284 Revised On: August 31, 2007 APPLICATION NUMBER: 2840

SEPTIC FEE: 200.00 DATE: 10/16/07 ggc

MECKLENBURG COUNTY GROUNDWATER & WASTEWATER SERVICES
APPLICATION FOR A RESIDENTIAL SITE IMPROVEMENT PERMIT/ CONSTRUCTION AUTHORIZATION FOR AN ON-SITE WASTEWATER SYSTEM, NEW WELL INSTALLATION, OR REPAIR OF EXISTING WELL

WELL FEE: _____ DATE: _____

1. SEPTIC / TYPE APPLICATION: ☐ NONE ☒ NEW SYSTEM ☐ ALTERATION ☐ REPAIR ☐ MODIFIED PLOT PLAN

2. WELL / TYPE APPLICATION: ☒ NONE ☐ NEW WELL ☐ MAJOR REPAIR ☐ ABANDONMENT

3. JOB LOCATION INFORMATION:
TAX PARCEL NUMBER: 139-161-08
STREET ADDRESS: Old Camden Rd
CITY: Midland
STATE: NC ZIP: 28107
SUBDIVISION NAME:
LOT #: 1 LOT SIZE (acres): .688
TOWNSHIP:
☐ 0-MECKLENBURG ☐ 3-CORNELIUS ☐ 6-HUNTERSVILLE
☐ 1-CHARLOTTE ☐ 4-PINEVILLE ☒ 7-MINT HILL
☐ 2-DAVIDSON ☐ 5-MATTHEWS

4. BUILDING INFORMATION:
BUILDING TYPE:
☐ SINGLE MOBILE HOME ☐ MODULAR HOME
☐ DOUBLE WIDE ☐ MULTIPLE FAMILY
☒ HOUSE ☐ OTHER _____
HEATED SQUARE FOOTAGE: 3000
NUMBER OF BEDROOMS: 5
NUMBER OF OCCUPANTS:
FOUNDATION TYPE:
☐ CONCRETE SLAB ☐ BASEMENT WITH PLUMBING
☒ CRAWL SPACE ☐ BASMENT WITH NO PLUMBING

5. IF PLANNING TO EXPAND OR ALTER THE EXISTING SYSTEM PLEASE COMPLETE THE FOLLOWING SECTION: ☐ N/A
NUMBER OF BEDROOMS TO BE ADDED: _____ NUMBER OF ADDITIONAL OCCUPANTS IN THE RESIDENCE: _____

6. WATER SUPPLY: ☐ MUNICIPAL ☒ PUBLIC WELL ☐ PRIVATE WELL ☐ SHARED WELL ☐ SPRING

7. PROPOSED USE OF WELL: ☐ N/A ☐ IRRIGATION ☐ POTABLE ☐ GEOTHERMAL ☐ OTHER

8. PLEASE INDICATE AND RANK DESIRED SEPTIC SYSTEM TYPE(S) IN ORDER OF PREFERENCE *(1-MOST DESIRED 5-LEAST DESIRED)*:

	☒ ANY TYPE	☐ CONVENTIONAL	☐ ACCEPTED	☐ INNOVATIVE	☐ ALTERNATIVE	☐ OTHER
8A. RANK:	4	1	____	2	3	____

9. DO ANY OF THE FOLLOWING APPLY TO THE PROPERTY IN QUESTION? IF "YES" PLEASE ATTACH SUPPORTING DOCUMENTATION.

BURIED CABLES, LANDFILLS, STUMPHOLES	☐ YES ☒ NO	GRADING/SOIL REMOVAL PERFORMED	☐ YES ☒ NO
EXISTING WASTEWATER (SEPTIC) SYSTEMS	☐ YES ☒ NO	JURISDICTIONAL WETLANDS	☐ YES ☒ NO
WELLS, SPRINGS, OR WATER LINES	☐ YES ☒ NO	APPROVAL REQUIRED BY ANY OTHER PUBLIC AGENCY	☐ YES ☒ NO
EASEMENTS OR RIGHT-OF-WAYS	☐ YES ☒ NO	WASTEWATER OTHER THAN DOMESTIC SEWAGE	☐ YES ☒ NO

10. PROPERTY OWNER:
NAME: Gold Medallion Homes, LLC
ADDRESS: 5923-A Stockbridge Drive
CITY: Monroe
STATE: NC ZIP: 28110
HOME PHONE: WORK PHONE: (704)821-7606
MOBILE PHONE: FAX:

11. OWNER'S LEGAL REPRESENTATIVE, IF APPLICABLE:
NAME: Joseph L. Collins
ADDRESS: 1101 Lester Mullis Road
CITY: Indian Trail
STATE: NC ZIP: 28079
HOME PHONE: WORK PHONE:
MOBILE PHONE: (704)641-5898 FAX: (704)753-5898

12. WHAT DATE WAS THE PROPERTY ORIGINALLY DEEDED AND RECORDED? 9/7/2007
13 WHAT IS THE ANTICIPATED CLOSING DATE FOR THIS PROPERTY? already closed on 9/7/2007


14. SEPTIC SYSTEM PERMIT APPLICATION SIGNATURE SECTION:
If the information in this application is falsified, changed, or the site is altered, then the Improvement Permit and Authorization to Construct shall become invalid. I have read this application and certify that the information provided herein is true, complete and correct. Authorized county and state officials are granted right of entry to conduct necessary inspections to determine compliance with applicable laws and rules. I understand that I am solely responsible for the proper identification and labeling of all property lines and corners and making the site accessible so that a complete site evaluation can be performed. The permit is valid for either 60 months or is non-expiring depending upon the documentation submitted: complete site plan = 60 months, complete plat = non-expiring.

Joseph L Collins 10/16/07
Property Owner's or Owner's Legal Representative Signature Date

15. WELL PERMIT APPLICATION SIGNATURE SECTION:
If the information in this application is falsified, changed, or the site is altered, then the Well Permit shall become invalid. I have read this application and certify that the information provided herein is true, complete and correct. Authorized county and state officials are granted right of entry to conduct necessary inspections to determine compliance with applicable laws and rules. I understand that I am solely responsible for the proper identification and labeling of all property lines and corners and making the site accessible so that a complete site evaluation can be performed. The permit is valid for a period of 12 months from the date of issuance.

Property Owner's or Owner's Legal Representative Signature Date

☐ SURVEY PLAT TO SCALE SUBMITTED ☒ SCALED SITE PLAN SUBMITTED ☐ UN-SCALED SITE PLAN SUBMITTED

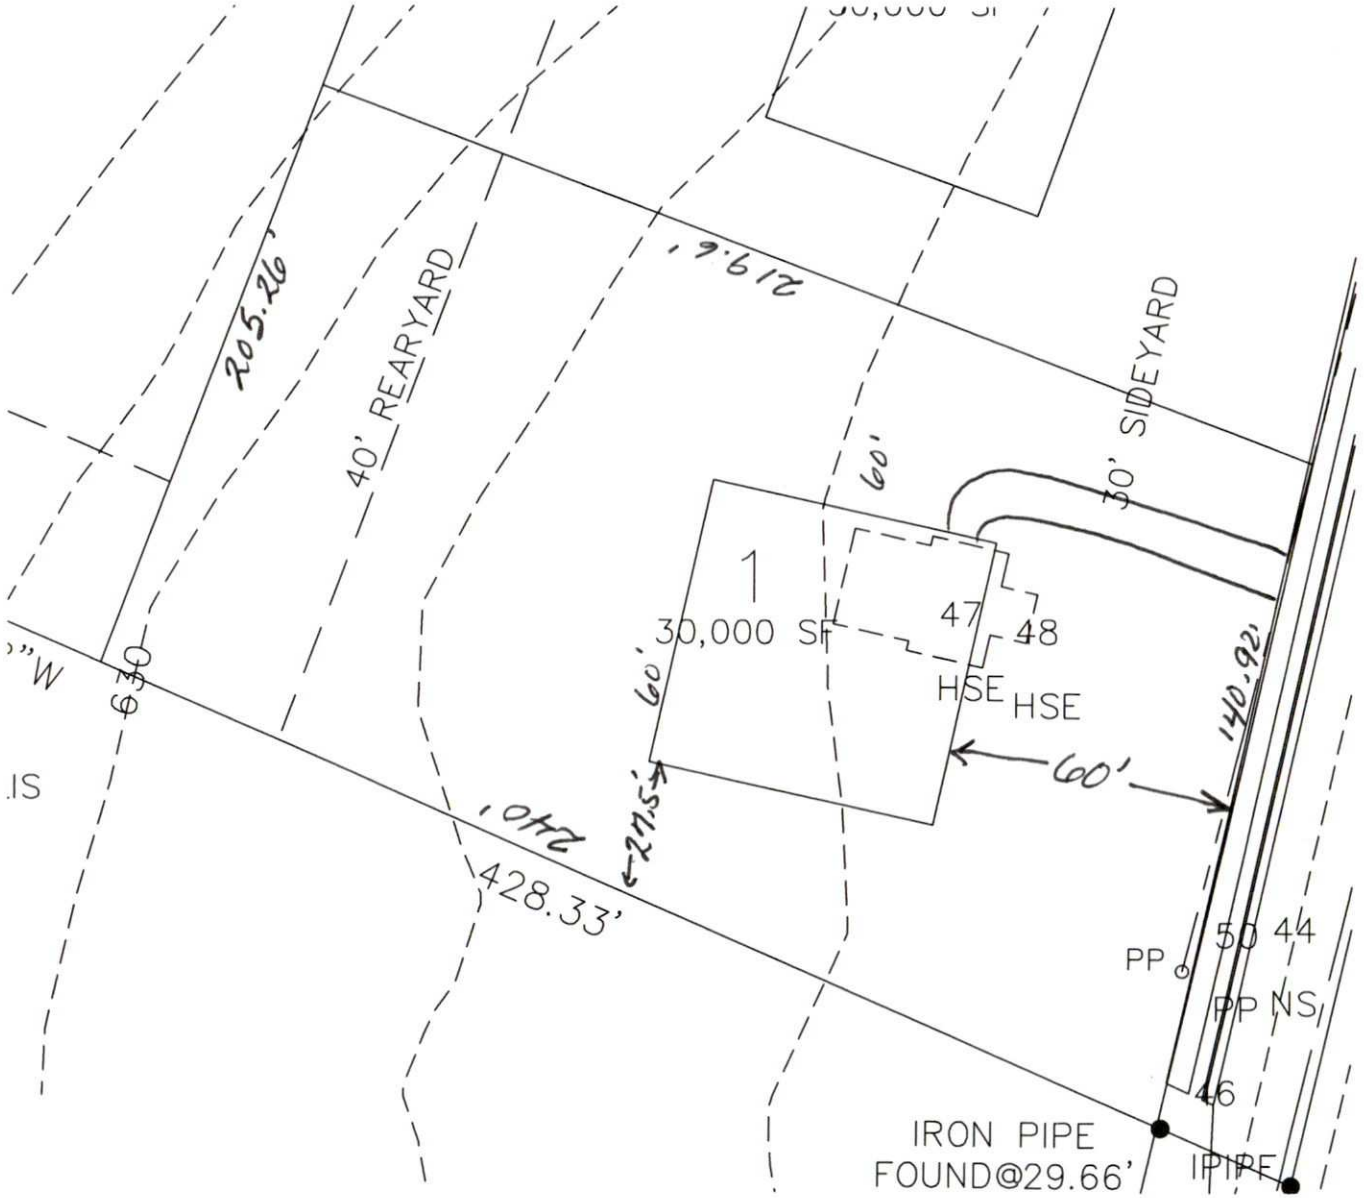
205.26'
40' REARYARD
219.12'
60'
30' SIDEYARD
1
30,000 SF
47
48
HSE
HSE
60'
140.92'
60'
27.5'
240'
428.33'
PP
50
44
PP NS
46
IRON PIPE
FOUND@29.66'
IPIPE

1"=50' 40'

PROPOSED PLOT PLAN

HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH DIVISION
700 NORTH TRYON ST., SUITE 211
CHARLOTTE, NC 28202
PHONE (704) 336-5103


OLD CAMDEN RD. LOT 1

FILE: 7387B

TC: 139-161-08

Draw in and name all roads adjoining the property. Draw in and accurately dimension the lot concerned. Accurately indicate property boundaries proposed and/or existing structures and driveways, underground utilities, and wells and springs within 100 feet of the proposed building or drainfield.

- SEPTIL SYSTEM DESIGN FOR A 5 BEDROOM HOUSE.
- 600 GAL/DAY MAX
- LTAR = 0.3 GAL/DAY/FT²

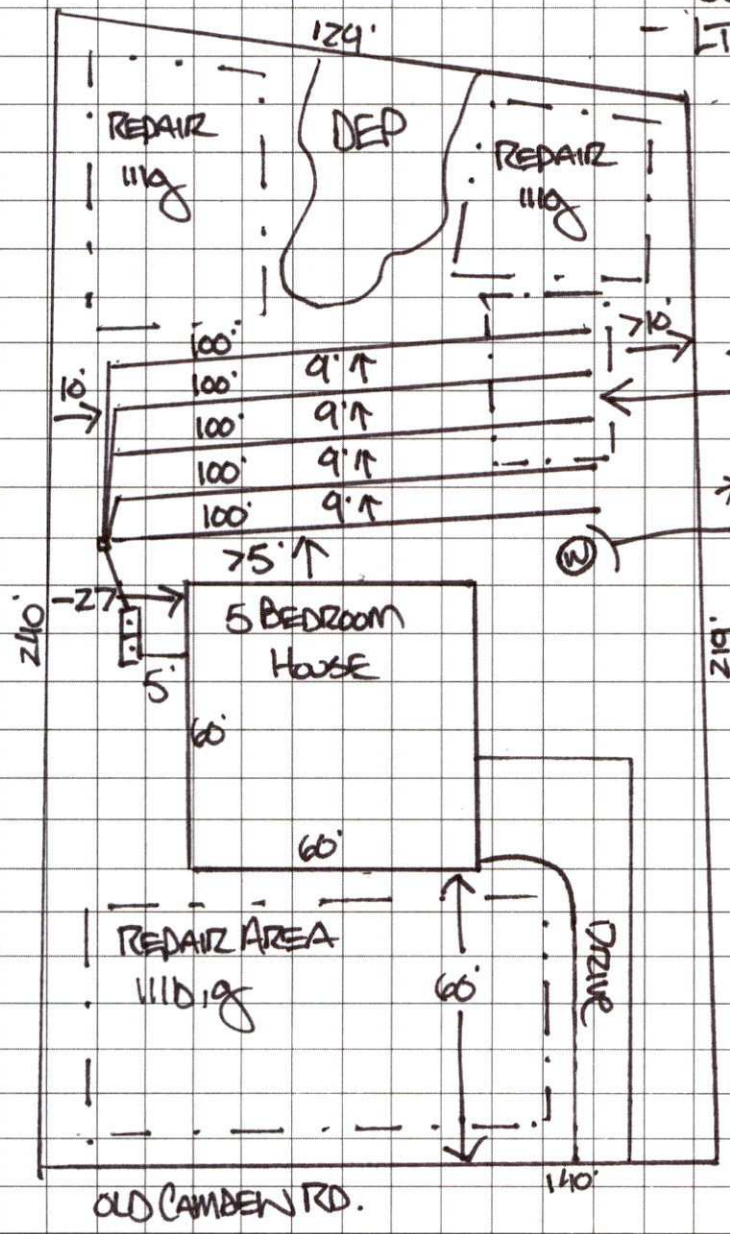

* EXISTING DETACHED GARAGE TO BE REMOVED.

* EXISTING WELL TO BE PROPERLY ABANDONED BEFORE INSTALLATION PERMIT WILL BE ISSUED

INNOVATIVE, 25% REDUCTION TYPE III g

INSTALL 5 LINES @ 100' EA. PLACE LINES LEVEL, ON CONTOUR & ON 9' CENTERS.

1500 GAL SEPTIL TANK

REPAIR AREA IIID,g

SETBACKS: 75' FROM HOUSE
10' FROM PROPERTY LINE
50' FROM ANY WELL

Matthew Cohn
OWNER/AGENT SIGNATURE

DATE 11-18-08

APPROVAL DATE

White - Health Department's Copy

Canary - E.H.S. Copy

Pink - Owner's Copy

Department of Environment, Health, and Natural Resources
Division of Environmental Health
On-site Wastewater Section

Sheet: 1 of 2
Property ID: PO 139-161-08
Lot #: 1
File #: 7387B
AppID: 2840

SOIL/SITE EVALUATION for ON-SITE WASTEWATER SYSTEM

Owner: Gold Medallion Homes LLC
Applicant: Joseph L. Collins
Address: 5923-A Stockbridge Drive, Monroe, N. C. 28110
Date Evaluated: 11/14/07
Proposed Facility: Residence
Design Flow (.1949): 600gpd
Property Size: .69a
Location of Site: Old Camden Road
Property Recorded:
Water Supply: [x] Public [ ] Individual [x] Well [ ] Spring [ ] Other
Evaluation Method: [x] Auger Boring [ ] Pit [ ] Cut
Type of Wastewater: [x] Sewage [ ] Industrial Process [ ] Mixed

PROFILE #	.1940 Landscape Position/ Slope%	Horizon Depth (IN.)	SOIL MORPHOLOGY .1941 Structure/ Texture	SOIL MORPHOLOGY .1941 Consistence Mineralogy	b PROFILE FACTORS .1942 Soil Wetness/ Color	.1943 Soil Depth (IN.)	.1956 Sapro Class	.1944 Restr Horiz	Profile Class & LTAR
1	LS, 8	0-8	GR/CL	FR/SEXP/SS/SP	>48" TO SOIL WETNESS	48+	N/A	NONE	PS, IV
		8-48	SBK/C	FI/SEXP/S/P					.3GPD/FT^2
2	"	0-4	GR/CL	FR/SEXP/SS/SP	"	"	"	"	"
		4-48	SBK/C	FI/SEXP/S/P					
3	LS, 6	0-4	GR/CL	FR/SEXP/SS/SP	>40" TO SOIL WETNESS	40	"	"	"
		4-37	SBK/C	FI/SEXP/S/P					
		37-40	SBK/CL	FR/SEXP/SS/SP					
4	"	0-3	GR/CL	"	>48" TO SOIL WETNESS	48+	"	"	"
		3-48	SBK/C	FI/SEXP/S/P					
5	"	0-6	GR/CL	FR/SEXP/SS/SP	"	"	"	"	"
		6-48	SBK/C	FI/SEXP/S/P					
					SITE LTAR .3GPD/FT^2				

Description	Initial System	Repair System
Available Space (.1945)	PS	PS
System Type(s)	IIIg	IIIbg
Site LTAR	0.3	0.3

Other Factors (.1946):
Soil Evaluation By: W. R. Marlin,LSS, 11/14/2007,
Others Present:
Site Classification (.1948): Provisionally Suitable
Site Evaluation By: David Cornelius, RS
Others Present:


COMMENTS:

100% repair, could not locate existing septic tank system, well would need to be properly abandoned, system located, tank pumped and filled in

Landscape Position	Group	Texture	.1955 LTAR	Structure
R-Ridge	I	S-Sand	1.2 - 0.8	SG-Single Grain
SS-Shoulder Slope		LS-Loamy Sand		M-Massive
LS-Linear Slope				CR-Crumb
FS-Foot Slope	II	SL-Sandy Loam	0.8 - 0.6	GR-Granular
NS-Nose Slope		L-Loam		SBK-Subangular Blocky
HS-Head Slope				ABK-Angular Blocky
CC-Concave Slope	III	SI-Silt	0.6 - 0.3	PL-Platy
CV-Convex Slope		SICL-Silty Clay Loam		PR-Prismatic
T-Terrace				
FP-Flood Plain		CL-Clay Loam		
		SCL-Sandy Clay Loam		
	IV	SC-Sandy Clay	0.4 - 0.1	
		SIC-Silty Clay		
		C-Clay		

Consistence Moist	Consistence Wet	Mineralogy
VFR-Very Friable	NS-Non-Sticky	SEXP-Slightly Expansive
FR-Friable	SS-Slightly Sticky	EXP-Expansive
FI-Firm	S-Sticky	
VFI-Very Firm	VS-Very Sticky	
EFI-Extremely Firm	NP-Non-Plastic	
	SP-Slightly Plastic	
	P-Plastic	
	VP-Very Plastic	

Sketch of Soil Evaluation Locations

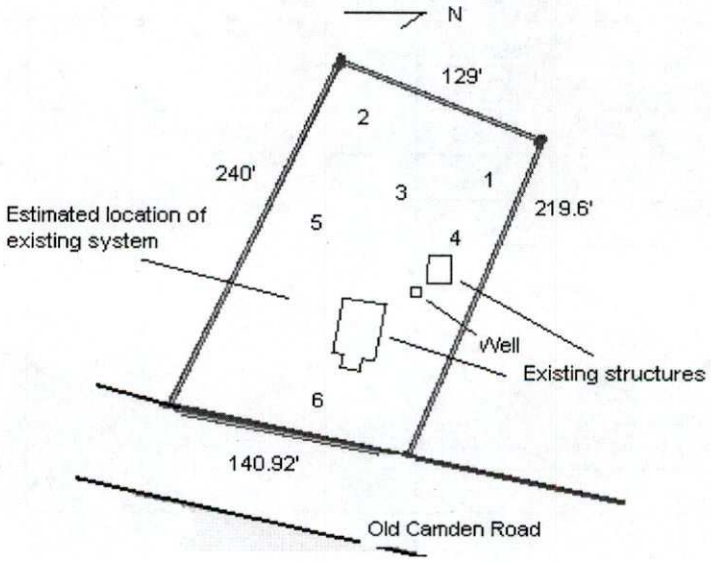

Department of Environment, Health, and Natural Resources
Division of Environmental Health
On-site Wastewater Section

Sheet: 1 of 2
Property ID: PO 139-161-08
Lot #: 1
File #: 7387B
AppID: 2840

SOIL/SITE EVALUATION for ON-SITE WASTEWATER SYSTEM

Owner: Gold Medallion Homes LLC
Applicant: Joseph L. Collins
Address: 5923-A Stockbridge Drive, Monroe, N. C. 28110
Date Evaluated: 11/14/07
Proposed Facility: Residence
Design Flow (.1949): 600gpd
Property Size: .69a
Location of Site: Old Camden Road
Property Recorded:
Water Supply: [x] Public [ ] Individual [x] Well [ ] Spring [ ] Other
Evaluation Method: [x] Auger Boring [ ] Pit [ ] Cut
Type of Wastewater: [x] Sewage [ ] Industrial Process [ ] Mixed

PROFILE #	.1940 Landscape Position/ Slope%	Horizon Depth (IN.)	SOIL MORPHOLOGY .1941 .1941 Structure/ Texture	.1941 Consistence Mineralogy	b PROFILE FACTORS .1942 Soil Wetness/ Color	.1943 Soil Depth (IN.)	.1956 Sapro Class	.1944 Restr Horiz	Profile Class & LTAR
1	LS, 8	0-8	GR/CL	FR/SEXP/SS/SP	>48" TO SOIL WETNESS	48+	N/A	NONE	PS, IV
		8-48	SBK/C	FI/SEXP/S/P					.3GPD/FT^2
2	"	0-4	GR/CL	FR/SEXP/SS/SP	"	"	"	"	"
		4-48	SBK/C	FI/SEXP/S/P					
3	LS, 6	0-4	GR/CL	FR/SEXP/SS/SP	>40" TO SOIL WETNESS	40	"	"	"
		4-37	SBK/C	FI/SEXP/S/P					
		37-40	SBK/CL	FR/SEXP/SS/SP					
4	"	0-3	GR/CL	"	>48" TO SOIL WETNESS	48+	"	"	"
		3-48	SBK/C	FI/SEXP/S/P					
5	"	0-6	GR/CL	FR/SEXP/SS/SP	"	"	"	"	"
		6-48	SBK/C	FI/SEXP/S/P					
					SITE LTAR .3GPD/FT^2				

Description	Initial System	Repair System
Available Space (.1945)		
System Type(s)		
Site LTAR		

Other Factors (.1946):
Soil Evaluation By: W. R. Marlin,LSS, 11/14/2007. W. R. Marlin
Others Present:
Site Classification (.1948):
Site Evaluation By:
Others Present:


COMMENTS:

100% repair, could not locate existing septic tank system, well would need to be properly abandoned, system located, tank pumped and filled in

Landscape Position	Group	Texture	.1955 LTAR	Structure
R-Ridge	I	S-Sand	1.2 - 0.8	SG-Single Grain
SS-Shoulder Slope		LS-Loamy Sand		M-Massive
LS-Linear Slope				CR-Crumb
FS-Foot Slope	II	SL-Sandy Loam	0.8 - 0.6	GR-Granular
NS-Nose Slope		L-Loam		SBK-Subangular Blocky
HS-Head Slope				ABK-Angular Blocky
CC-Concave Slope	III	SI-Silt	0.6 - 0.3	PL-Platy
CV-Convex Slope		SICL-Silty Clay Loam		PR-Prismatic
T-Terrace				
FP-Flood Plain		CL-Clay Loam		
		SCL-Sandy Clay Loam		
	IV	SC-Sandy Clay	0.4 - 0.1	
		SIC-Silty Clay		
		C-Clay		

Consistence Moist	Consistence Wet	Mineralogy
VFR-Very Friable	NS-Non-Sticky	SEXP-Slightly Expansive
FR-Friable	SS-Slightly Sticky	EXP-Expansive
FI-Firm	S-Sticky	
VFI-Very Firm	VS-Very Sticky	
EFI-Extremely Firm	NP-Non-Plastic	
	SP-Slightly Plastic	
	P-Plastic	
	VP-Very Plastic	

Sketch of Soil Evaluation Locations

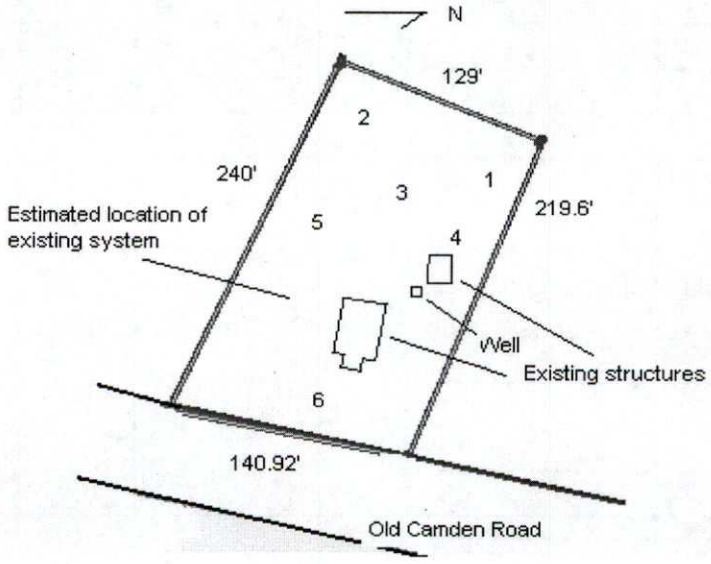

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St, Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

IMPROVEMENT PERMIT for a RESIDENTIAL ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

Permit #: **30002840** GWS File #: **7387B** Tax Parcel #: **139-161-08**

- This IMPROVEMENT PERMIT is subject to revocation if site plans or the intended use change. There is to be **NO** grading, filling, or disturbance of the soil in the area of the septic tank system or repair area.
- CONSTRUCTION AUTHORIZATION must be obtained prior to receiving a Building Permit. The Construction Authorization is **NOT** transferable. Do not clear, grade, fill or disturb soil prior to obtaining a Construction Authorization.
- Domestic-type wastewater only. No industrial process wastewater may be discharged into the system.

I. This Improvement Permit Shall: Expire in Five (5) Years **Expiration Date (If Applicable):** 12/7/2012

Type of Installation: Residential - New System Lot Number: 1

Structure Type: HOUSE Size (ft^2): 3000 # Bedrooms: 5 # Occupants: 3

Building Foundation: Crawl Space Water Supply: Community

II. Initial System Type: Innovative **System Classification:** IIIg

Initial System Specifications:

Design Flow (gpd):	600	LTAR (gpd/ft^2):	0.3	Septic Tank Size (gal):	1500	Pump Tank Size (gal):	N/A
Trench Width (ft):	3	Trench Spacing (ft):	9	Absorption Area (ft^2):	1500	Total Trench Length (ft):	500
Maximum Trench Depth (in):	30	Depth of Media (in):	N/A	Distribution Device:	Distribution Box		

III. Repair System Type: Pump to Innovative **System Classification:** IIIb

Repair System Specifications:

Design Flow (gpd):	600	LTAR (gpd/ft^2):	0.3	Septic Tank Size (gal):	1500	Pump Tank Size (gal):	N/A
Trench Width (ft):	3	Trench Spacing (ft):	9	Absorption Area (ft^2):	1500	Total Trench Length (ft):	500
Maximum Trench Depth (in):	30	Depth of Media (in):	N/A	Distribution Device:	Pressure Manifold		

IV. Permit Conditions/Comments:

(Please See the Following Page for Permit Conditions.)

The undersigned, an authorized agent of the MECKLENBURG COUNTY HEALTH DEPARTMENT, certifies that the Department is issuing an IMPROVEMENT PERMIT for the above referenced property. This permit is being issued in accordance with the *Laws and Rules For Sewage Treatment, and Disposal Systems* and is subject to the following provisions:

- No work shall be conducted on the septic system until an INSTALLATION APPROVAL is granted by the Department.
- The septic system installer shall be a registered septic contractor with Mecklenburg County Health Department.
- The permitted system shall be installed in accordance with the included PLOT PLAN.
- This IMPROVEMENT PERMIT is transferable.

DENR Authorized Agent: David Cornelius

Signature: _____

Date Issued: 12/7/2007

Owner/Legal Agent: Matthew Cohn

Print Name

Signature: Matthew Cohn

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St, Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

IMPROVEMENT PERMIT for a RESIDENTIAL ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

Permit #: **30002840** GWS File #: **7387B**

IV. Permit Conditions/Comments:

- Proper well abandonment is required prior to receiving an Installation Approval from our office to install the septic system.
- All components of the septic system must be installed in accordance with the required setbacks listed on the corresponding plot plan.
- All components of the septic system must be located at least 100 ft. (50 ft. minimum) from all private wells.

The undersigned, an authorized agent of the MECKLENBURG COUNTY HEALTH DEPARTMENT, certifies that the Department is issuing an IMPROVEMENT PERMIT for the above referenced property. This permit is being issued in accordance with the *Laws and Rules For Sewage Treatment and Disposal Systems* and is subject to the following provisions:

- No work shall be conducted on the septic system until an INSTALLATION APPROVAL is granted by the Department.
- The septic system installer shall be a registered septic contractor with Mecklenburg County Health Department.
- The permitted system shall be installed in accordance with the included PLOT PLAN.
- This IMPROVEMENT PERMIT is transferable.

DENR Authorized Agent: David Cornelius

Signature: _____

Date Issued: 12/7/2007

Owner/Legal Agent: Matthew Cohn
Print Name

Signature: Matthew Cohn

Page 2 of 2
