

4630 RIVER BLUFF CT

11322353

1/11/2008

duponbj

Groundwater and Wastewater Services File Imaging Project
May 2007
Barcode Font = IDAutomationHC39M

Groundwater & Wastewater Services
Septic Project File & Data Review Worksheet

LD

GWS File #: 6006B WASPS App #: 1737

Primary ES assigned to project: 4J

Secondary ES assigned to project:

Project Type: New System ☑ Alteration ☐ Repair ☐ Modified Plot Plan ☐

I. File Review:

Rule or Law				
	Permit Application			
.1937(d)	Is the Application complete	Yes ☑	No ☐	N/A ☐
.1937(d)	Is there a Site plan/Plat with application	Yes ☑	No ☐	N/A ☐
.1937(d)	Is the Facility shown?	Yes ☑	No ☐	N/A ☐
.1937(d)	Are appurtenances shown	Yes ☑	No ☐	N/A ☐
	Site Evaluation Information			
.1939 (a)(1)	Topography and Landscape Position Recorded?	Yes ☑	No ☐	N/A ☐
.1940 (a-g)	Slope % Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(2)	Texture Class Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(2)	Structure type Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(2)	Consistence Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(2)	Mineralogy Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(3)	Soil Wetness Condition Recorded?	Yes ☐	No ☐	N/A ☑
.1939 (a)(4)	Soil Depth to Rock or Parent Material Recorded When Encountered	Yes ☐	No ☐	N/A ☑
.1939 (a)(5)	Depth to Restrictive Horizons Recorded When Encountered?	Yes ☐	No ☐	N/A ☑
.1939 (a)(6)	Sufficient Available Space Recorded?	Yes ☐	No ☐	N/A ☐
.1937(m)	Are the Profile Locations Shown?			
.1939(a)	Are the S/PS Profiles in system & in repair area?	Yes ☑	No ☐	N/A ☐
& .1945(b)	Number of auger borings made: 4 Were sufficient auger borings made?	Yes ☑	No ☐	N/A ☐
.1939(d), .1955, .1956, .1957	LTAR .3	Yes ☑	No ☐	N/A ☐
	Improvement Permit/Construction Authorization			
.1937(g) 130A-336(a)	Proposed System Type stated-Initial	Yes ☑	No ☐	N/A ☐
.1945(b)	Proposed System Type stated-Repair	Yes ☑	No ☐	N/A ☐
130A-336 (a)(3)	System location identifiable by setbacks - Initial	Yes ☑	No ☐	N/A ☐
.1937(g) .1945(b)	System components shown – Initial	Yes ☑	No ☐	N/A ☐
.1945(b)	Repair area shown	Yes ☑	No ☐	N/A ☐
.1937 (f)(g)	Does System design match facility, flow & WWcharacteristics?	Yes ☑	No ☐	N/A ☐
.1937 (f)(g)	Is System design consistent with soil/site conditions?	Yes ☑	No ☐	N/A ☐
.1937 (f)(g)	Is the System located in the approved area?	Yes ☑	No ☐	N/A ☐
130A-336(a)	Is the Design flow (gpd) indicated?	Yes ☑	No ☐	N/A ☐

130A-336(a)	Number of Bedrooms, employees, seats, etc. indicated?	Yes ☑	No ☐	N/A ☐
.1937(g)	Trench depth indicated?	Yes ☑	No ☐	N/A ☐
.1937(g)	Trench width indicated?	Yes ☑	No ☐	N/A ☐
.1937(g)	Trench length indicated?	Yes ☑	No ☐	N/A ☐
130A-336(a)(1)	Proposed/existing well shown?	Yes ☐	No ☐	N/A ☑
130A-336(a)(1)	Property line lengths shown?	Yes ☑	No ☐	N/A ☐
130A-336(a)	Facility/appurtenance setbacks shown from fixed points?	Yes ☐	No ☐	N/A ☐
	Operation Permit			
.1937(i)	System type as described in table V(a) of rule .1961	Yes ☑	No ☐	N/A ☐
.1937(i)	Conditions for system performance, operation, maintenance, monitoring and reporting.	Yes ☑	No ☐	N/A ☐

II. WASPS Review:

Construction authorization issued	Yes ☐	No ☐	N/A ☐
Installation approval issued	Yes ☐	No ☐	N/A ☐
Operation permit issued	Yes ☐	No ☐	N/A ☐
Other related documentation	Yes ☐	No ☐	N/A ☐

Items requiring correction/modification: _____

Comments:

IA issued date: 3-1908

OP issued date: 4-1008

Review performed by: JR

Date performed: 12-07

#1737

GWS – RES. APP 07/05

SEPTIC FEE: 200.00
DATE: 12/15/06
CRT [ ] Ck # 3300

PERMIT APPLICATION FOR A RESIDENTIAL SITE IMPROVEMENT PERMIT / CONSTRUCTION AUTHORIZATION FOR ON-SITE WASTEWATER SYSTEM NEW WELL INSTALLATION OR REPAIR OF EXISTING WELL MECKLENBURG COUNTY GROUNDWATER & WASTEWATER SERVICES

WELL FEE: _____
DATE: _____
CRT [ ]

FILE # 6886B

SEPTIC / TYPE APPLICATION: ☐ NONE ☑ NEW SYSTEM ☐ ALTERATION ☐ REPAIR ☐ MODIFY PLOT PLAN

WELL / TYPE APPLICATION: ☐ NONE ☐ NEW WELL ☐ MAJOR REPAIR ☐ ABANDONMENT

JOB LOCATION INFORMATION:
TAX/PARCEL #: 113-223-53
STREET ADDRESS: 4630 River Bluff Ct.
CITY: Charlotte
STATE: NC ZIP:
SUBDIVISION OR MOBILE HOME PARK NAME:
LOT #: 43 River Walk Plantation
TOWNSHIP: parent 113-071-17

☑ 0-MECKLENBURG ☐ 4-PINEVILLE
☐ 1-CHARLOTTE ☐ 5-MATTHEWS
☐ 2-DAVIDSON ☐ 6-HUNTERSVILLE
☐ 3-CORNELIUS ☐ 7-MINT HILL

BUILDING INFORMATION:
TYPE OF BUILDING:
☐ SINGLE MOBILE HOME (S) ☐ MODULAR HOME (M)
☐ DOUBLE WIDE (D) ☐ MULTIPLE FAMILY (U)
☑ HOUSE (H) ☐ OTHER
HEATED SQUARE FOOTAGE: 3600 sq. 60'x60'
NUMBER OF BEDROOMS: 3
NUMBER OF OCCUPANTS: 2

FOUNDATION FOR RESIDENCE: opt.
☐ CONCRETE SLAB ☑ BASEMENT WITH PLUMBING
☑ CRAWLSPACE ☐ BASEMENT WITH NO PLUMBING

IF PLANNING TO EXPAND/ALTER THE EXISTING SYSTEM INDICATE THE FOLLOWING CHANGES:
NUMBER OF BEDROOMS TO BE ADDED: NUMBER OF ADDITIONAL OCCUPANTS IN THE RESIDENCE:
WILL THERE BE A HOME BUSINESS IN THE RESIDENCE? ☐ YES ☑ NO TYPE:

WATER SUPPLY:
☐ MUNICIPAL (M) ☐ PUBLIC (C) ☐ PRIVATE WELL (P) ☑ SHARED WELL (S) community well ☐ OTHER 'SPRINGS' (O)

PROPOSED USE OF WELL: ☐ N/A ☐ IRRIGATION ☐ POTABLE ☐ GEOTHERMAL ☑ OTHER Com. well

ARE ANY OF THE FOLLOWING LOCATED ON THE PROPERTY? IF SO, PLEASE SHOW LOCATION ON SITE PLAN/PLAT.

BURIED CABLES, LANDFILLS, STUMPHOLES	☐ YES	☑ NO	WELLS, SPRINGS, OR WATER LINES	☐ YES	☑ NO
EXISTING WASTEWATER SYSTEMS	☐ YES	☑ NO	DESIGNATED WETLANDS	☐ YES	☑ NO
EASEMENTS OR RIGHT-OF-WAYS	☐ YES	☑ NO	GRADING/SOIL REMOVAL PERFORMED	☐ YES	☑ NO

PROPERTY OWNER:
NAME: Vernon L. Wood
ADDRESS: 1374 Drexmore Ave.
CITY: Charlotte
STATE: NC ZIP: 28209
HOME PHONE: 704 523-2228 WORK PHONE:
MOBILE PHONE: FAX:

LEGAL AGENT FOR PROPERTY OWNER, IF APPLICABLE:
NAME: Tim Whittaker
ADDRESS: 1112 Queensgate St.
CITY: Gastonia
STATE: NC ZIP: 28054
HOME PHONE: 704 866-9540 WORK PHONE:
MOBILE PHONE: 704 830-4344 FAX:

WHAT DATE WAS THE PROPERTY ORIGINALLY DEEDED AND RECORDED? after 1983
WHAT IS THE ANTICIPATED CLOSING DATE FOR THIS PROPERTY? Jan. 07

*An Improvement Permit is subject to suspension or revocation if site plans or the intended use change or if information submitted in this application is falsified or changed. The undersigned, owner, or legal agent for the owner, of the property described above as the "Job Location" has read the foregoing application, acknowledges that the contents of same are true, and authorizes the Mecklenburg County Health Department to enter onto the property for the purpose of processing this request.

T. Whittaker 12/15/06
Owner's/Agent's Signature Date

NORTH CAROLINA DEPARTMENT OF
ENVIRONMENT & NATURAL RESOURCES DIVISION
OF ENVIRONMENTAL HEALTH ON-SITE
WASTEWATER SECTION

*A Well Permit is subject to suspension or revocation if site plans or the intended use change or if information submitted in this application is falsified or changed. The undersigned, owner, or legal agent for the owner, of the property described above as the "Job Location" has read the foregoing application, acknowledges that the contents of same are true, and authorizes the Mecklenburg County Health Department to enter onto the property for the purpose of processing this request.

Owner's/Agent's Signature Date

MECKLENBURG COUNTY HEALTH DEPARTMENT
GROUNDWATER & WASTEWATER SERVICES
700 N. TRYON ST., SUITE 211
CHARLOTTE, NC 28202 704-336-5103 / FAX: 704-336-6894

(check 3300)

Mecklenburg County, North Carolina


POLARIS

Property Ownership Land Records Information System

Date Printed: Sat Nov 25 13:49:59 EST 2006

M.C.H.D.
File:
Lot 43

4630 River Bluff Court, River Walk Plantation

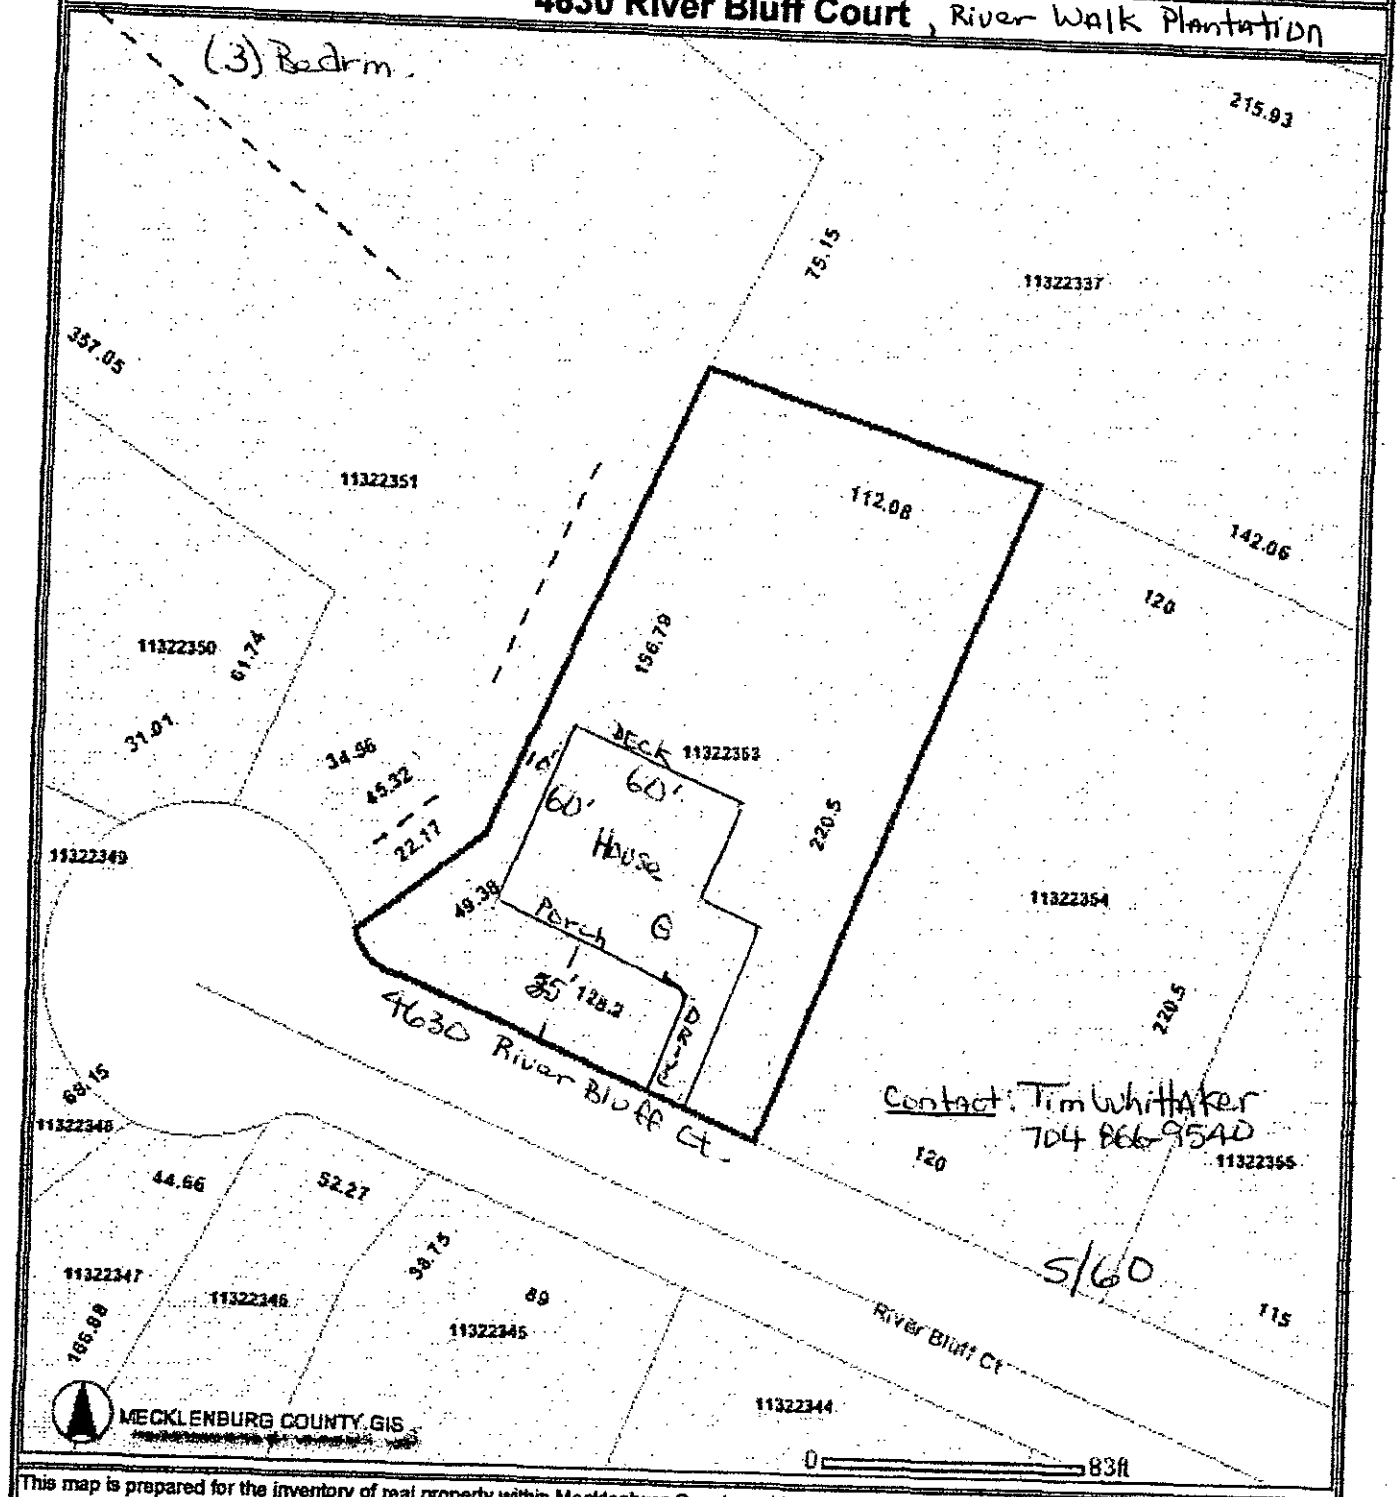

This map is prepared for the inventory of real property within Mecklenburg County and is compiled from recorded deeds, plats, tax maps, surveys, planimetric maps, and other public records and data. Users of this map are hereby notified that the aforementioned public primary information sources should be consulted for verification. Mecklenburg County and its mapping contractors assume no legal responsibility for the information contained herein.

PARCEL ID 113-223-52

Department of Environment, Health, and Natural Resources
Division of Environmental Health
On-site Wastewater Section

Sheet: 1 of 2
Property ID: 113-223-53
Lot #: 43
File #: 6886B
AppID: 1737
Code: 2

SOIL/SITE EVALUATION
for ON-SITE WASTEWATER SYSTEM

Owner: Vernon L. Wood
Applicant: Tim Whittaker
Address: 1374 Drexmore Ave., Charlotte, N. C. 28209
Date Evaluated: 12/20/06
Proposed Facility: Residence
Design Flow (.1949): 360gpd
Property Size: .57a
Location of Site: 4630 river Bluff Ct.
Property Recorded:
Water Supply: [ ] Public [ ] Individual [ ] Well [ ] Spring [x] Other shared
Evaluation Method: [x] Auger Boring [ ] Pit [ ] Cut
Type of Wastewater: [x] Sewage [ ] Industrial Process [ ] Mixed

PROFILE #	.1940 Landscape Position/ Slope%	Horizon Depth (IN.)	SOIL MORPHOLOGY .1941 .1941 Structure/ Texture	.1941 Consistence Mineralogy	b PROFILE FACTORS .1942 Soil Wetness/ Color	.1943 Soil Depth (IN.)	.1956 Sapro Class	.1944 Restr Horiz	Profile Class & LTAR
1	LS, 40%	0-6	GR/CL	FR/SEXP/SS/SP	>49" TO SOIL WETNESS	49	N/A	NONE	US, IV
		6-36	SBK/C	FI/SEXP/S/P					.3GPD/FT^2
		36-49	SBK/CL	FR/SEXP/SS/SP					
2	LS, 37%	0-7	GR/CL	"	>45" TO SOIL WETNESS	45	"	"	"
		7-45	SBK/C	FI/SEXP/S/P					
3	LS, 18%	0-7	GR/CL	FR/SEXP/SS/SP	>48" TO SOIL WETNESS	48	"	"	"
		7-48	SBK/C	FI/SEXP/S/P					
4	LS, 12%	0-6	GR/CL	FR/SEXP/SS/SP	"	"	"	"	"
		6-48	SBK/C	FI/SEXP/S/P					

Description	Initial System	Repair System
Available Space (.1945)	PS	RS
System Type(s)	Trench	Trench
Site LTAR	.3GPD/FT^2	.3GPD/FT^2


Other Factors (.1946):
Site Classification (.1948): ~~UNSUITABLE~~ PREV. SUITABLE
Evaluated By: W. R. Martin, LSS, 12/22/06, W. R. Martin
Others Present:

COMMENTS:
100% repair

Landscape Position	Group	Texture	.1955 LTAR	Structure
R-Ridge	I	S-Sand	1.2 - 0.8	SG-Single Grain
SS-Shoulder Slope		LS-Loamy Sand		M-Massive
LS-Linear Slope				CR-Crumb
FS-Foot Slope	II	SL-Sandy Loam	0.8 - 0.6	GR-Granular
NS-Nose Slope		L-Loam		SBK-Subangular Blocky
HS-Head Slope				ABK-Angular Blocky
CC-Concave Slope	III	SI-Silt	0.6 - 0.3	PL-Platy
CV-Convex Slope		SICL-Silty Clay Loam		PR-Prismatic
T-Terrace				
FP-Flood Plain		CL-Clay Loam		
		SCL-Sandy Clay Loam		
	IV	SC-Sandy Clay	0.4 - 0.1	
		SIC-Silty Clay		
		C-Clay		

Consistence Moist	Consistence Wet	Mineralogy
VFR-Very Friable	NS-Non-Sticky	SEXP-Slightly Expansive
FR-Friable	SS-Slightly Sticky	EXP-Expansive
FI-Firm	S-Sticky	
VFI-Very Firm	VS-Very Sticky	
EFI-Extremely Firm	NP-Non-Plastic	
	SP-Slightly Plastic	
	P-Plastic	
	VP-Very Plastic	

Sketch of Soil Evaluation Locations

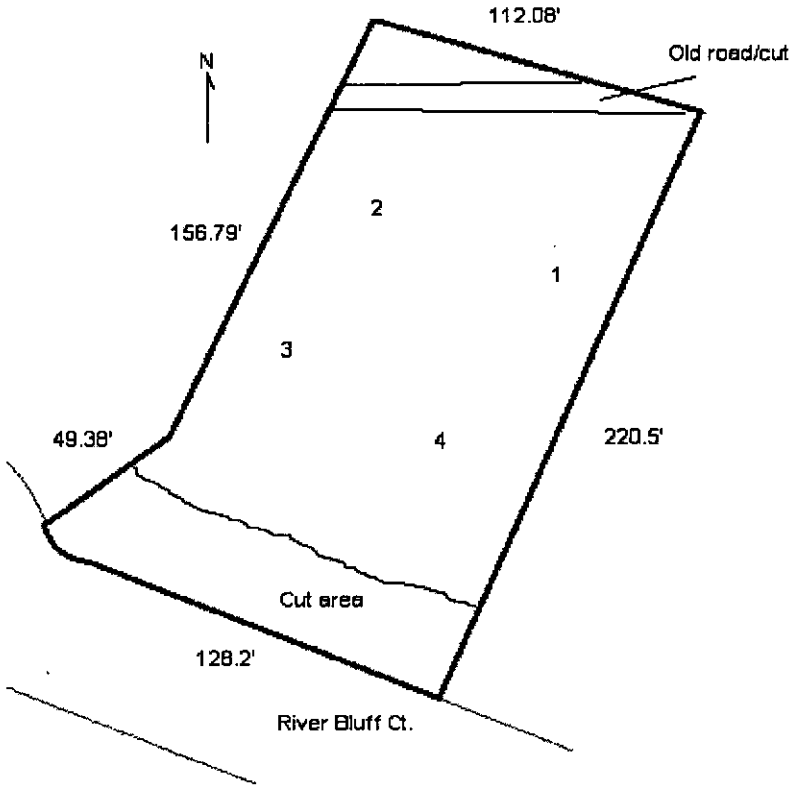


COMMENTS:
100% repair

Landscape Position	Group	Texture	.1955 LTAR	Structure
R-Ridge	I	S-Sand	1.2 - 0.8	SG-Single Grain
SS-Shoulder Slope		LS-Loamy Sand		M-Massive
LS-Linear Slope				CR-Crumb
FS-Foot Slope	II	SL-Sandy Loam	0.8 - 0.6	GR-Granular
NS-Nose Slope		L-Loam		SBK-Subangular Blocky
HS-Head Slope				ABK-Angular Blocky
CC-Concave Slope	III	SI-Silt	0.6 - 0.3	PL-Platy
CV-Convex Slope		SICL-Silty Clay Loam		PR-Prismatic
T-Terrace		CL-Clay Loam		
FP-Flood Plain		SCL-Sandy Clay Loam		
	IV	SC-Sandy Clay	0.4 - 0.1	
		SIC-Silty Clay		
		C-Clay		

Consistence Moist	Consistence Wet	Mineralogy
VFR-Very Friable	NS-Non-Sticky	SEXP-Slightly Expansive
FR-Friable	SS-Slightly Sticky	EXP-Expansive
FI-Firm	S-Sticky	
VFI-Very Firm	VS-Very Sticky	
EFI-Extremely Firm	NP-Non-Plastic	
	SP-Slightly Plastic	
	P-Plastic	
	VP-Very Plastic	

Sketch of Soil Evaluation Locations

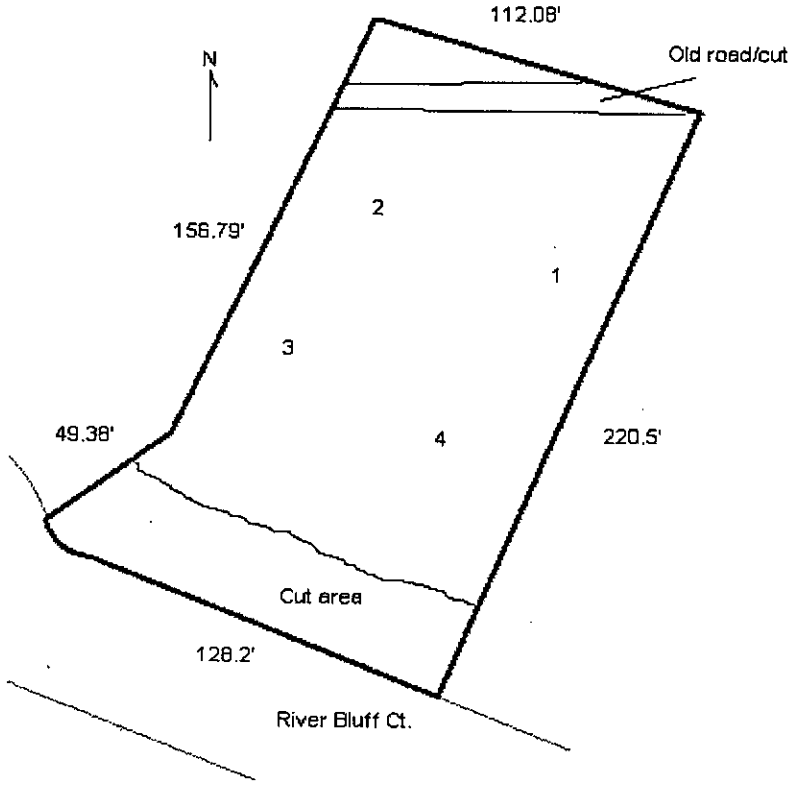

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St, Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

IMPROVEMENT PERMIT for a RESIDENTIAL ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

Permit #: **30001737** GWS File #: **6886B** Tax Parcel #: **113-223-53**

- This IMPROVEMENT PERMIT is subject to revocation if site plans or the intended use change. There is to be **NO** grading, filling, or disturbance of the soil in the area of the septic tank system or repair area.
- CONSTRUCTION AUTHORIZATION must be obtained prior to receiving a Building Permit. The Construction Authorization is **NOT** transferable. Do not clear, grade, fill or disturb soil prior to obtaining a Construction Authorization.
- Domestic-type wastewater only. No industrial process wastewater may be discharged into the system.

I. This Improvement Permit Shall: Expire in Five (5) Years **Expiration Date (If Applicable):** 1/17/2012

Type of Installation: Residential - New System Lot Number: 43

Structure Type: HOUSE Size (ft^2): 3600 # Bedrooms: 3 # Occupants: 2

Building Foundation: Crawl Space Water Supply: Community

II. Initial System Type: Approved Accepted **System Classification:** IIIg

Initial System Specifications:

Design Flow (gpd):	360	LTAR (gpd/ft^2):	0.3	Septic Tank Size (gal):	1500	Pump Tank Size (gal):	N/A
Trench Width (ft):	3	Trench Spacing (ft):	9	Absorption Area (ft^2):	900	Total Trench Length (ft):	300
Maximum Trench Depth (in):	~~36~~ 33	Depth of Media (in):	12	Distribution Device:	Drop Boxes		

III. Repair System Type: PPBPS (pressurized) **System Classification:** IVa

Repair System Specifications:

Design Flow (gpd):	360	LTAR (gpd/ft^2):	0.3	Septic Tank Size (gal):	1500	Pump Tank Size (gal):	N/A
Trench Width (ft):	3	Trench Spacing (ft):	9	Absorption Area (ft^2):	801	Total Trench Length (ft):	200
Maximum Trench Depth (in):	~~36~~ 33	Depth of Media (in):	24	Distribution Device:	Manifold (LPP Distri		

IV. Permit Conditions/Comments:

(Please See the Following Page for Permit Conditions.)

The undersigned, an authorized agent of the MECKLENBURG COUNTY HEALTH DEPARTMENT, certifies that the Department is issuing an IMPROVEMENT PERMIT for the above referenced property. This permit is being issued in accordance with the *Laws and Rules For Sewage Treatment, and Disposal Systems* and is subject to the following provisions:

- No work shall be conducted on the septic system until an INSTALLATION APPROVAL is granted by the Department.
- The septic system installer shall be a registered septic contractor with Mecklenburg County Health Department.
- The permitted system shall be installed in accordance with the included PLOT PLAN.
- This IMPROVEMENT PERMIT is transferable.

DENR Authorized Agent: Jeremy Michael Owner/Legal Agent: Tim Whittaker
Print Name

Signature: Jeremy Michael Signature: Tim Whittaker

Date Issued: 1/17/2007

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St, Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

IMPROVEMENT PERMIT for a RESIDENTIAL
ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

Permit #: **30001737** GWS File #: **6886B**

IV. Permit Conditions/Comments:

- The septic system shall be installed in accordance with the plans submitted by the wastewater system design consultant.
- All components of the septic system must be installed in accordance with the required setbacks listed on the corresponding plot plan.

The undersigned, an authorized agent of the MECKLENBURG COUNTY HEALTH DEPARTMENT, *certifies that* the Department is issuing an IMPROVEMENT PERMIT for the above referenced property. This permit is being issued in accordance with the *Laws and Rules For Sewage Treatment and Disposal Systems* and is subject to the following provisions:

- No work shall be conducted on the septic system until an INSTALLATION APPROVAL is granted by the Department.
- The septic system installer shall be a registered septic contractor with Mecklenburg County Health Department.
- The permitted system shall be installed in accordance with the included PLOT PLAN.
- This IMPROVEMENT PERMIT is transferable.

DENR Authorized Agent: Jeremy Michael

Signature: Jeremy J Michael

Date Issued: 1/17/2007


Owner/Legal Agent: Tim Whitaker
Print Name

Signature: Tim Whitaker

M.C.H.D.
File: 6886-B
Lot 43 River Walk Plantation
113-223-33

(3) Bedrm. EASY Flow Chamber Septic System.
Panel Block Repair Sys.

Primary Septic System: 300' EASY Flow Chambers
(See SPEC Sheet)

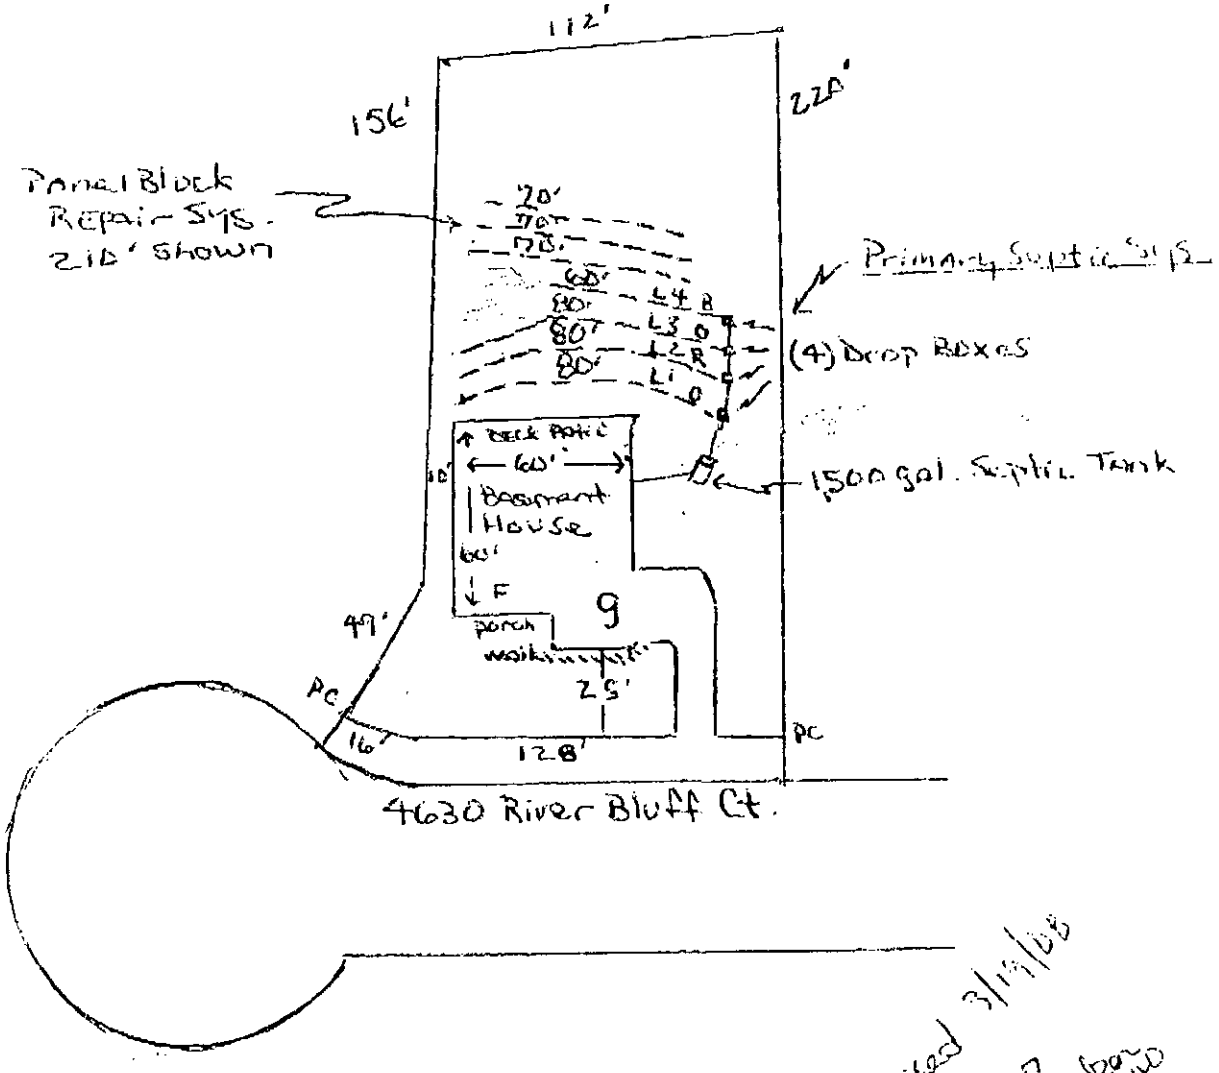

Revised 3/19/08
12/5/07
Witnessed by
704 [illegible]
S/ED

MCHD.
File: 6886-B
Lot 93 Riverwalk Plantation


(3) Bedrm. (Easy flow chamber) 25% Reduction Sys.

SPECS:
1,500 gal. Septic Tank - filter / Riser
Distribution Box - 1
(4) Drop Boxes

Drainfield:

L^1 =	80',	8 chambers
L^2 =	80',	8 chambers
L^3 =	80'	8 chambers
L^4 =	60'	6 chambers
Totals	300'	30 chambers

* Starting Points for Drainfield: (pulled from Edge of Rd.)
Primary Septic Sys:
* Install sys. on grade & contour per manufactured SPECS.

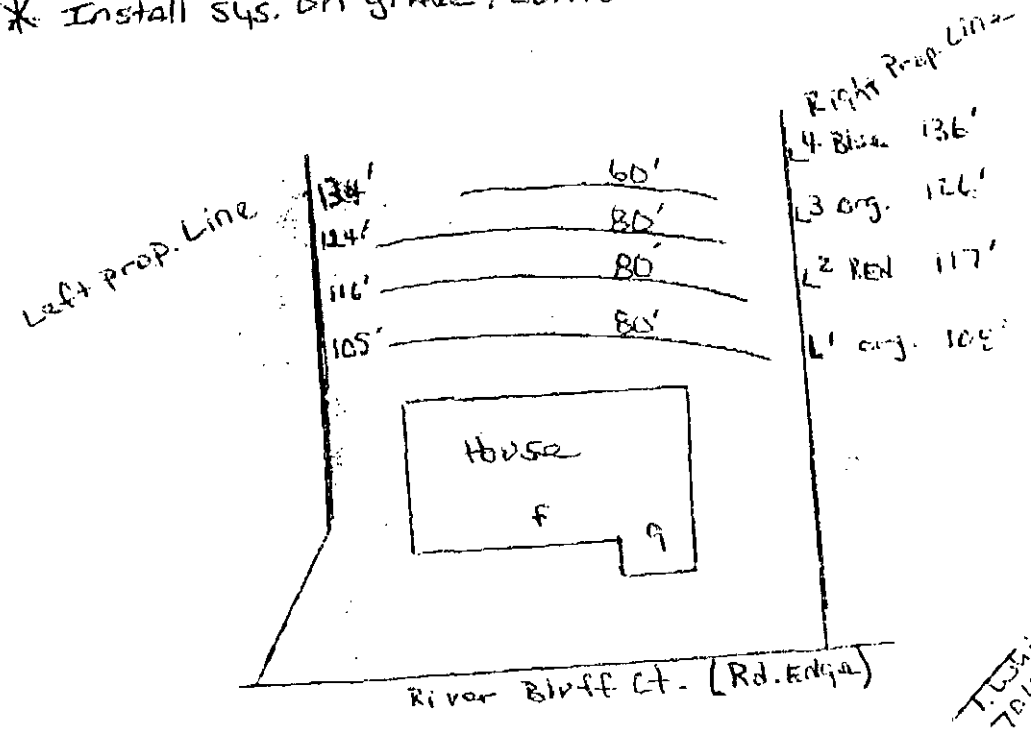

T. Whittaker
704 882-9540
not sealed

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St., Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

INSTALLATION APPROVAL for an
ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

File #: 6886B Permit #: _____ Tax Parcel #: 113-223-53

Property Owner: VERNON L. WOOD

Job Location Address: 4630 RIVER BLUFF CT. (LOT # 43)

City: CHARLOTTE State: NC Zip Code: 28214

Installation Approval Issuance Date: 3/19/08

Permission is hereby given to ☑ install ☐ alter ☐ repair an on-site wastewater treatment & and disposal system, with subsurface soil absorption and effluent discharge, as specified herein at the described location. This approval is granted based upon the application information submitted to our office. All work shall be completed on or before 4/21/08, after which date this approval shall be null and void. The system shall meet all of the construction requirements of 15A NCAC 18A. 1900 which are in effect on the date of granting this approval. An ***Operation Permit*** must be obtained from the Mecklenburg County Health Department before any system can be covered up or placed into service. The issuance of this permit does not in any way guarantee that the system anticipated to be constructed will operate properly, or relieve any person now of hereafter owning, controlling or using such system from any liability resulting from the failure of the system to operate properly.

***NOTICE: This system shall not be installed while soils are in a wet condition.**

Permitted Design Flow: 360 GPD

Site LTAR: .3 GPD/ft² *(For new installations only.)*

Liquid Capacity of Septic Tank: 1500 gallons

Liquid Capacity of Dosing Tank: — gallons

Drainfield Design ☐ N/A

Trench Depth: 33 inches

Trench Width: 3 feet

Line Spacing: 9 feet (O.C.)

Total line length: 300 feet

# of Lines: 4 @ VAR feet

Depth of Media: 12 inches (Type) INNOVATIVE

Distribution Device: DROP BOXES

Bed Design *(For Repair Installations ONLY.)* ☑ N/A

Bed Depth: _____ inches

Bed Width: _____ feet

Total line length: _____ feet

# of Lines: _____ @ _____ feet

Depth of Media: _____ inches (Type) _____

Distribution Device: _____

Water Supply Source

☐ Municipal ☐ Private Well ☑ Community Well

☐ Other _____

Minimum System Setbacks

Distance from Building Foundation: 10 feet

Distance from Property Line: 10 feet

Distance from Water Supply Source: 10 feet

SKETCH OF SYSTEM LAYOUT
(Proposed Layout)

* INSTALL IN ACCORDANCE WITH PLANS SUBMITTED BY TIM WHITTAKER, WASTEWATER CONSULTANT.

Comments: System Classification & Type: IIIg

DENR Authorized Agent: Chris Sherrill, RS, LSS Signature: Chris Sherrill

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St., Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

OPERATION PERMIT for an
ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

File #: 6886 B Permit #: _____ Tax Parcel #: 113-223-53

Property Owner: VERNON L. WOOD

Job Location Address: 4630 RIVER BLUFF CT (LOT #43)

City: CHARLOTTE State: NC Zip Code: 28214

Operation Permit Issuance Date: 4/18/08 Contractor Name: TRENT RHEA

Permitted Design Flow: 360 GPD
Liquid Capacity of Septic Tank: 1500 gallons
Liquid Capacity of Dosing Tank: — gallons
Effluent Pump Model: —

Drainfield Installation ☐ N/A
Trench Depth: 33 inches
Trench Width: 3 feet
Line Spacing: 9 feet (O.C.)
Total line length: 300 feet
# of Lines: 4 @ VAR feet
Depth of Media: 12 inches (Type) EZFLOW
Depth of Cover: 21 inches
Distribution Device: DROP BOXES


Inspection Dates
Tank(s) Inspected: 4/18/08
Excavation Inspected: 4/18/08
Pump & Controls Inspected: _____

Bed Installation *(For Repair Installations ONLY.)* ☑ N/A
Bed Depth: _____ inches
Bed Width: _____ feet
Total line length: _____ feet
# of Lines: _____ @ _____ feet
Depth of Media: _____ inches (Type) _____
Depth of Cover: _____ inches
Distribution Device: _____

Water Supply Source
☐ Municipal ☐ Private Well ☑ Community Well
☐ Other _____

System Installation Setbacks
Distance from Building Foundation: 10 feet
Distance from Property Line: 10 feet
Distance from Water Supply Source: 10 feet

SKETCH OF SYSTEM INSTALLATION
(As-Built Drawing)

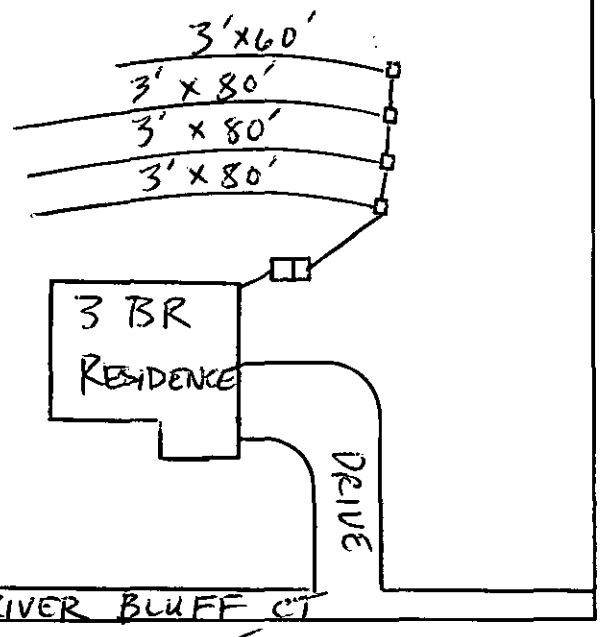

The undersigned has inspected the Septic Tank System described above, and certifies it has been ☑ installed ☐ altered ☐ repaired ☑ as detailed in the plot above ☐ in accordance with the permit issued and meets the provisions of 15A NCAC 18A. 1900, "Laws and Rules for Sewage Treatment and Disposal Systems" in effect on the date of issuance of the permit. The issuance of this Operation Permit does not in any way guarantee that the system will operate properly or relieve any person now or hereafter owning, controlling, or using such system from any liability resulting from the failure of the system to operate properly. This document is issued subject to those restrictions and conditions shown on the permit(s) and the provisions of 15A NCAC 18A. 1900 in addition to those listed below under "Comments." This document shall be null and void if any information contained in the application is untrue or if any additions are made to the property which would increase the requirements for said system.

Notice: Disturbance of the designated repair area may result in the Suspension or Revocation of this permit.

Comments: System Classification & Type: IIIg, EZ 1203H, G, NA, NA

DENR Authorized Agent: Chris Sherrill, RS, LSS Signature: Chris Sherrill

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St., Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

OPERATION PERMIT for an
ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

File #: 6886B Permit #: _____ Tax Parcel #: 113-223-53

Property Owner: VERNON L. WOOD

Job Location Address: 4630 RIVER BLUFF CT. (LOT # 43)

City: CHARLOTTE State: NC Zip Code: 28214

OPERATION PERMIT CONDITIONS:

I. Performance: System shall perform in accordance with 15A NCAC 18A .1961.

II. Monitoring: System shall be monitored as required by 15A NCAC 18A .1961.

III. Maintenance: Ground absorption sewage treatment and disposal systems shall be checked, and the contents of the septic tank removed, periodically from all compartments, to ensure proper operation of the system. The contents shall be pumped whenever the solids level is found to be more than 1/3 of the liquid depth in any compartment.

IV. Operation: System shall be operated in accordance with 15A NCAC 18A .1961.

System Classification: IIIg

*Operation Permits for Type V and VI systems expire five (5) years from the date of issuance (in accordance with Table V(a)). The system owner must contact GWS six (6) months prior to expiration for permit renewal.

Subsurface system operator required: Yes ☐ No ☑

☐ This type of system requires the system owner to maintain a contract with a certified operator to perform system inspection, maintenance, and reporting as required in 15A NCAC 18A .1961. and Table V(a). The system owner is responsible for all fees associated with these services.

☑ System does not require inspection by GWS on a routine frequency.

☐ System requires inspection by GWS once every five (5) years. The system owner is responsible for all fees associated with the inspection.

☐ System requires inspection by GWS once every three (3) years. The system owner is responsible for all fees associated with the inspection.

☐ System requires inspection by GWS once every twelve (12) months. The system owner is responsible for all fees associated with the inspection.

☐ System requires inspection by GWS once every six (6) months. The system owner is responsible for all fees associated with the inspection.

V. Other:

_____

_____

_____

_____

DENR Authorized Agent: Chris Sherrill, RS, LSS Date: 4/18/08

Signature: Christopher M Sherrill

FEE: 300.00

DATE: 12/13/2007

CONSTRUCTION AUTHORIZATION FOR AN ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

MECKLENBURG COUNTY

GROUNDWATER & WASTEWATER SERVICES

FILE NUMBER: 6886B

PERMIT NUMBER: 30001737

PARCEL NUMBER: 11322353

JOB LOCATION INFORMATION

ADDRESS: 4630 RIVER BLUFF CT

CITY: CHARLOTTE **STATE: NC** **ZIP:** 28214

ISSUED TO: Vernon L. Wood

CONSTRUCTION AUTHORIZATION ISSUANCE DATE: 12/13/2007

CONSTRUCTION AUTHORIZATION CONDITIONS

1. WASTEWATER SYSTEM CONSTRUCTION AND INSTALLATION MUST MEET ALL CONDITIONS AND SPECIFICATIONS AS SET FORTH IN IMPROVEMENT PERMIT NUMBER 30001737, AND THE ATTACHED SITE PLAN WITH SYSTEM DETAILS. CONSTRUCTION AND INSTALLATION MUST ALSO MEET ALL REQUIREMENTS SET FORTH IN THE RULES GOVERNING SANITARY SEWAGE COLLECTION, TREATMENT, AND DISPOSAL AND ANY OTHER APPLICABLE RULES AND LAWS.

2. AN INSTALLATION APPROVAL MUST BE SECURED PRIOR TO INSTALLATION OF THE SEPTIC TANK SYSTEM. THE INSTALLER OF THE SYSTEM SHALL BE A REGISTERED SEPTIC TANK CONTRACTOR WITH THE MECKLENBURG COUNTY HEALTH DEPARTMENT.

3. ANY ALTERATION IN SITE OR SOIL CONDITIONS (INCLUDING LOCATION OF STRUCTURES AND APPURTENANCES) OR MODIFICATION IN USE, DESIGN WASTEWATER FLOW, OR WASTEWATER CHARACTERISTICS AS SPECIFIED IN THE ASSOCIATED IMPROVEMENT PERMIT AND APPLICATION, MAY SUBJECT THIS CONSTRUCTION AUTHORIZATION AND ASSOCIATED PERMIT(S) TO REVOCATION.

4. THIS CONSTRUCTION AUTHORIZATION AS PROVIDED IN G.S. 130A-335(f) AND G.S. 130A-336(b) SHALL BE VALID FOR A PERIOD EQUAL TO THE VALIDITY OF THE IMPROVEMENT PERMIT, NOT TO EXCEED 60 MONTHS.
   *CONSTRUCTION AUTHORIZATION EXPIRATION DATE: 1/17/2012

MECKLENBURG COUNTY
LAND USE AND ENVIRONMENTAL SERVICES
Payment Receipt

Receipt Information

Date:	12/07/07	**Amount:**	150.00
Receipt #:	54030	**Tendered:**	150.00
Check / Auth #:	VISA 011032	**Returned:**	0.00
Received By:	GLADNAG		

Account Information

Account #: 200000
Contractor: WOOD VERNON L.
Attn:
Address: 1374 DREXMORE AV
Address:
City/State/Zip: CHARLOTTE, NC 28209

Item	Description	Permit#	Quantity	Unit Price	Total Price
0734	Auth for Waste Wtr Sys Constr 4630 RIVER BLUFF CT		1	150.00	150.00

----------Outstanding Balances----------

Month-To-Date	Prior Month	30 Days	60 Days	90 Days	Balance

MECKLENBURG COUNTY
LAND USE AND ENVIRONMENTAL SERVICES
Payment Receipt

Receipt Information

Date:	12/07/07	**Amount:**	150.00
Receipt #:	54031	**Tendered:**	0.00
Check / Auth #:	VISA 011032	**Returned:**	-150.00
Received By:	GLADNAG		

Account Information

Account #: 200000
Contractor: WOOD VERNON L.
Attn:
Address: 1374 DREXMORE AV
Address:
City/State/Zip: CHARLOTTE, NC 28209

Item	Description	Permit#	Quantity	Unit Price	Total Price
0703	Installation/Final Approval 4630 RIVER BLUFF CT		1	150.00	150.00

----------Outstanding Balances----------

Month-To-Date	Prior Month	30 Days	60 Days	90 Days	Balance

File #: 6886B
Date: 4/21/08
Inspected By: CMS

Final Inspection Check List

Septic Tank

Tank construction PCC

Septic tank installed in correct orientation and is level? Yes ☑ No ☐

Septic tank is in good condition with no visible defects or leaks? Yes ☑ No ☐

Septic tank stamped with appropriate markings? Yes ☑ No ☐

Id Number: STB-379 Date: 11/11/07 Size: 1500 Gallons

Lids present and in good condition? Yes ☑ No ☐

Tank air vent unobstructed? Yes ☑ No ☐

Baffle wall with 4" opening unobstructed? Yes ☑ No ☐

Effluent filter installed correctly in tank? Yes ☑ No ☐

Outlet pipe has a watertight seal with cast in place boot and clamp? Yes ☑ No ☐

1/8" per ft. of fall on outlet pipe? Yes ☑ No ☐

Risers used appropriately if required? Yes ☑ No ☐

Pump Tank (If Applicable)

Pump tank installed with riser above grade and is level? Yes ☐ No ☐

Pump tank is in good condition with no visible defects or leaks? Yes ☐ No ☐

Inlet pipe properly sealed/grouted? Yes ☐ No ☐

Discharge pipe properly sealed/grouted? Yes ☐ No ☐

Pump tank stamped with appropriate markings? Yes ☐ No ☐

Id Number: _____ Date: _____ Size: _____ Gallons

Lids present and in good condition? Yes ☐ No ☐

Pump installed in tank? Yes ☐ No ☐

Pump Make _____ Model _____

Control floats installed correctly? Yes ☐ No ☐

Check valve installed correctly? Yes ☐ No ☐

Gate valve installed on discharge piping? Yes ☐ No ☐

Discharge pipe size? _____ in.

Nema 4X control panel used? Yes ☐ No ☐

Electrical conduits sealed from gas entry? Yes ☐ No ☐

Distribution Box (If Applicable)

1/8" per ft. of fall on inlet pipe? Yes ☐ No ☐

Distribution box installed at least 2' from septic tank? Yes ☐ No ☐

Distance from tank outlet _____ ft.

Distribution box and lid in good condition? Yes ☐ No ☐

D-box level and stable? Yes ☐ No ☐

Inlet and outlet/s properly sealed and watertight? Yes ☐ No ☐

Speed levels present and adjusted properly? Yes ☐ No ☐

Pressure Manifold (If Applicable)

Manifold material, Schedule _____ PVC

Manifold diameter _____ in.

Size of taps _____ in. / Number of taps _____

Shutoff valves provided for each tap? Yes ☐ No ☐

Cleanout installed and accessible? Yes ☐ No ☐

Access provided to set head pressure? Yes ☐ No ☐

Gate valve installed to regulate flow through manifold? Yes ☐ No ☐

Location of valve: _____

Manifold housed in appropriate enclosure? Yes ☐ No ☐

Manifold installed level and secured to enclosure? Yes ☐ No ☐

Pressure head set to _____ ft.

Drainfield (Conventional)

Number of lines installed _____

Total length of drainline installed _____ft.

Trench width _____ft.

Trench spacing O.C. _____ft.

Trench depth _____in.

Tire Chips Used? Yes ☐ No ☐

Geotextile fabric in place? Yes ☐ No ☐

Depth of stone / tire chips _____in.

Distance from house _____ft.

Distance from property lines: Left _____ft. Right _____ft. Front _____ ft. Rear _____ft.

Distance from well _____ft.

Drainlines installed level and on contour? Yes ☐ No ☐

Drainfield (Innovative 25% Reduction)

Number of lines installed 4

Total length of drainline installed 300 ft.

Trench width 3 ft.

Trench spacing O.C. 9 ft.

Trench depth 33 in.

Protective barrier installed over polystyrene? Yes ☑ No ☐

Distance from house 10 ft.

Distance from property lines: Left 10+ ft. Right 10+ ft. Front 10+ ft. Rear 10+ ft.

Distance from well N/A ft.

Drainlines installed level and on contour? Yes ☑ No ☐

Drainfield (PPBPS 50% Reduction)

Number of lines installed _____

Total length of drainline installed _____ft.

Trench width _____ft.

Trench spacing O.C. _____ft.

Trench depth _____in.

6" sand bed on trench bottom? Yes ☐ No ☐

Correct type & amount of sand installed inside panels? Yes ☐ No ☐

Distance from house _____ft.

Distance from property lines: Left _____ft. Right _____ft. Front ____ ft. Rear _____ft.

Distance from well _____ft.

Drainlines installed level and on contour? Yes ☐ No ☐

Grade Shots with Level

Trench #: 1

Shot #	Reading
1	9.25
2	"
3	"

Trench #: 2

Shot #	Reading
1	11.3
2	"
3	"

Trench #: 3

Shot #	Reading
1	14.7
2	"
3	"

Trench #: 4

Shot #	Reading
1	10.6
2	"
3	"

*MOVED LASER

Trench #: ___

Shot #	Reading

Trench #: ___

Shot #	Reading

Trench #: ___

Shot #	Reading

Trench #: ___

Shot #	Reading

Trench #: ___

Shot #	Reading

Trench #: ___

Shot #	Reading
