

3513 GREY RD

1/11/2008

duponbj

Groundwater and Wastewater Services File Imaging Project
May 2007
Barcode Font = IDAutomationHC39M

Groundwater & Wastewater Services
Septic Project File & Data Review Worksheet

GWS File #: 7206B WASPS App #: 2426

Primary ES assigned to project: BW

Secondary ES assigned to project:

Project Type: New System ☑ Alteration ☐ Repair ☐ Modified Plot Plan ☐

I. File Review:

Rule or Law				
	Permit Application			
.1937(d)	Is the Application complete	Yes ☑	No ☐	N/A ☐
.1937(d)	Is there a Site plan/Plat with application	Yes ☑	No ☐	N/A ☐
.1937(d)	Is the Facility shown?	Yes ☑	No ☐	N/A ☐
.1937(d)	Are appurtenances shown	Yes ☑	No ☐	N/A ☐
	Site Evaluation Information			
.1939 (a)(1)	Topography and Landscape Position Recorded?	Yes ☑	No ☐	N/A ☐
.1940 (a-g)	Slope % Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(2)	Texture Class Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(2)	Structure type Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(2)	Consistence Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(2)	Mineralogy Recorded?	Yes ☑	No ☐	N/A ☐
.1939 (a)(3)	Soil Wetness Condition Recorded?	Yes ☐	No ☐	N/A ☑
.1939 (a)(4)	Soil Depth to Rock or Parent Material Recorded When Encountered	Yes ☐	No ☐	N/A ☑
.1939 (a)(5)	Depth to Restrictive Horizons Recorded When Encountered?	Yes ☐	No ☐	N/A ☑
.1939 (a)(6)	Sufficient Available Space Recorded?	Yes ☑	No ☐	N/A ☐
.1937(m)	Are the Profile Locations Shown?			
.1939(a)	Are the S/PS Profiles in system & in repair area?	Yes ☑	No ☐	N/A ☐
& .1945(b)	Number of auger borings made: 3 Were sufficient auger borings made?	Yes ☑	No ☐	N/A ☐
.1939(d), .1955, .1956, .1957	LTAR .275	Yes ☑	No ☐	N/A ☐
	Improvement Permit/Construction Authorization			
.1937(g) 130A-336(a)	Proposed System Type stated-Initial	Yes ☑	No ☐	N/A ☐
.1945(b)	Proposed System Type stated-Repair	Yes ☑	No ☐	N/A ☐
130A-336 (a)(3)	System location identifiable by setbacks - Initial	Yes ☑	No ☑	N/A ☐
.1937(g) .1945(b)	System components shown – Initial	Yes ☐	No ☑	N/A ☐
.1945(b)	Repair area shown	Yes ☑	No ☐	N/A ☐
.1937 (f)(g)	Does System design match facility, flow & WWcharacteristics?	Yes ☑	No ☐	N/A ☐
.1937 (f)(g)	Is System design consistent with soil/site conditions?	Yes ☑	No ☐	N/A ☐
.1937 (f)(g)	Is the System located in the approved area?	Yes ☑	No ☐	N/A ☐
130A-336(a)	Is the Design flow (gpd) indicated?	Yes ☑	No ☐	N/A ☐

130A-336(a)	Number of Bedrooms, employees, seats, etc. indicated?	Yes ☑	No ☐	N/A ☐
.1937(g)	Trench depth indicated?	Yes ☑	No ☐	N/A ☐
.1937(g)	Trench width indicated?	Yes ☑	No ☐	N/A ☐
.1937(g)	Trench length indicated?	Yes ☑	No ☐	N/A ☐
130A-336(a)(1)	Proposed/existing well shown?	Yes ☑	No ☐	N/A ☐
130A-336(a)(1)	Property line lengths shown?	Yes ☐	No ☑	N/A ☐
130A-336(a)	Facility/appurtenance setbacks shown from fixed points?	Yes ☐	No ☑	N/A ☐
	Operation Permit			
.1937(i)	System type as described in table V(a) of rule .1961	Yes ☐	No ☐	N/A ☐
.1937(i)	Conditions for system performance, operation, maintenance, monitoring and reporting.	Yes ☐	No ☐	N/A ☐

II. WASPS Review:

Construction authorization issued	Yes ☐	No ☐	N/A ☐
Installation approval issued	Yes ☐	No ☐	N/A ☐
Operation permit issued	Yes ☐	No ☐	N/A ☐
Other related documentation	Yes ☐	No ☐	N/A ☐

Items requiring correction/modification: ____

Comments: meter + Bounds scale on plot

IA issued date: _____

OP issued date: _____

Review performed by: _____ Date performed: 10 25 07

FILE NUMBER: 7206B

Revised On: January 3, 2007

APPLICATION NUMBER: 2476

SEPTIC FEE: 200.00
DATE: 7/6/07 CK # 36828 JKA

MECKLENBURG COUNTY GROUNDWATER & WASTEWATER SERVICES
APPLICATION FOR A RESIDENTIAL SITE IMPROVEMENT PERMIT/ CONSTRUCTION AUTHORIZATION FOR AN ON-SITE WASTEWATER SYSTEM, NEW WELL INSTALLATION, OR REPAIR OF EXISTING WELL

WELL FEE: _____
DATE: _____

1. **SEPTIC / TYPE APPLICATION:** ☐ NONE ☒ NEW SYSTEM ☐ ALTERATION ☐ REPAIR ☐ MODIFIED PLOT PLAN

2. **WELL / TYPE APPLICATION:** ☐ NONE ☐ NEW WELL ☐ MAJOR REPAIR ☐ ABANDONMENT

3. **JOB LOCATION INFORMATION:**
TAX PARCEL NUMBER: 00333101, 00304103, Part of 00333102
STREET ADDRESS: ~~3513~~ Grey Road
CITY: Davidson
STATE: NC ZIP: 28036
SUBDIVISION NAME: ABERSHAM
LOT #: 1 LOT SIZE (acres): 2.65 acres
TOWNSHIP:
☐ 0-MECKLENBURG ☐ 3-CORNELIUS ☐ 6-HUNTERSVILLE
☐ 1-CHARLOTTE ☐ 4-PINEVILLE ☐ 7-MINT HILL
☒ 2-DAVIDSON ☐ 5-MATTHEWS

4. **BUILDING INFORMATION:**
BUILDING TYPE:
☐ SINGLE MOBILE HOME ☐ MODULAR HOME
☐ DOUBLE WIDE ☐ MULTIPLE FAMILY
☒ HOUSE ☐ OTHER _____
HEATED SQUARE FOOTAGE:
NUMBER OF BEDROOMS: 6
NUMBER OF OCCUPANTS: 12 maximum
FOUNDATION TYPE:
☐ CONCRETE SLAB ☒ BASEMENT WITH PLUMBING
☐ CRAWL SPACE ☐ BASMENT WITH NO PLUMBING

5. **IF PLANNING TO EXPAND OR ALTER THE EXISTING SYSTEM PLEASE COMPLETE THE FOLLOWING SECTION:** ☒ N/A
NUMBER OF BEDROOMS TO BE ADDED: _____ NUMBER OF ADDITIONAL OCCUPANTS IN THE RESIDENCE: _____

6. **WATER SUPPLY:** ☐ MUNICIPAL ☐ PUBLIC WELL ☒ PRIVATE WELL ☐ SHARED WELL ☐ SPRING

7. **PROPOSED USE OF WELL:** ☒ N/A ☐ IRRIGATION ☐ POTABLE ☐ GEOTHERMAL ☐ OTHER

8. **PLEASE INDICATE AND RANK DESIRED SEPTIC SYSTEM TYPE(S) IN ORDER OF PREFERENCE** *(1-MOST DESIRED 5-LEAST DESIRED):*

8A. **RANK:** ☐ ANY TYPE ☒ CONVENTIONAL 1 ☒ ACCEPTED 2 ☒ INNOVATIVE 3 ☒ ALTERNATIVE 4 ☐ OTHER ____

9. **DO ANY OF THE FOLLOWING APPLY TO THE PROPERTY IN QUESTION? IF "YES" PLEASE ATTACH SUPPORTING DOCUMENTATION.**

BURIED CABLES, LANDFILLS, STUMPHOLES	☐ YES ☒ NO	GRADING/SOIL REMOVAL PERFORMED	☐ YES ☒ NO
EXISTING WASTEWATER SYSTEMS	☐ YES ☒ NO	JURISDICTIONAL WETLANDS	☐ YES ☒ NO
WELLS, SPRINGS, OR WATER LINES	☐ YES ☒ NO	APPROVAL REQUIRED BY ANY OTHER PUBLIC AGENCY	☐ YES ☒ NO
EASEMENTS OR RIGHT-OF-WAYS	☐ YES ☒ NO	WASTEWATER OTHER THAN DOMESTIC SEWAGE	☐ YES ☒ NO

10. **PROPERTY OWNER:**
NAME: Neighborhoods at Abersham
ADDRESS: P.O. Box 99
CITY: Davidson
STATE: NC ZIP: 28036
HOME PHONE: N/A WORK PHONE: 704.895.0556
MOBILE PHONE: N/A FAX: 704.895.0558

11. **OWNER'S LEGAL REPRESENTATIVE, IF APPLICABLE:**
NAME: Rollans Soil & Environmental Services
ADDRESS: 470 N. Broad St., Suite D
CITY: Mooresville
STATE: NC ZIP: 28115
HOME PHONE: N/A WORK PHONE: 704.658.1723
MOBILE PHONE: 704.746.5046 FAX: 704.658.1724

12. **WHAT DATE WAS THE PROPERTY ORIGINALLY DEEDED AND RECORDED?** _____
13 **WHAT IS THE ANTICIPATED CLOSING DATE FOR THIS PROPERTY?** _____

14. **SEPTIC SYSTEM PERMIT APPLICATION SIGNATURE SECTION:**
If the information in this application is falsified, changed, or the site is altered, then the Improvement Permit and Authorization to Construct shall become invalid. I have read this application and certify that the information provided herein is true, complete and correct. Authorized county and state officials are granted right of entry to conduct necessary inspections to determine compliance with applicable laws and rules. I understand that I am solely responsible for the proper identification and labeling of all property lines and corners and making the site accessible so that a complete site evaluation can be performed. The permit is valid for either 60 months or is non-expiring depending upon the documentation submitted: complete site plan = 60 months, complete plat = non-expiring.

Samuel R Rollans
Property Owner's or Owner's Legal Representative Signature Date

15. **WELL PERMIT APPLICATION SIGNATURE SECTION:**
If the information in this application is falsified, changed, or the site is altered, then the Well Permit shall become invalid. I have read this application and certify that the information provided herein is true, complete and correct. Authorized county and state officials are granted right of entry to conduct necessary inspections to determine compliance with applicable laws and rules. I understand that I am solely responsible for the proper identification and labeling of all property lines and corners and making the site accessible so that a complete site evaluation can be performed. The permit is valid for a period of 12 months from the date of issuance.

Property Owner's or Owner's Legal Representative Signature Date

☐ SURVEY PLAT TO SCALE SUBMITTED ☒ SCALED SITE PLAN SUBMITTED ☐ UN-SCALED SITE PLAN SUBMITTED

N88°36'39"W
374.27'
3' setback
60' setback
N55°24'29"W
228.05'
L=343.61'
R=415.00
60' setback
3' setback
N62°39'23"W
504.44'
LOT 1
2.65 acres
HOUSE
60'x60'
(TYP.)
Homeowner's
Clearing Limits
LOT 1
SEPTIC FIELD
24,412 SF
(TYP.)
20' setback
N34°28'54"E
300.31'
LOT 2
SEPTIC FIELD
16,734 SF
3' setback
LOT 2
acres
1" = 60'

Department of Environment, Health, and Natural Resources
Division of Environmental Health
On-site Wastewater Section

Sheet: 1 of 2
Property ID: PO 003-331-01
Lot #: 1
File #: 7206B
AppID: 2476

SOIL/SITE EVALUATION for ON-SITE WASTEWATER SYSTEM

Owner: Neighborhoods at Abersham
Address: PO Box 99, Davidson, N. C. 28036
Proposed Facility: Residence
Design Flow (.1949): 720gpd
Location of Site: Off Grey Road
Water Supply: [ ] Public [x] Individual [x] Well [ ] Spring [ ] Other
Evaluation Method: [ ] Auger Boring [x] Pit [ ] Cut
Type of Wastewater: [x] Sewage [ ] Industrial Process [ ] Mixed

Applicant: Rollans Soil & Env. Services
Date Evaluated: 7/27/07
Property Size: 2.65a
Property Recorded:

PROFILE #	.1940 Landscape Position/ Slope%	Horizon Depth (IN.)	SOIL MORPHOLOGY .1941 .1941 Structure/ Texture	.1941 Consistence Mineralogy	b PROFILE FACTORS .1942 Soil Wetness/ Color	.1943 Soil Depth (IN.)	.1956 Sapro Class	.1944 Restr Horiz	Profile Class & LTAR
1	LS, 15	0-3	GR/CL	FR/SEXP/SS/SP	>43" TO SOIL WETNESS	43	N/A	NONE	PS, IV
		3-16	SBK/C	FI/SEXP/S/P					.275GPD/FT^2
		16-43	SBK/CL	FR/SEXP/SS/SP					
2	NS, 8	0-39	SBK/ABK/C	FI/SEXP/S/P	>48" TO SOIL WETNESS	48	"	"	PS, IV
		39-48	SBK/CL	FR/SEXP/SS/SP					.3GPD/FT^2
3	LS, 15	0-38	SBK/ABK/C	FI/SEXP/S/P	>48" TO SOIL WETNESS	"	"	"	PS, IV
		38-48	SBK/C	"					.275GPD/FT^2
					SITE LTAR.275GPD/FT^2				

Description	Initial System	Repair System
Available Space (.1945)		
System Type(s)		
Site LTAR		


Other Factors (.1946):
Soil Evaluation By: W. R. Marlin, LSS, 8/9/2007, W. R. Marlin
Others Present:
Site Classification (.1948):
Site Evaluation By:
Others Present:

COMMENTS:
100% repair

Landscape Position	Group	Texture	.1955 LTAR	Structure
R-Ridge	I	S-Sand	1.2 - 0.8	SG-Single Grain
SS-Shoulder Slope		LS-Loamy Sand		M-Massive
LS-Linear Slope				CR-Crumb
FS-Foot Slope	II	SL-Sandy Loam	0.8 - 0.6	GR-Granular
NS-Nose Slope		L-Loam		SBK-Subangular Blocky
HS-Head Slope				ABK-Angular Blocky
CC-Concave Slope	III	SI-Silt	0.6 - 0.3	PL-Platy
CV-Convex Slope		SICL-Silty Clay Loam		PR-Prismatic
T-Terrace				
FP-Flood Plain		CL-Clay Loam		
		SCL-Sandy Clay Loam		
	IV	SC-Sandy Clay	0.4 - 0.1	
		SIC-Silty Clay		
		C-Clay		

Consistence Moist	Consistence Wet	Mineralogy
VFR-Very Friable	NS-Non-Sticky	SEXP-Slightly Expansive
FR-Friable	SS-Slightly Sticky	EXP-Expansive
FI-Firm	S-Sticky	
VFI-Very Firm	VS-Very Sticky	
EFI-Extremely Firm	NP-Non-Plastic	
	SP-Slightly Plastic	
	P-Plastic	
	VP-Very Plastic	

Sketch of Soil Evaluation Locations

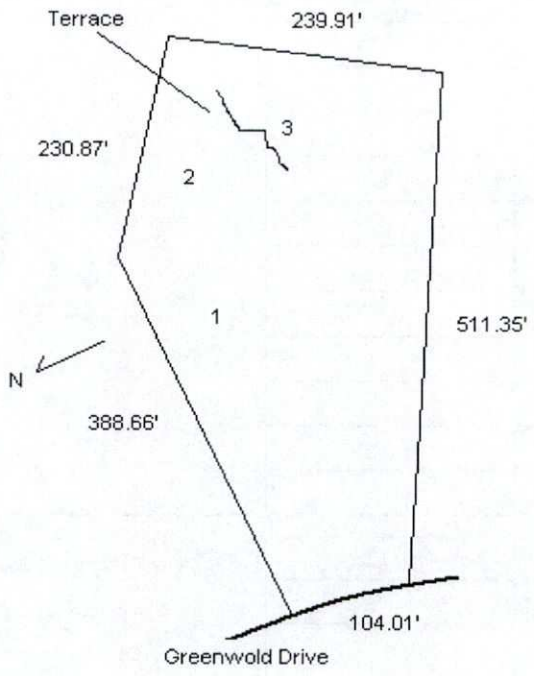

Department of Environment, Health, and Natural Resources
Division of Environmental Health
On-site Wastewater Section

Sheet: 1 of 2
Property ID: PO 003-331-01
Lot #: 1
File #: 7206B
AppID: 2476

SOIL/SITE EVALUATION for ON-SITE WASTEWATER SYSTEM

Owner: Neighborhoods at Abersham
Applicant: Rollans Soil & Env. Services
Address: PO Box 99, Davidson, N. C. 28036
Date Evaluated: 7/27/2007
Proposed Facility: Residence
Design Flow (.1949): 720gpd
Property Size: 2.65a
Location of Site: Off Grey Road
Property Recorded:
Water Supply: [ ] Public [x] Individual [x] Well [ ] Spring [ ] Other
Evaluation Method: [ ] Auger Boring [x] Pit [ ] Cut
Type of Wastewater: [x] Sewage [ ] Industrial Process [ ] Mixed

PROFILE #	.1940 Landscape Position/ Slope%	Horizon Depth (IN.)	SOIL MORPHOLOGY .1941 .1941 Structure/ Texture	.1941 Consistence Mineralogy	b PROFILE FACTORS .1942 Soil Wetness/ Color	.1943 Soil Depth (IN.)	.1956 Sapro Class	.1944 Restr Horiz	Profile Class & LTAR
1	LS, 15	0-3	GR/CL	FR/SEXP/SS/SP	>43" TO SOIL WETNESS	43	N/A	NONE	PS, IV
		3-16	SBK/C	FI/SEXP/S/P					.275GPD/FT^2
		16-43	SBK/CL	FR/SEXP/SS/SP					
2	NS, 8	0-39	SBK/ABK/C	FI/SEXP/S/P	>48" TO SOIL WETNESS	48	"	"	PS, IV
		39-48	SBK/CL	FR/SEXP/SS/SP					.3GPD/FT^2
3	LS, 15	0-38	SBK/ABK/C	FI/SEXP/S/P	>48" TO SOIL WETNESS	"	"	"	PS, IV
		38-48	SBK/C	"					.275GPD/FT^2
					SITE LTAR.275GPD/FT^2				

Description	Initial System	Repair System
Available Space (.1945)	PS	PS
System Type(s)	IIIg	Iva
Site LTAR	0.25	0.25


Other Factors (.1946):
Soil Evaluation By: W. R. Marlin, LSS, 8/9/2007,
Others Present:
Site Classification (.1948): PS
Site Evaluation By: PHILO WALKER 10/17/07
Others Present:

COMMENTS:
100% repair

Landscape Position	Group	Texture	.1955 LTAR	Structure
R-Ridge	I	S-Sand	1.2 - 0.8	SG-Single Grain
SS-Shoulder Slope		LS-Loamy Sand		M-Massive
LS-Linear Slope				CR-Crumb
FS-Foot Slope	II	SL-Sandy Loam	0.8 - 0.6	GR-Granular
NS-Nose Slope		L-Loam		SBK-Subangular Blocky
HS-Head Slope				ABK-Angular Blocky
CC-Concave Slope	III	SI-Silt	0.6 - 0.3	PL-Platy
CV-Convex Slope		SICL-Silty Clay Loam		PR-Prismatic
T-Terrace		CL-Clay Loam		
FP-Flood Plain		SCL-Sandy Clay Loam		
	IV	SC-Sandy Clay	0.4 - 0.1	
		SIC-Silty Clay		
		C-Clay		

Consistence Moist	Consistence Wet	Mineralogy
VFR-Very Friable	NS-Non-Sticky	SEXP-Slightly Expansive
FR-Friable	SS-Slightly Sticky	EXP-Expansive
FI-Firm	S-Sticky	
VFI-Very Firm	VS-Very Sticky	
EFI-Extremely Firm	NP-Non-Plastic	
	SP-Slightly Plastic	
	P-Plastic	
	VP-Very Plastic	

Sketch of Soil Evaluation Locations

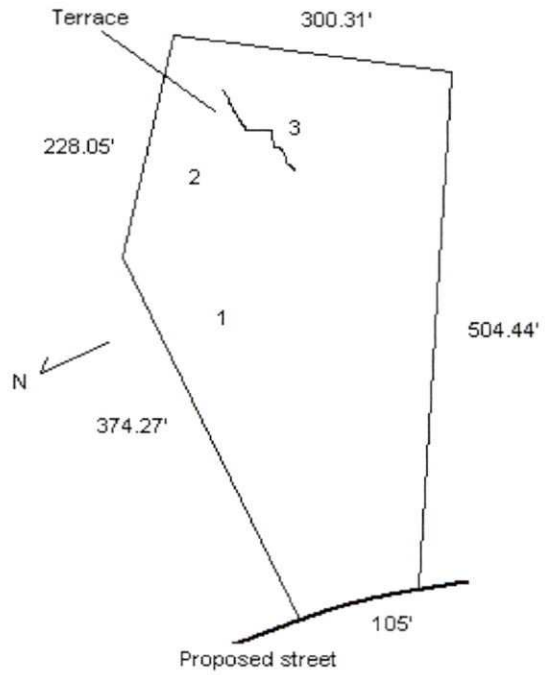

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St, Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

IMPROVEMENT PERMIT for a RESIDENTIAL ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

Permit #: **30002476** GWS File #: **7206B** Tax Parcel #: **003-331-01**

- This IMPROVEMENT PERMIT is subject to revocation if site plans or the intended use change. There is to be **NO** grading, filling, or disturbance of the soil in the area of the septic tank system or repair area.
- CONSTRUCTION AUTHORIZATION must be obtained prior to receiving a Building Permit. The Construction Authorization is **NOT** transferable. Do not clear, grade, fill or disturb soil prior to obtaining a Construction Authorization.
- Domestic-type wastewater only. No industrial process wastewater may be discharged into the system.

I. This Improvement Permit Shall: Expire in Five (5) Years **Expiration Date (If Applicable):** 10/18/2012

Type of Installation: Residential - New System Lot Number: 1

Structure Type: HOUSE Size (ft^2): 0 # Bedrooms: 6 # Occupants: 12

Building Foundation: Basement With Plumbing Water Supply: Private Well

II. Initial System Type: Approved **System Classification:** IIIg

Initial System Specifications:

Design Flow (gpd):	720	LTAR (gpd/ft^2):	0.25	Septic Tank Size (gal):	1500	Pump Tank Size (gal):	N/A
Trench Width (ft):	3	Trench Spacing (ft):	9	Absorption Area (ft^2):	2160	Total Trench Length (ft):	720
Maximum Trench Depth (in):	30	Depth of Media (in):	12	Distribution Device:	Drop Boxes		

III. Repair System Type: PPBPS (pressurized) **System Classification:** IVa

Repair System Specifications:

Design Flow (gpd):	720	LTAR (gpd/ft^2):	0.25	Septic Tank Size (gal):	1500	Pump Tank Size (gal):	1500
Trench Width (ft):	3	Trench Spacing (ft):	9	Absorption Area (ft^2):	1440	Total Trench Length (ft):	480
Maximum Trench Depth (in):	42	Depth of Media (in):	N/A	Distribution Device:	Manifold (LPP Distri		

IV. Permit Conditions/Comments:

(Please See the Following Page for Permit Conditions.)

The undersigned, an authorized agent of the MECKLENBURG COUNTY HEALTH DEPARTMENT, certifies that the Department is issuing an IMPROVEMENT PERMIT for the above referenced property. This permit is being issued in accordance with the *Laws and Rules For Sewage Treatment, and Disposal Systems* and is subject to the following provisions:

- No work shall be conducted on the septic system until an INSTALLATION APPROVAL is granted by the Department.
- The septic system installer shall be a registered septic contractor with Mecklenburg County Health Department.
- The permitted system shall be installed in accordance with the included PLOT PLAN.
- This IMPROVEMENT PERMIT is transferable.

DENR Authorized Agent: Philo Walker

Signature: Philo Walker 21

Date Issued: 10/18/2007

Owner/Legal Agent: Greg Williams
Print Name

Signature:

Mecklenburg County Groundwater & Wastewater Services
700 N. Tryon St, Suite 211 Charlotte, NC 28202
Phone: (704) 336-5103 Fax: (704) 336-6894

NC DENR
Division of Environmental Health
On-Site Wastewater Section

IMPROVEMENT PERMIT for a RESIDENTIAL ON-SITE WASTEWATER TREATMENT & DISPOSAL SYSTEM

Permit #: **30002476** GWS File #: **7206B**

IV. Permit Conditions/Comments:

- Easement agreement forms shall be on file and the property shall be deeded and recorded prior to issuance of Construction Authorization.
- All components of the septic system must be located at least 100 ft. (50 ft. minimum) from all private wells.

The undersigned, an authorized agent of the MECKLENBURG COUNTY HEALTH DEPARTMENT, certifies that the Department is issuing an IMPROVEMENT PERMIT for the above referenced property. This permit is being issued in accordance with the *Laws and Rules For Sewage Treatment and Disposal Systems* and is subject to the following provisions:

- No work shall be conducted on the septic system until an INSTALLATION APPROVAL is granted by the Department.
- The septic system installer shall be a registered septic contractor with Mecklenburg County Health Department.
- The permitted system shall be installed in accordance with the included PLOT PLAN.
- This IMPROVEMENT PERMIT is transferable.

DENR Authorized Agent: Philo Walker

Signature: Philo Walker PS

Date Issued: 10/18/2007

Owner/Legal Agent: GREG WILLIAMS
Print Name

Signature:

Page 2 of 2

GWS FILE # 7206B

ROLLANS ***Soil & Environmental Services, Inc.***

470 North Broad St , Suite D, Mooresville, NC 28115 Phone: (704) 658-1723 Fax: (704) 658-1724

Ashley Rollans, NC Licensed Soil Scientist
Mobile: (704) 746-5046
E-mail: Rollansfortcj@aol.com

Brady Freeman, Registered Sanitarian
Mobile: (704) 746-6497
E-mail: bfree209@yahoo.com

Attached is a proposed design for an Accepted (25% reduction) Septic System with Gravity distribution for a 6 bedroom single family residence on Lot #1 Abersham Subdivision, Mecklenburg County, North Carolina.

Contents: **Page**

Information for the Installer---------- 1

Design Information
- Design Specifications---------- 2-3
- Layout Specifications---------- 4

Site Plan/System Plan---------- 5

Calculations---------- 6

Profile Descriptions---------- 7

August 17, 2007
Project #: 01-1044
Design By: Rollans Soil and Environmental Services

GWS Septic System Design Review

GWS File #: 7206B	**Approved**	**Disapproved**
Design Review: TCT 10-18-07	☒	☐
Field Review: 10/12/07 JSW	☒	☐

*Projects are not considered "APPROVED" until both sections above are completed and indicate an APPROVED status.

INFORMATION FOR THE INSTALLER:

- The permit should be read very carefully prior to bidding. The following are details that must be considered along with all other considerations.
- Tanks shall be approved by NC DENR, and certification supplied by the manufacturer.
- Tanks shall be water tested prior to installation.
- The installer shall be responsible to the owner for placement of the tanks and to insure that final grades are returned to the original natural grade, with exception of added structural features.
- The supply trench shall be compacted to eliminate cavities left during initial fill placement.
- Installation of the system shall be during dry conditions in order to protect the soil structure.
- All fittings shall be pressure rated fittings.
- All joints shall be cleaned with PVC pipe cleaner and a heavy bodied glue applied to weld all joints.
- Where required by the county health department, post installation inspections by the designer must be scheduled 5 week days in advance.
- Trenches shall be carefully excavated so the bottom is within 2" from the highest to . the lowest points of elevation within the trench. If the bottom elevation needs adjusting after it has been trenched, it will be done by removing high points rather than filling low points. It is extremely important to insure that trenches are not over excavated during initial trenching. All fine grading within the trench will be hand done with a shovel. No loose material will be left in the trench
- All pipe openings in the tanks shall be properly grouted. This also applies to the joints around the riser.
- All tanks shall be properly back filled and compacted to prevent slump at a later date.
- Earth dams, constructed of relatively impervious material, shall be installed at the beginning and end of each lateral.
- No heavy equipment shall be used on the field during or after installation. The use of a small loader (i.e. Bobcat) or a trencher (i.e. Ditch Witch 2300/2310) may be used for installation.
- Elevations at pinflag locations should be checked by the installer prior to beginning trenches.
- Pumptank riser should be 6" above grade, control panel should be 12" above grade.
- Septic tank riser shall be a minimum of 6" above finished grade.
- System is specified as an innovative 25% reduction installation.
- Repair is specified as a PPBPS with low pressure distribution installation.
- Rake trench walls, lime sidewalls, install trenches 36" wide and have no more than 1/4" fall in 10 feet.

GRAVITY SYSTEM
FOR WASTEWATER TREATMENT

Owner:	William Brewster Company
Address:	PO Box 99 Davidson NC 28036
Phone:	704 895 0556
County:	Mecklenburg
Location:	Abersham LOT #1
Source of Wastewater Flow:	6 Bedroom Single Family Residence
Estimated Gallons Per Day Flow:	720
System Flow:	N/A

Design Specifications

Drainfield Size:	735
Loading Rate (gpd/ft.^{2}):	0.25
Depth of Gravel in Trench:	NA (25% reduction)
Gravel Size:	NA (25% reduction)
Trench Depth:	36 in
Trench Width:	36 in
Septic Tank Size:	1500 gal.
Pump Tank Size:	N/A
Estimated Supply Line Length:	11
Supply Line Diameter:	3 in. SCH 40 PVC
Supply Line Volume:	1.91
Dosing Volume:	NA
Supply Manifold:	SERIAL DROP BOX
Supply Manifold Length:	N/A
Supply Manifold Volume:	N/A
Recommended Float Controls:	N/A
Recommended Control Panel:	N/A
Pressure Head:	NA
Friction Head:	NA
Elevation Head:	NA
Total Dynamic Head:	NA
Threaded Union:	NA
Gate Valves:	NA
	NA
Check Valves:	NA
Anti-Siphon Hole:	NA
Additional Comments:	Soil suitability was performed by Mecklenburg County Health Department

Abersham LOT #1
GRAVITY SYSTEM DESIGN

DESIGN FLOW (gpd):	720
SOIL APPLICATION RATE (gpd/ft.^{2}):	0.25
TOTAL AREA TRENCH BOTTOM:	2205
TOTAL LATERAL LENGTH:	735
NUMBER OF FIELDS:	1
LATERAL LENGTH REQUIRED PER FIELD:	720
SUPPLY LINE LENGTH:	11
TOTAL DYNAMIC HEAD:	NA
MANIFOLD SIZE:	NA
DOSING VOLUME:	NA
PUMP TANK DRAW DOWN*:	NA
SEPTIC TANK SIZE:	1500 gal.
PUMP TANK SIZE:	1500 gal.

**Pump tank draw down based on a volume basis of 29 gallons per inch. Draw down may vary among pump tank manufacturers.*

Abersham LOT #1

Project #: 01-1044

LAYOUT FOR 6 BEDROOM HOME

August 17, 2007

LINE #	FLAG COLOR	BS	HI	FS	ELEVATION	FLAGGED LINE LENGTH	DESIGN LINE LENGTH
TBM		NA			NA		
INSTR. 1			NA				
HOUSE CNR				NA	NA		
P. TANK				NA	NA		
1	BLUE			NA	NA	75	75
2	RED			NA	NA	75	75
3	PINK			NA	NA	100	100
4	*ORANGE*			*NA*	*NA*	*131*	*130*
5	*BLUE*			*NA*	*NA*	*138*	*135*
6	*RED*			*NA*	*NA*	*138*	*135*
7	*PINK*			*NA*	*NA*	*115*	*115*
8	*ORANGE*			*NA*	*NA*	*105*	*105*
9	*BLUE*			*NA*	*NA*	*89*	*85*
10	*RED*			*NA*	*NA*	*35*	*30*
11	RED			NA	NA	40	40
12	PINK			NA	NA	70	70
13	ORANGE			NA	NA	61	61
14	BLUE			*NA*	*NA*	60	60
					Total	1232	1216

	LINE LENGTH	LTAR GPD/FT^2	SYSTEM TYPE	SOIL LTAR GPD/FT^2	TRENCH SYSTEM	DISTRIBUTION
* *System*	*735*	*0.25*	*ACCEPT.*	*0.25*	*25% RED.*	GRAVITY
Repair	481	0.25	*MOD.*	0.25	PPBPS	DISTRIBUTION LOW PRESSURE

Notes:

**TBM is assumed to be 100'

**All measures in feet

**Nitrification lines are demonstrated on contour via colored pin flags

**BS, HI, and FS indicate rod readings


DRIVE
WELL
1" = 60'
Scale
Keep septic system >100' from well
5203
set pol
5202
set pol
5201
set pol
5200
set pol
5210
set pol
LOT 1
SEPTIC FIELD
24,412 SF
LOT 2
2.65 acres
100'
6 Bedroom House
LOT 2
2.26 acres
CVB
TURN OF
DROP BOXES
FIELD
1 B 75'
2 R 75'
3 P 100'
4 O 130'
5 B 135'
6 R 135'
7 P 115'
8 O 105'
9 B 85'
10 R 35'
11 R 40'
12 P 70'
13 O 61'
14 B 60'
1 R 34'
2 B 95'
3a P 61'
4a O 70'
5a R 70'
5 B 40'
8 O 30'
9 B 50'
10 B 75'
11 P 66'
347'
504'
150'
220'
300'
100'

CALCULATIONS

Location ABERSHAM

Project Number 01-1044

Lot No: Lot 1

No. of Bedrooms	6	
Design Flow	720	$^{gal}/_{day}$
I TAR	0.25	$^{gpd/ft^2}$
25% RED ? (YES OR NO)	YES	
Supply Line Length	11	ft.
Supply Line Volume	1.914	gal.
Required Feet of Line	720	ft.
Amount of Line from Layout	735	ft.
Gallons per Minute	N/A	$^{gal}/_{min}$
Required Septic Tank Capacity	1500	gal.
Minimum Standard Tank Size	1500 gal.	
Lateral Line Volume	479.955	gal.
Dosing Volume	NA	gal.

Note: Dosing Volume based on 70% of lateral line volume

FRICTION FACTOR INTERPOLATER
2" SCH 40 PVC

GPM	*f*
20	0.84
[illegible]	[illegible]
25	1.27
[illegible]	[illegible]
30	1.78
[illegible]	[illegible]
35	2.37
[illegible]	[illegible]
40	3.03
[illegible]	[illegible]
45	3.77
[illegible]	[illegible]
50	4.58
[illegible]	[illegible]
60	[illegible]

Tank Draw Down	NA	*Generic Draw Down of 29 gal.per in.*
Pump Run Time	NA	minutes
Elevation Head	NA	ft.
Pressure Head	NA	ft.
Friction Factor	NA	ft./100 ft. *(From the interpolater.)*
Friction Head	NA	ft.
Total Dynamic Head (+15%)	NA	ft.
